

Status of PHENIX and Run-12 Prep



RPC Installation complete

11/23

RPC Commissioning

Ongoing – 12/16

VTX/FVTX Installation

12/1-12/6

VTX/FVTX Survey, cabling, plumbing

12/7-12/16

East Carriage Roll In

Week of 12/12



Safety system checkout pink/blue/white sheets

12/12-12/23


Cool down start

1/17

Highlights

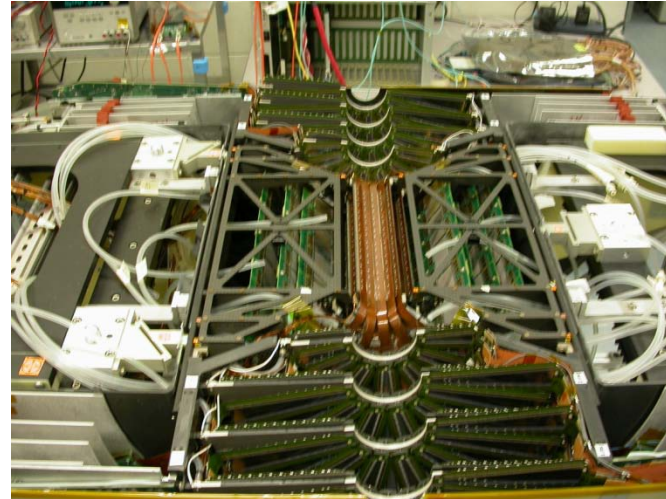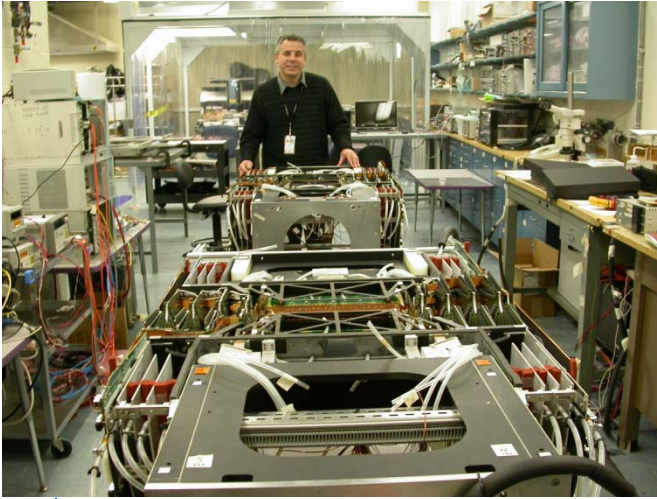

↑ VTX+FVTX assembly complete. Next pre-installation tests, pre-survey

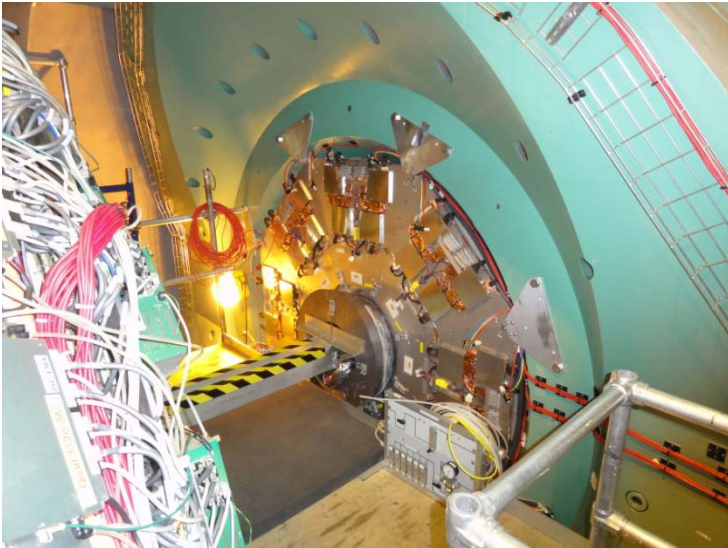

← RPC1-S installed in Central Magnet

Summary

- **PHENIX is on schedule to be fully installed and ready for final commissioning at RHIC cryo start Jan 17**
- **Major 2011 projects are nearing completion (VTX+FVTX fab and installation, RPC1 fab and installation, MuTracker St1 maintenance)**
- **The schedule relies on availability of various support groups: Survey, carpenters, riggers, PASS, CAS ..**
 - **As usual this is well coordinated between Don Lynch and Dave Phillips**
