

PHENIX Run-10 Preparations


Stefan Bathe

PHENIX Calendar

- East Carriage Roll-In Nov 10
- Completion of MuTrg RPC St3 installation Nov 12
- Shield wall closed, end of shutdown Nov 30
- Start of Run-10 Dec 1
 - Watch shifts
 - Flammable gas
- Full 5-person shifts Dec 15
- Expect Physics collisions Jan 1
- Au+Au 200 GeV (10 weeks)
- Au+Au 62.4 GeV run (4 weeks)
- Au+Au lower energies (length depending on budget)

PHENIX Recent Accomplishments

- HBD East is repaired and back in IR
- MuTrg FEE Installation is complete
- All north MUON RPC half octants installed in tunnel
- PC1 bad chamber swap is done
- DC-East wire repair done
- MuTrk work

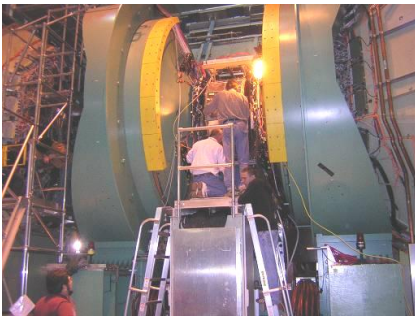

Summary and Outlook

- Detector installation complete for Run 10
- Safety system, magnet, and detector setup and testing under way
- Rack room air conditioning upgrade almost complete
- Preparing to begin detector operation Dec 1
- Thanks to C-A for air conditioning upgrade
- However half the IR air conditioners still need service
