

Run 10 plan based on 25 Nov Revised Plan and $\sqrt{s}=200$ extended by 1 week

- Dec. 1, Begin cool down to 4.5K
- Dec. 4, Cooldown to 4.5K complete in both rings!
- Dec. 5, beam setup in RHIC begins.
- Dec 16, 20 hr unplanned Maintenance day
- Dec 20 (AM)-21(PM), blizzard 09 shut us down
- Dec. 27, RHIC Setup complete, begin Ramp Up for Physics (was 14 Dec, late)
- Dec 31 (midnight-store 11340), Machine, Physics declared (store 11340) $\sqrt{s}=200$ GeV/n Au-Au
- Jan 2 (midnight) STAR in Physics Mode
- Jan 8 (0600) PHENIX in Physics Mode
- Jan 12, Rebucketing not yet routine, stochastic cooling still to come.
- Jan 22, changed beta* from 0.6 to 0.7 meters, rebucketing ~established, yellow transverse stochastic cooling on
- Mar. 18 (0556), End 10 week $\sqrt{s} = 200$ GeV/n Run, begin $\sqrt{s} = 62.4$ GeV/n setup
- Mar. ~~20~~ **19**, Begin 4 week $\sqrt{s} = 62.4$ GeV/n run
 - Machine physics 19 March for stores ≥ 11954
 - PHENIX Physics 19 Mar for stores ≥ 11955
 - STAR Physics 22 March for stores ≥ 11976
- Apr. ~~17~~**16**, End 4 week $\sqrt{s} = 62.4$ GeV/n Run, begin $\sqrt{s} = 39$ GeV/n setup
- Apr. 19, Begin 1.5 week $\sqrt{s} = 39$ GeV/n run
- Apr. 30, End 1.5 week $\sqrt{s} = 39$ GeV/n Run, begin $v = 0.67$ studies before polarity switches begin (i.e. this is a placeholder)
- May 1, complete $v = 0.67$ studies for pp and $\sqrt{s} = 7.7$ GeV/n setup (**12 hr pol. switches**)
- May. 3, Begin 4 week $\sqrt{s} = 7.7$ GeV/n run
- **May 23 – 28 IPAC (Kyoto)**
- **May 22 Jun 3, Satogata is away**
- May 31, End 4 week $\sqrt{s} = 7.7$ GeV/n Run, begin $\sqrt{s} = 11.5$ GeV/n setup (**4-6 hr polarity switch, if necessary**)
- Jun 2, begin $\sqrt{s} = 11.5$ GeV/n for STAR
- Jun 16, end 2 week $\sqrt{s} = 11.5$ GeV/n run, begin $\sqrt{s} = 5$ GeV/n setup (**4-6 hr polarity switch, if necessary**)
- Jun 18, begin $\sqrt{s} = 5$ GeV development
- Jun 21, end 3 days at $\sqrt{s} = 5$ GeV/n
- Jun 22 , Begin Cryo Warm-up
- Jun 23, Warm-up complete, Run 10 ends – **29.2 CRYO WEEKS**

**Run 10 plan based on 25 Nov Revised Plan
and $\sqrt{s}=200$ extended by 1 week**


- Mar. ~~20~~ **19**, Begin 4 week $\sqrt{s} = 62.4$ GeV/n run (**gained a day of contingency**)
 - Machine physics 19 March for stores ≥ 11954
 - PHENIX Physics 19 Mar for stores ≥ 11955
 - STAR Physics 22 March for stores ≥ 11976
- Apr. ~~17~~ **16 (??)**, End 4 week $\sqrt{s} = 62.4$ GeV/n Run, begin $\sqrt{s} = 39$ GeV/n setup
- Apr. 19, Begin 1.5 week $\sqrt{s} = 39$ GeV/n run
- Apr. 30, End 1.5 week $\sqrt{s} = 39$ GeV/n Run, begin $v = 0.67$ studies before polarity switches begin (i.e. this is a placeholder)
- May 1, complete $v = 0.67$ studies for pp and $\sqrt{s} = 7.7$ GeV/n setup (**12 hr pol. switches**)
- May. 3, Begin 4 week $\sqrt{s} = 7.7$ GeV/n run
- **May 23 – 28 IPAC (Kyoto)**
- **May 22 Jun 3, Satogata is away**
- May 31, End 4 week $\sqrt{s} = 7.7$ GeV/n Run, begin $\sqrt{s} = 11.5$ GeV/n setup (**4-6 hr polarity switch, if necessary**)
- Jun 2, begin $\sqrt{s} = 11.5$ GeV/n for STAR
- Jun 16, end 2 week $\sqrt{s} = 11.5$ GeV/n run, begin $\sqrt{s} = 5$ GeV/n setup (**4-6 hr polarity switch, if necessary**)
- Jun 18, begin $\sqrt{s} = 5$ GeV development
- Jun 21, end 3 days at $\sqrt{s} = 5$ GeV/n
- Jun 22, Begin Cryo Warm-up
- Jun 23, Warm-up complete, Run 10 ends – **29.2 CRYO WEEKS**

Run 10 Au-Au Goals


3/30/10

- STAR
 - $\sqrt{s} = 62 \text{ GeV/n}$
 - Luminosity Sampled/Delivered = ?/90 μb^{-1}
 - 100M Min-bias events
- PHENIX
 - $\sqrt{s} = 62 \text{ GeV/n}$
 - Luminosity Recorded/Delivered = 64/193 μb^{-1}
 - 400M Min-bias events


Run 10 31 x 31 GeV/n Au Delivered Luminosity

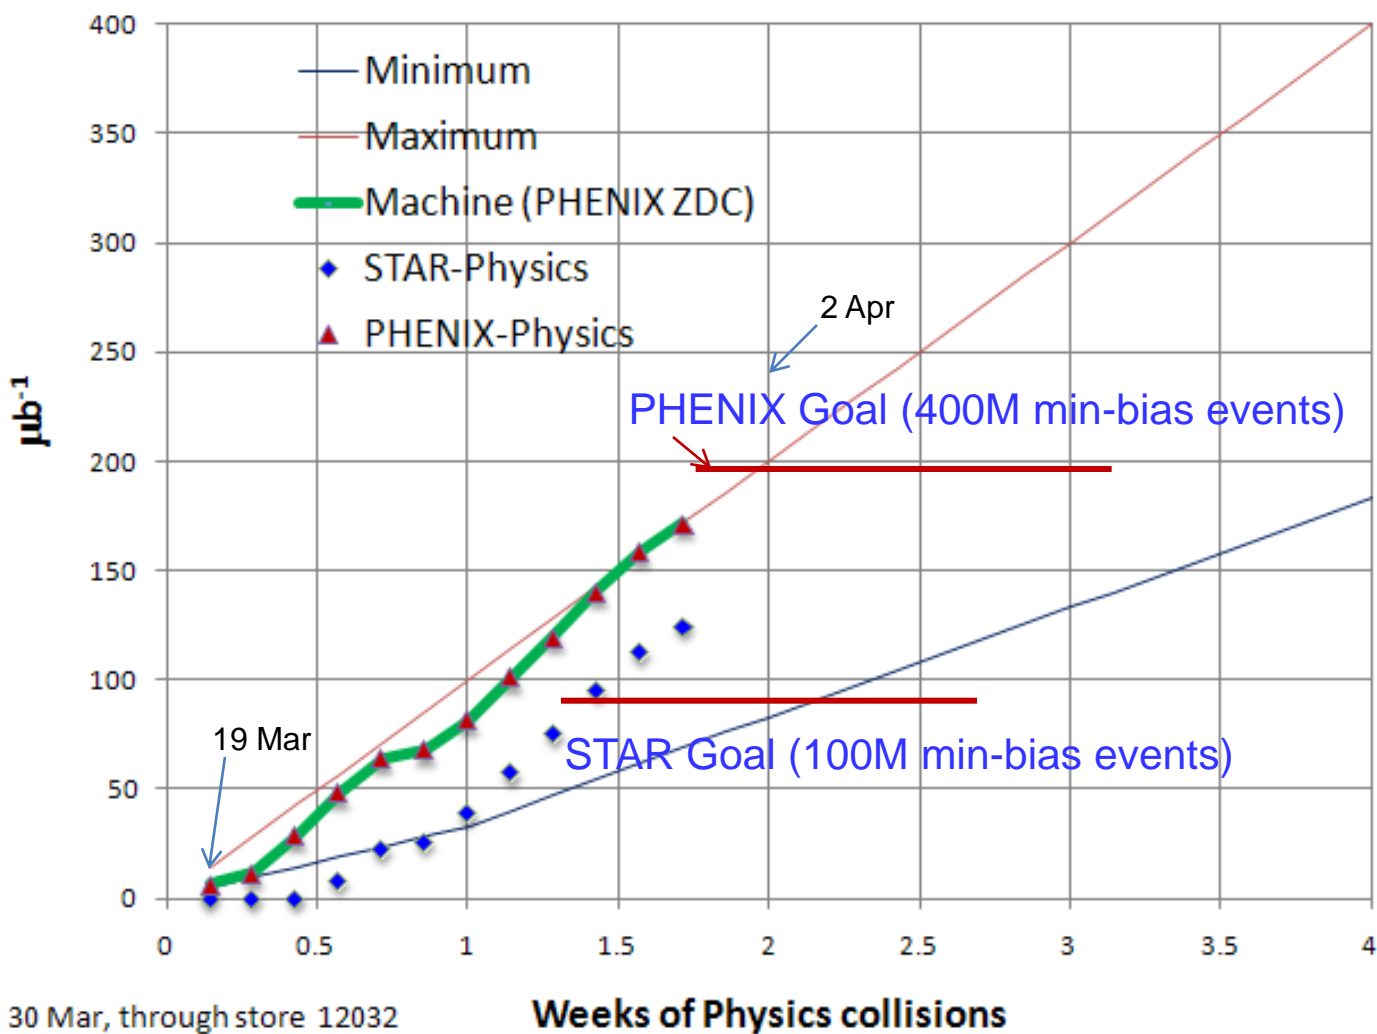

Run 10 31 x 31 GeV/n Au Delivered Luminosity per day


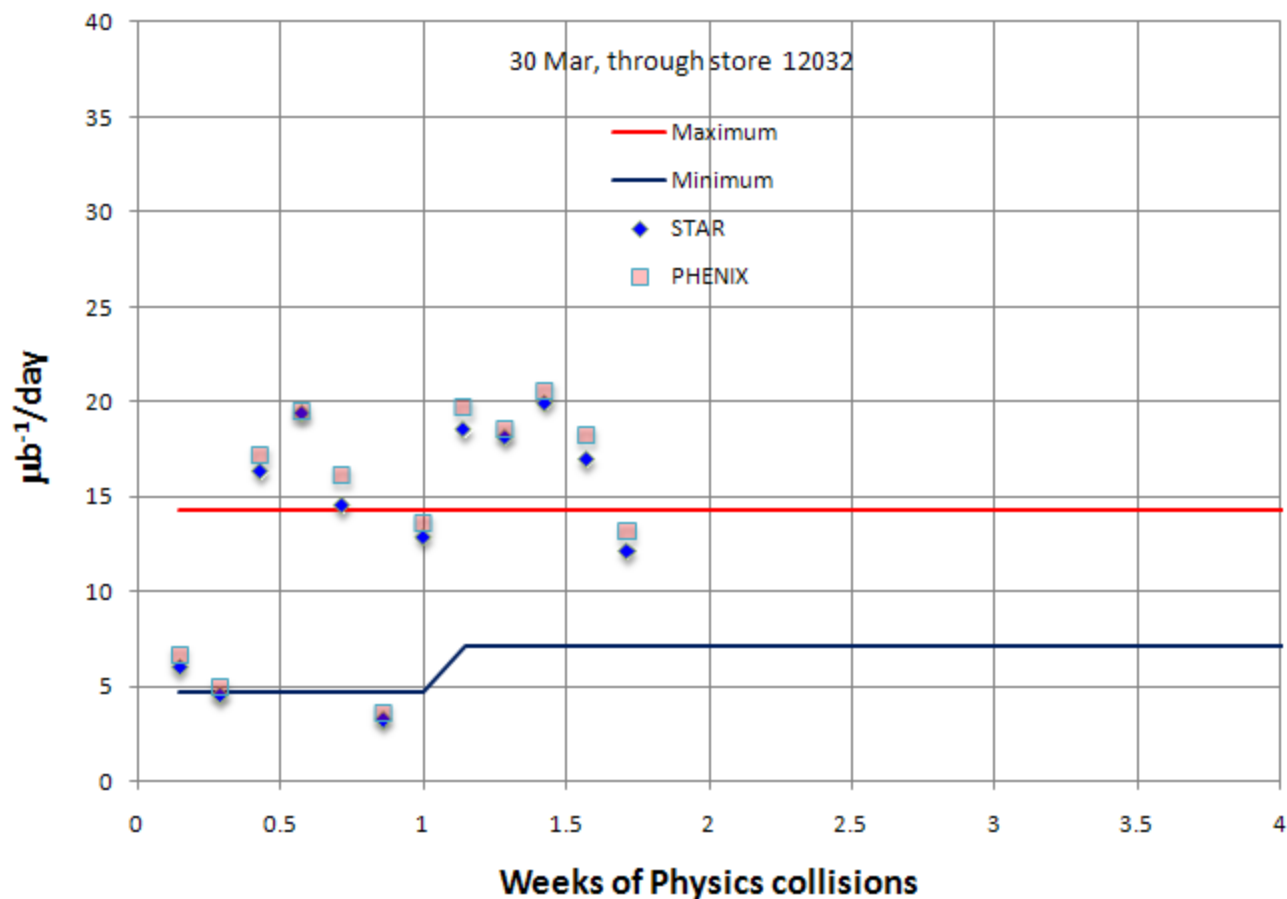


Run 10 (AuAu) -- Integrated Luminosity by week

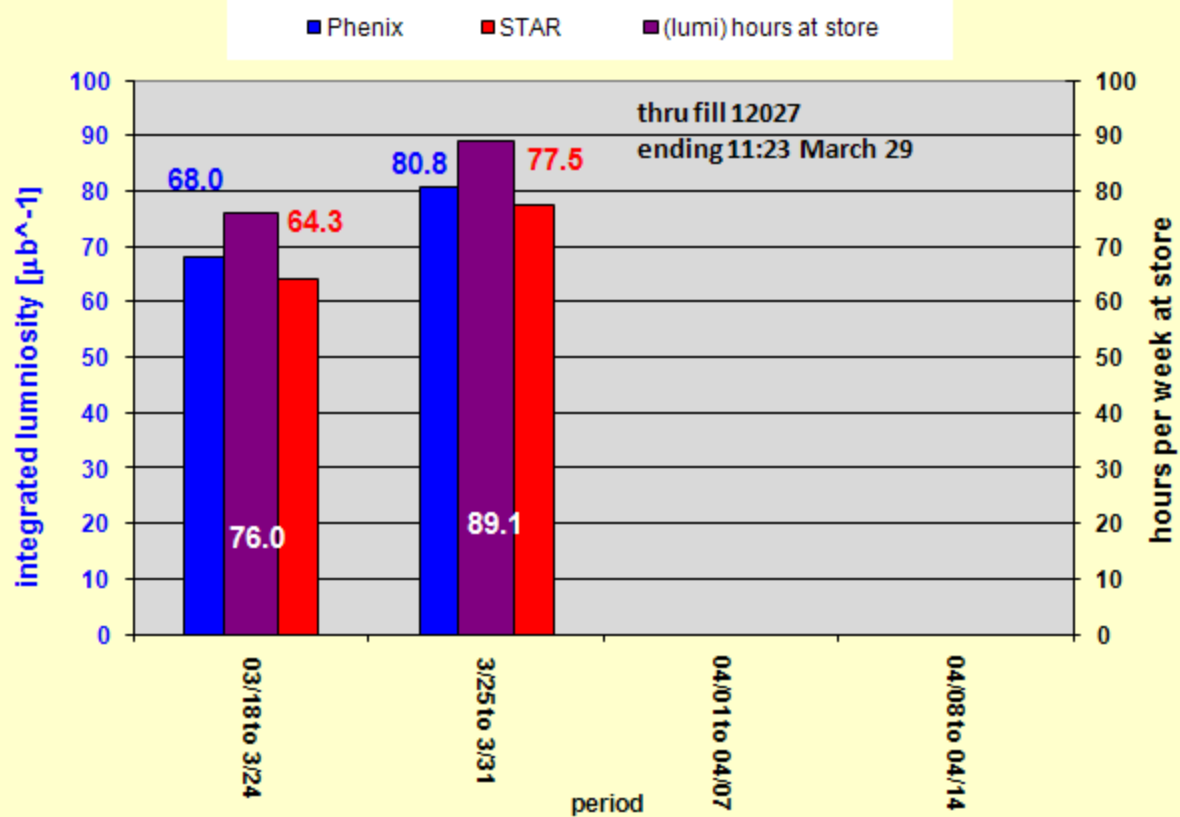


31 x 31 GeV/n Au, 26 March to Present

Store 12031

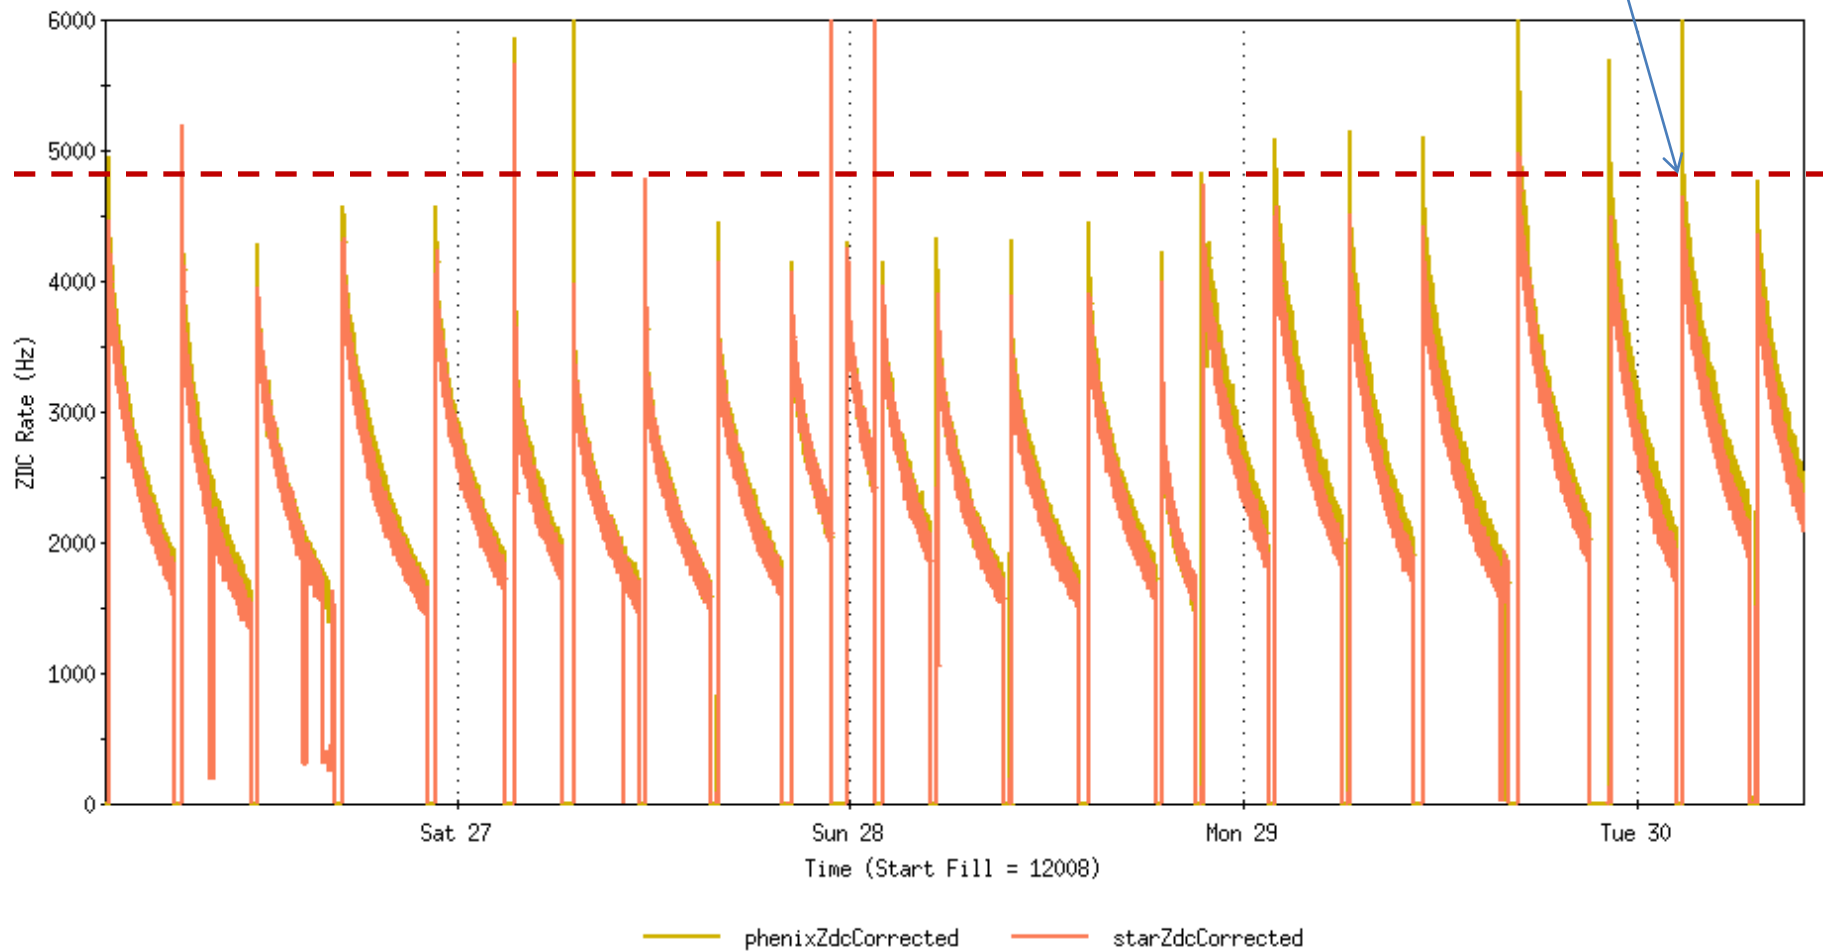


Store12031 ($1.43/1.47 \times 10^9$)

RHIC - DCCT total beam & WCM bunched beam

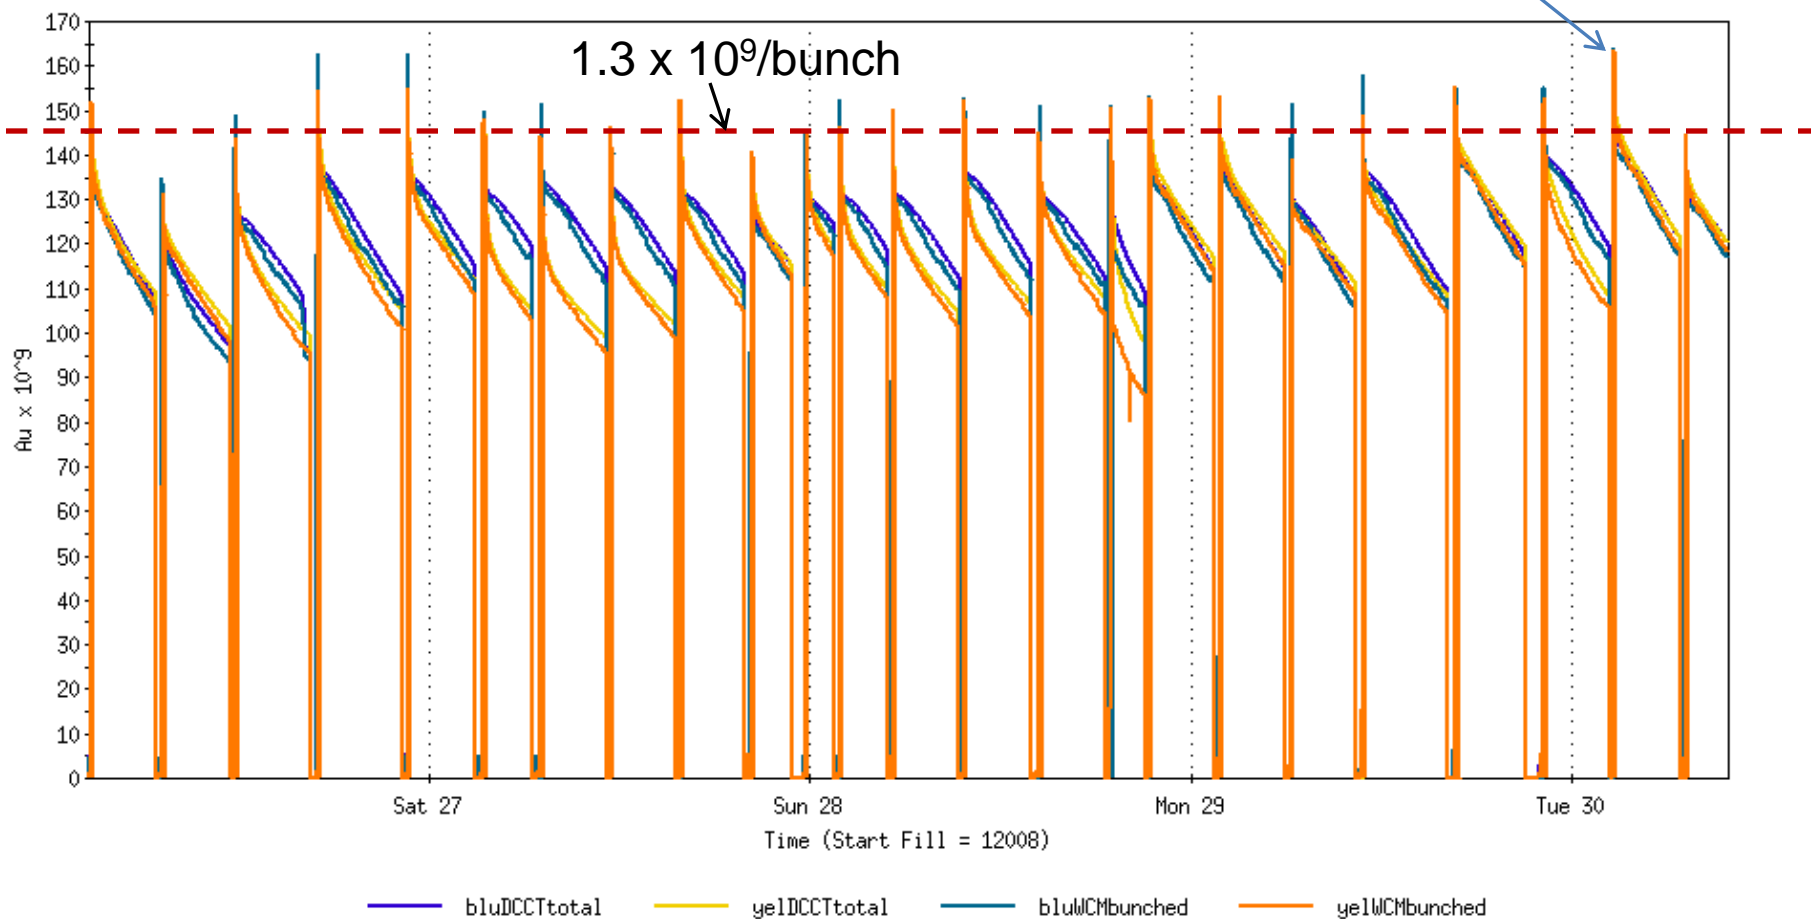


Store 12031

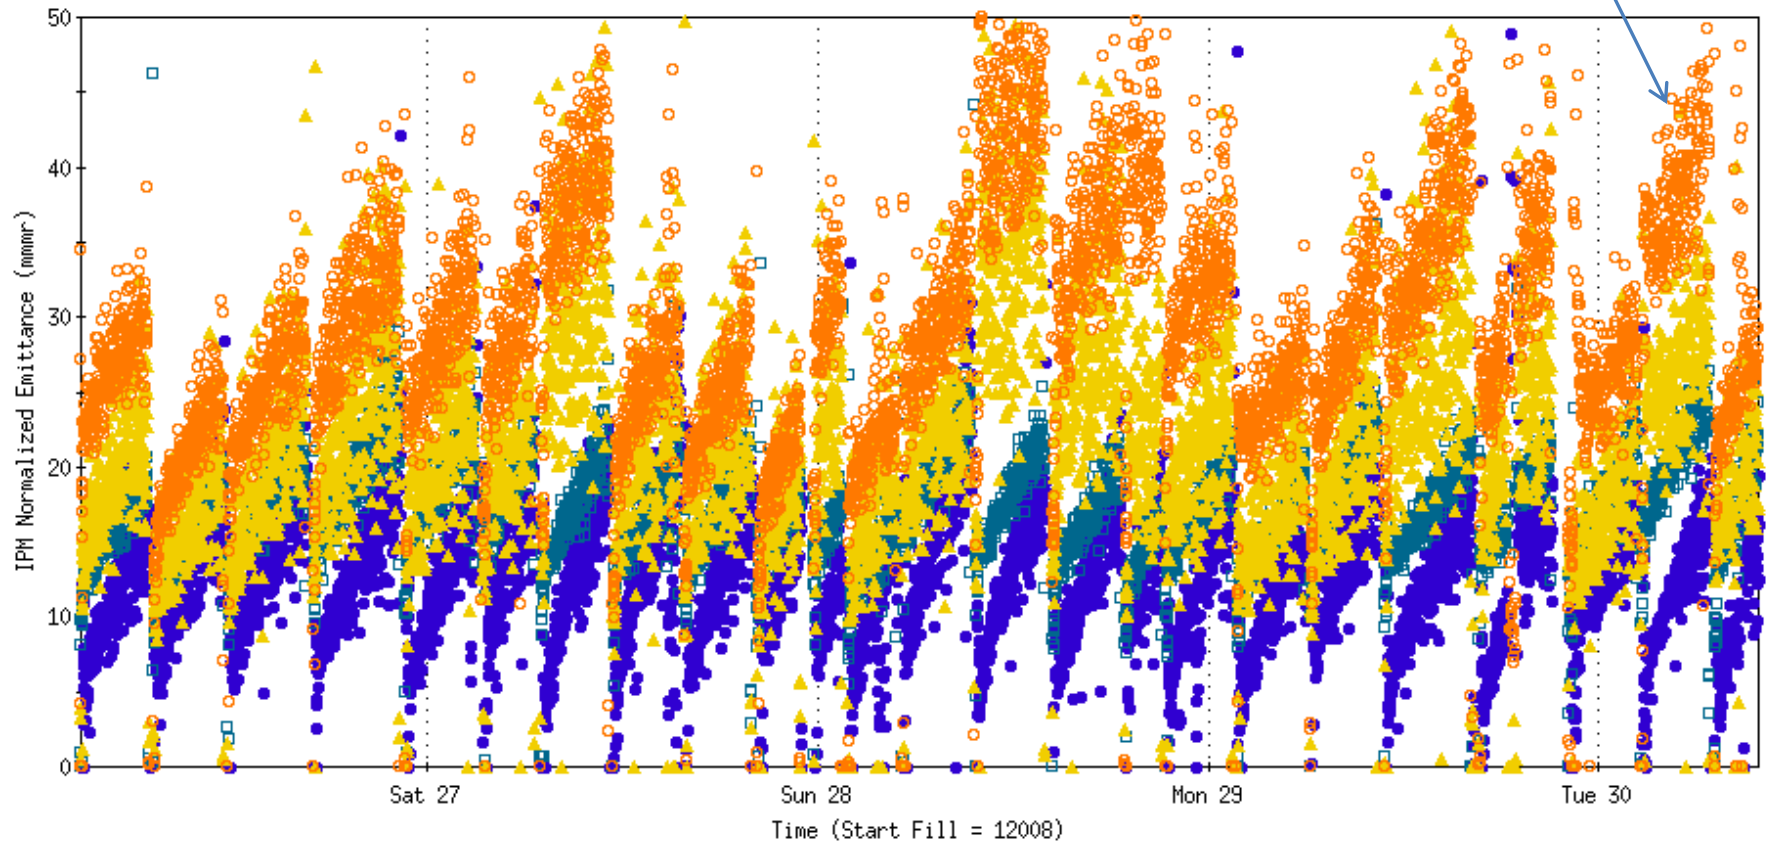

● RhicIpmManager.blue_horiz;normEmitM:valueAndTime[.]
▲ RhicIpmManager.yellow_horiz;normEmitM:valueAndTime[.]


□ RhicIpmManager.blue_vert;normEmitM:valueAndTime[.]
○ RhicIpmManager.yellow_vert;normEmitM:valueAndTime[.]

Store 12031

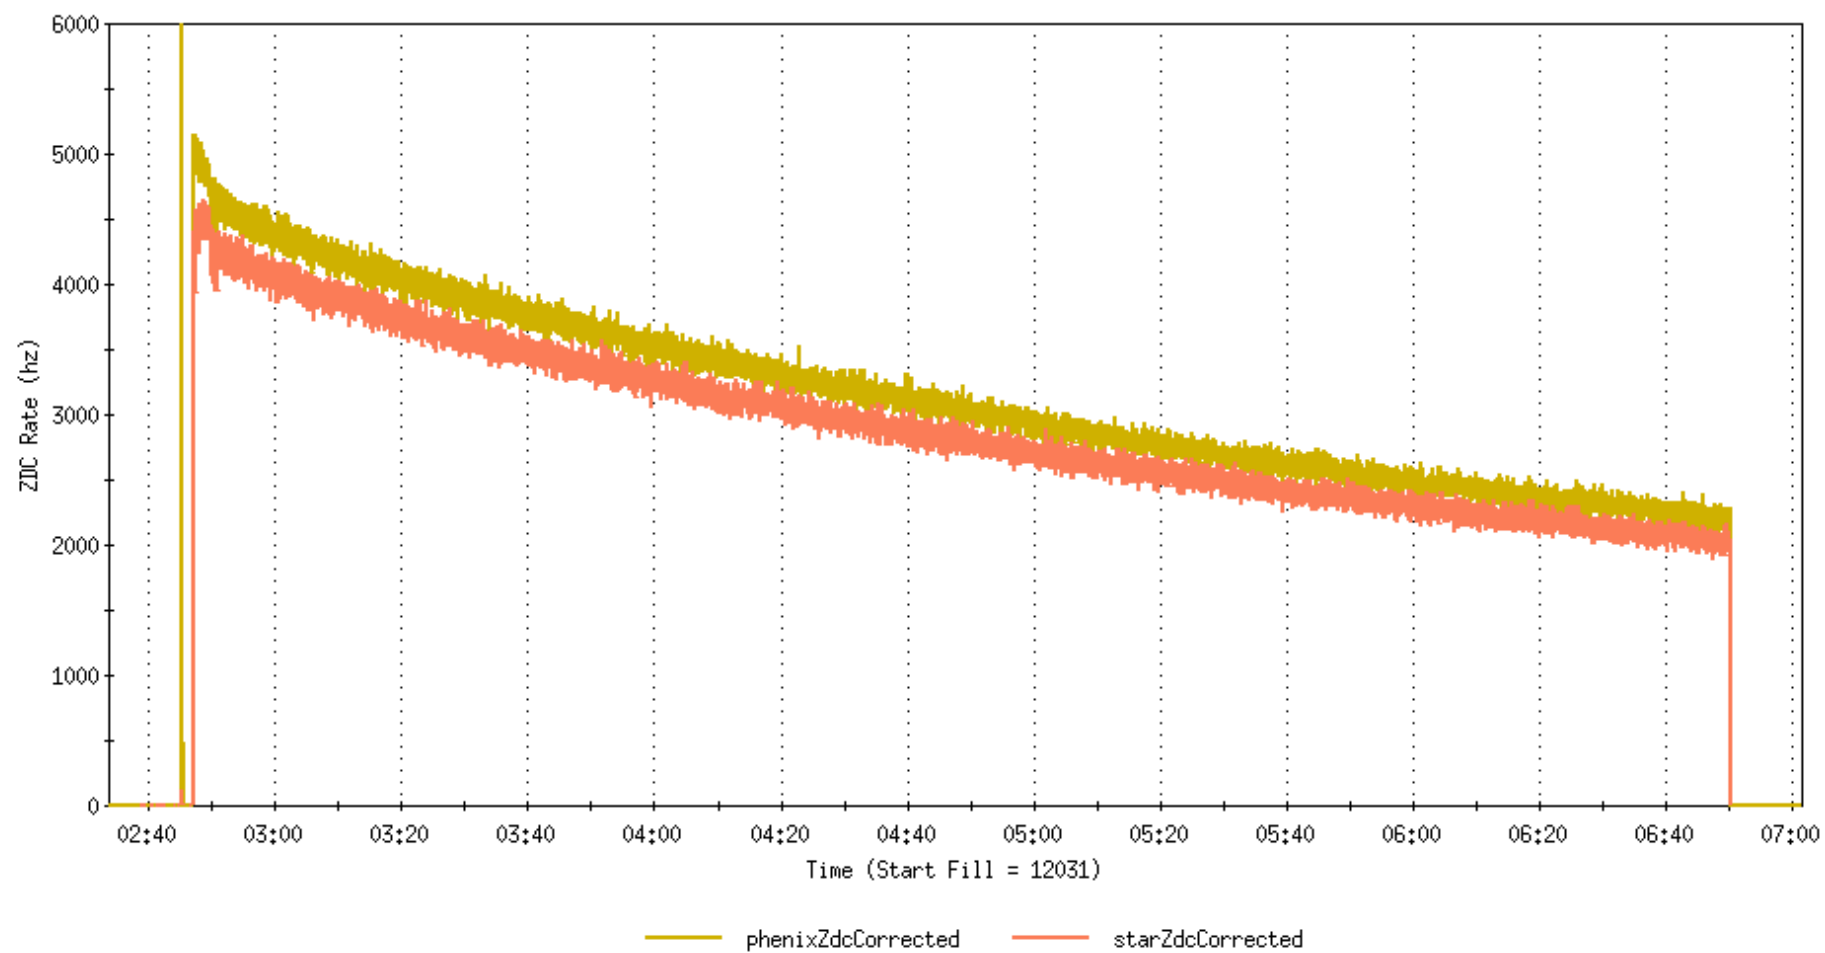

RHIC - DCCT total beam & WCM bunched beam


Store 12031

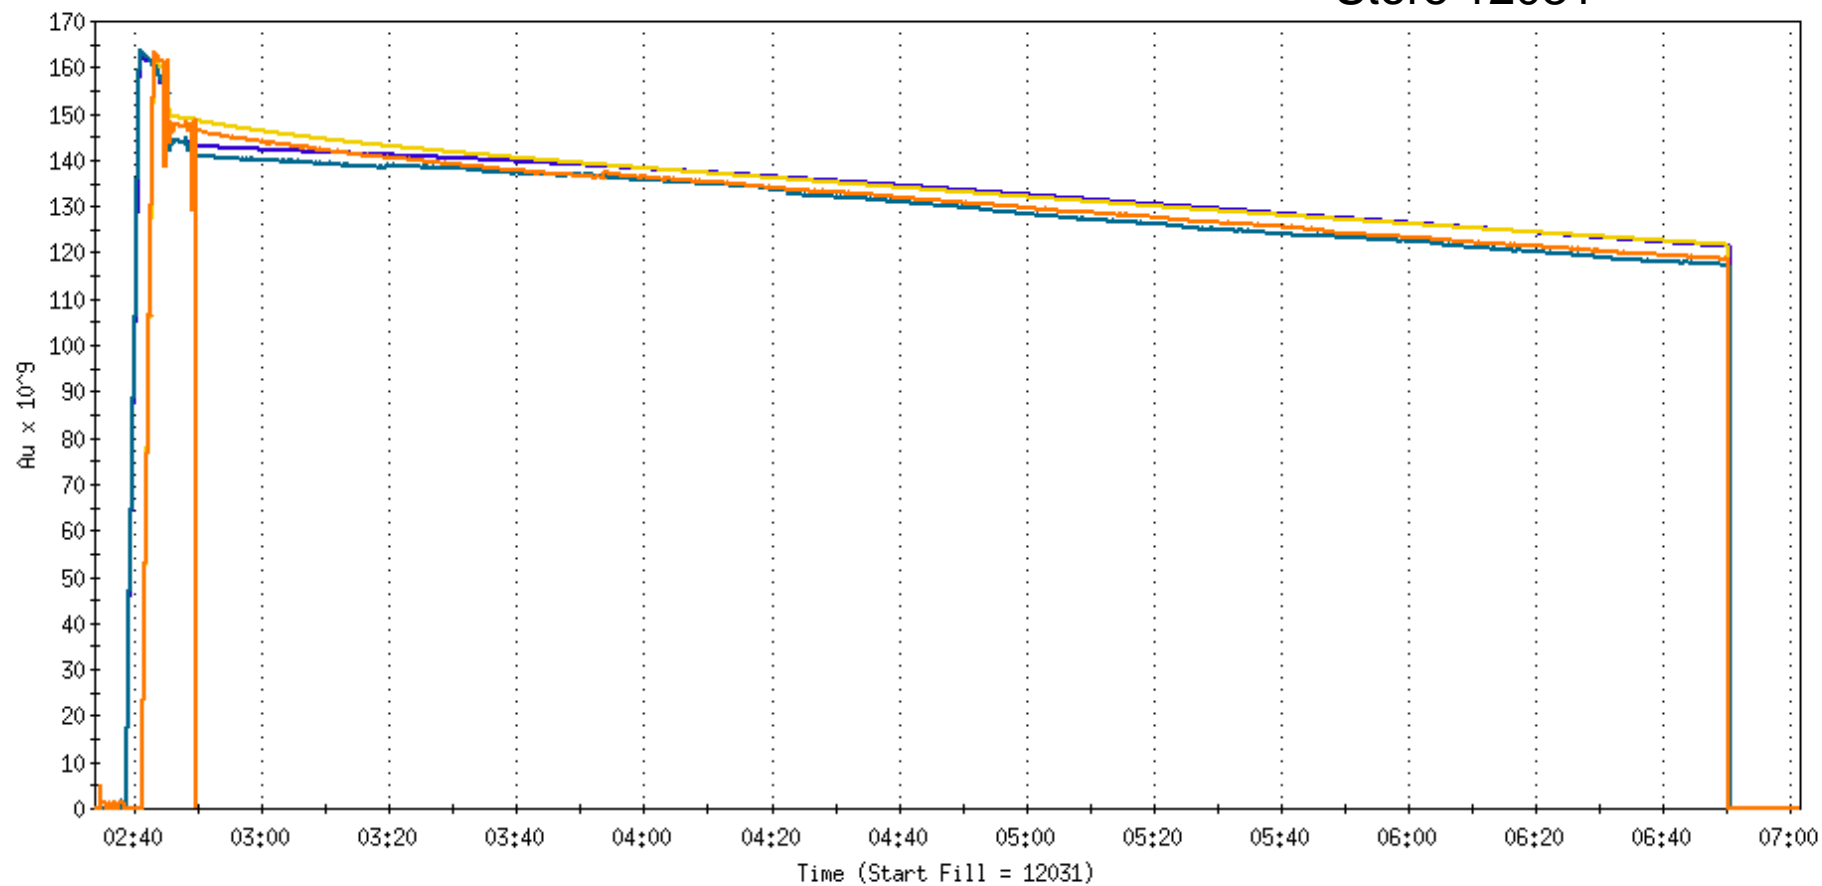

bluDCCTtotal yelDCCTtotal bluWCMbunched yelWCMbunched


Store 12031

RHIC - DCCT total beam & WCM bunched beam

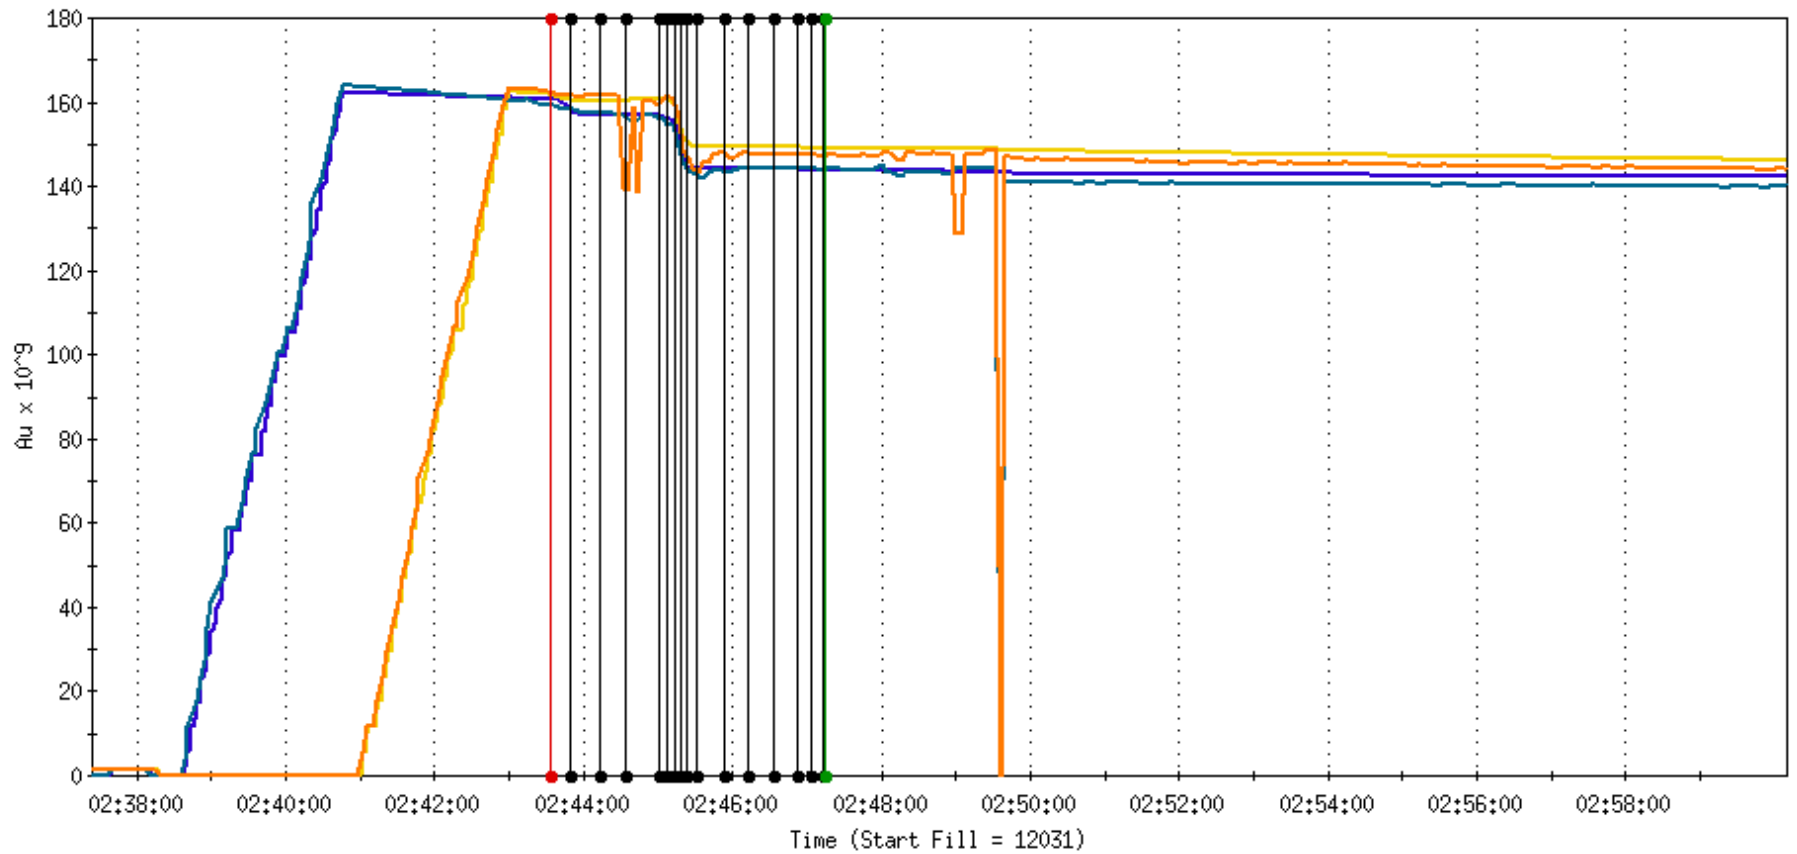


blueDCCTtotal yellowDCCTtotal blueWCMbunched yellowWCMbunched
 ev-accramp ev-stone ev-flattop ev-endramp


Store 12031

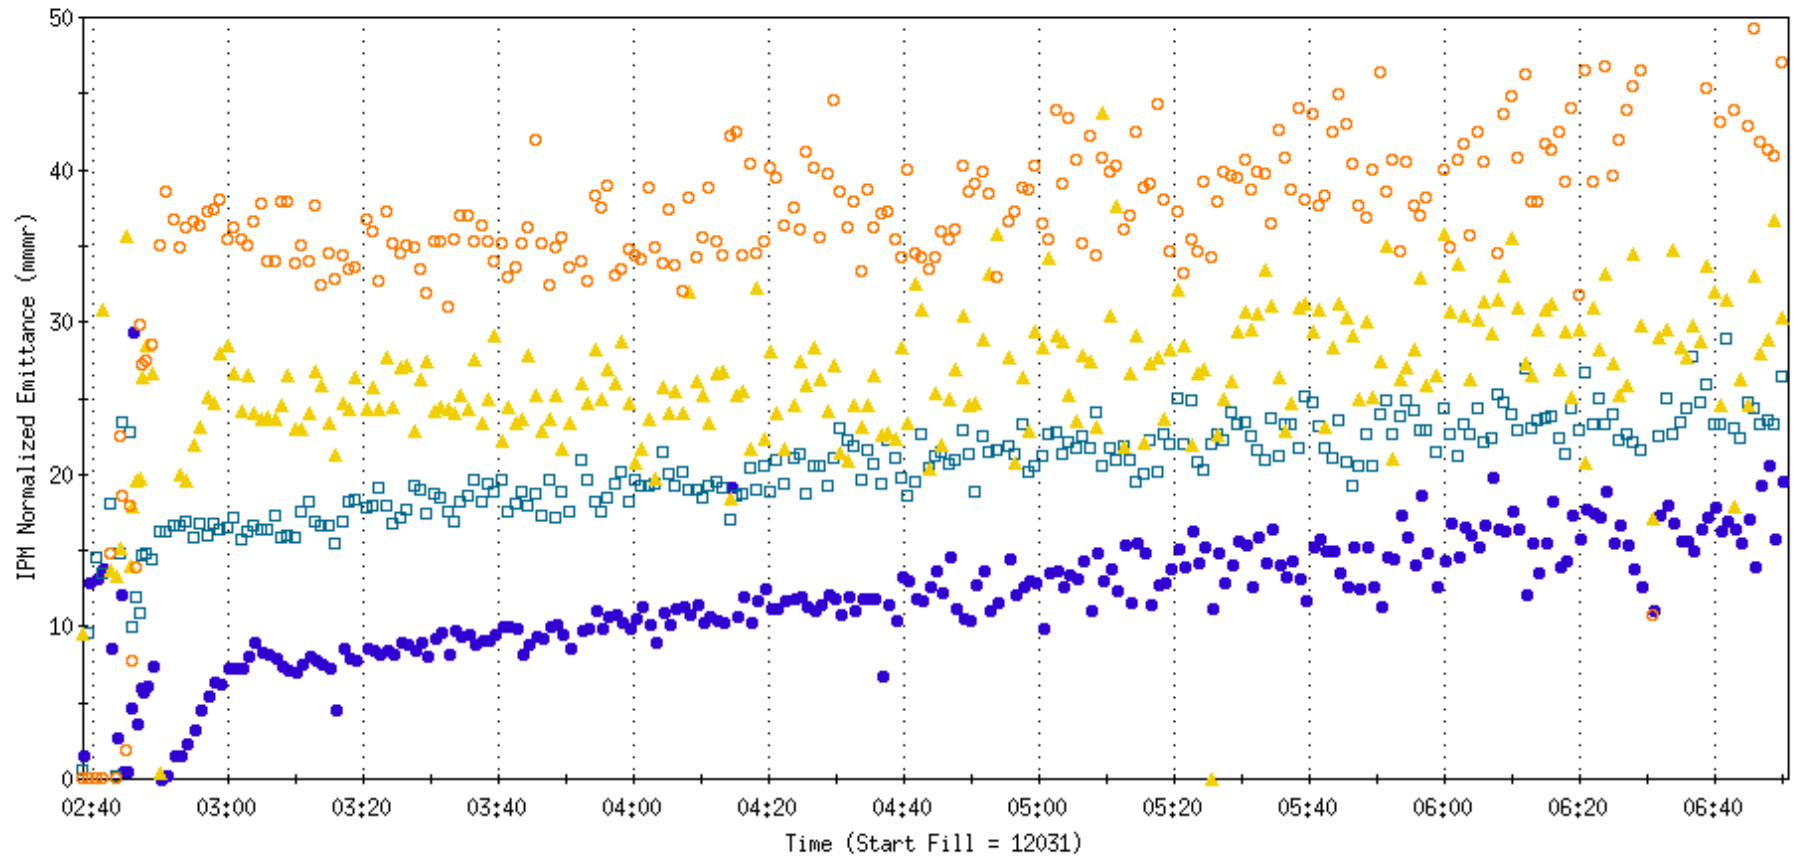

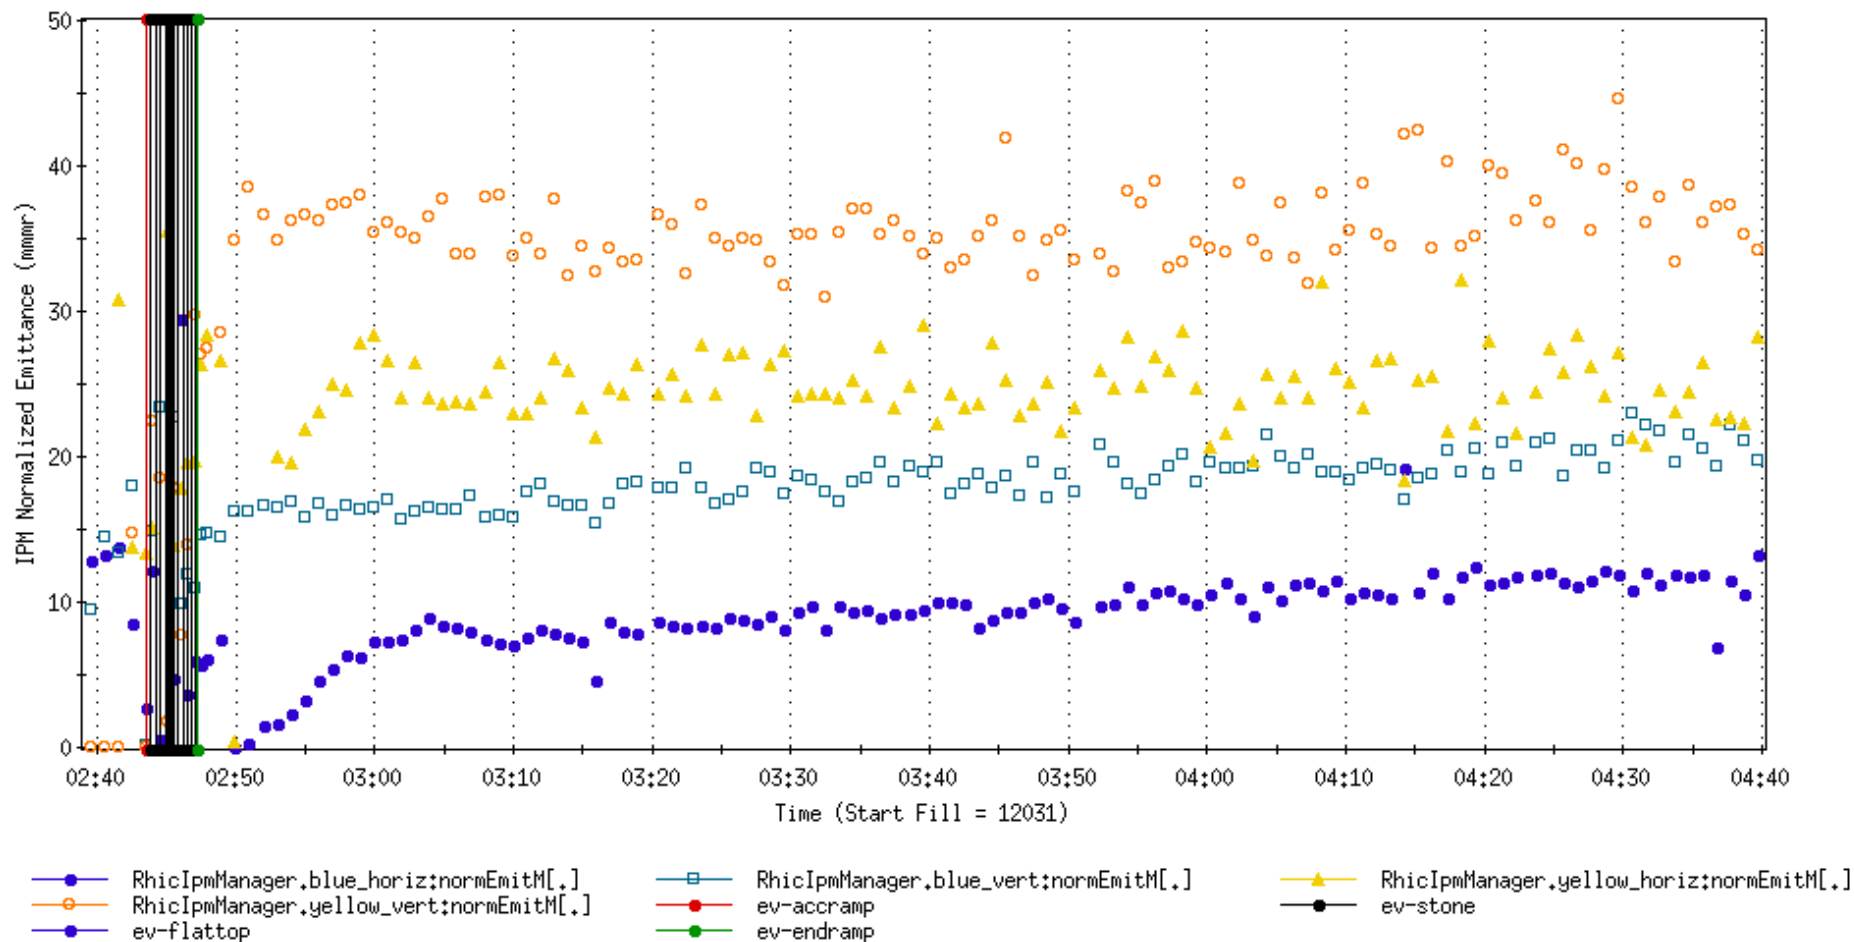


Store 12031

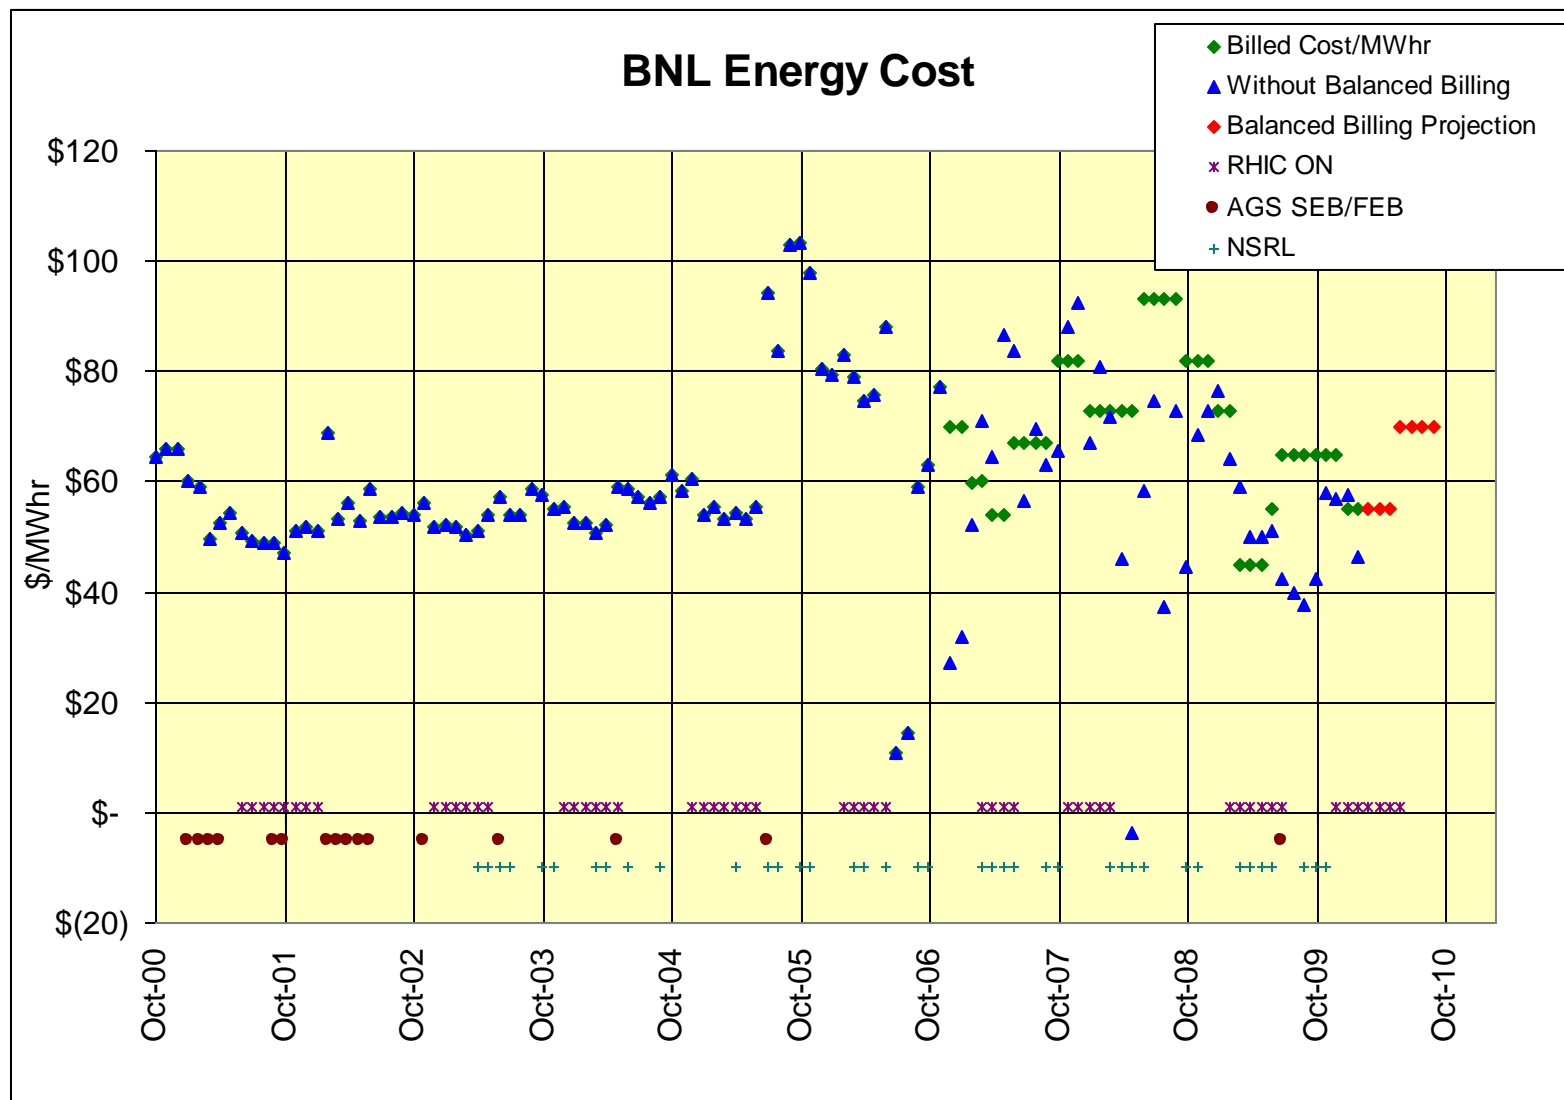


Through Feb 2010



with $\sqrt{s}=200$ extended 1 week (budget premitting)

-  concurrent with RHIC
-  setup with beams in both rings
-  ramp up luminosity

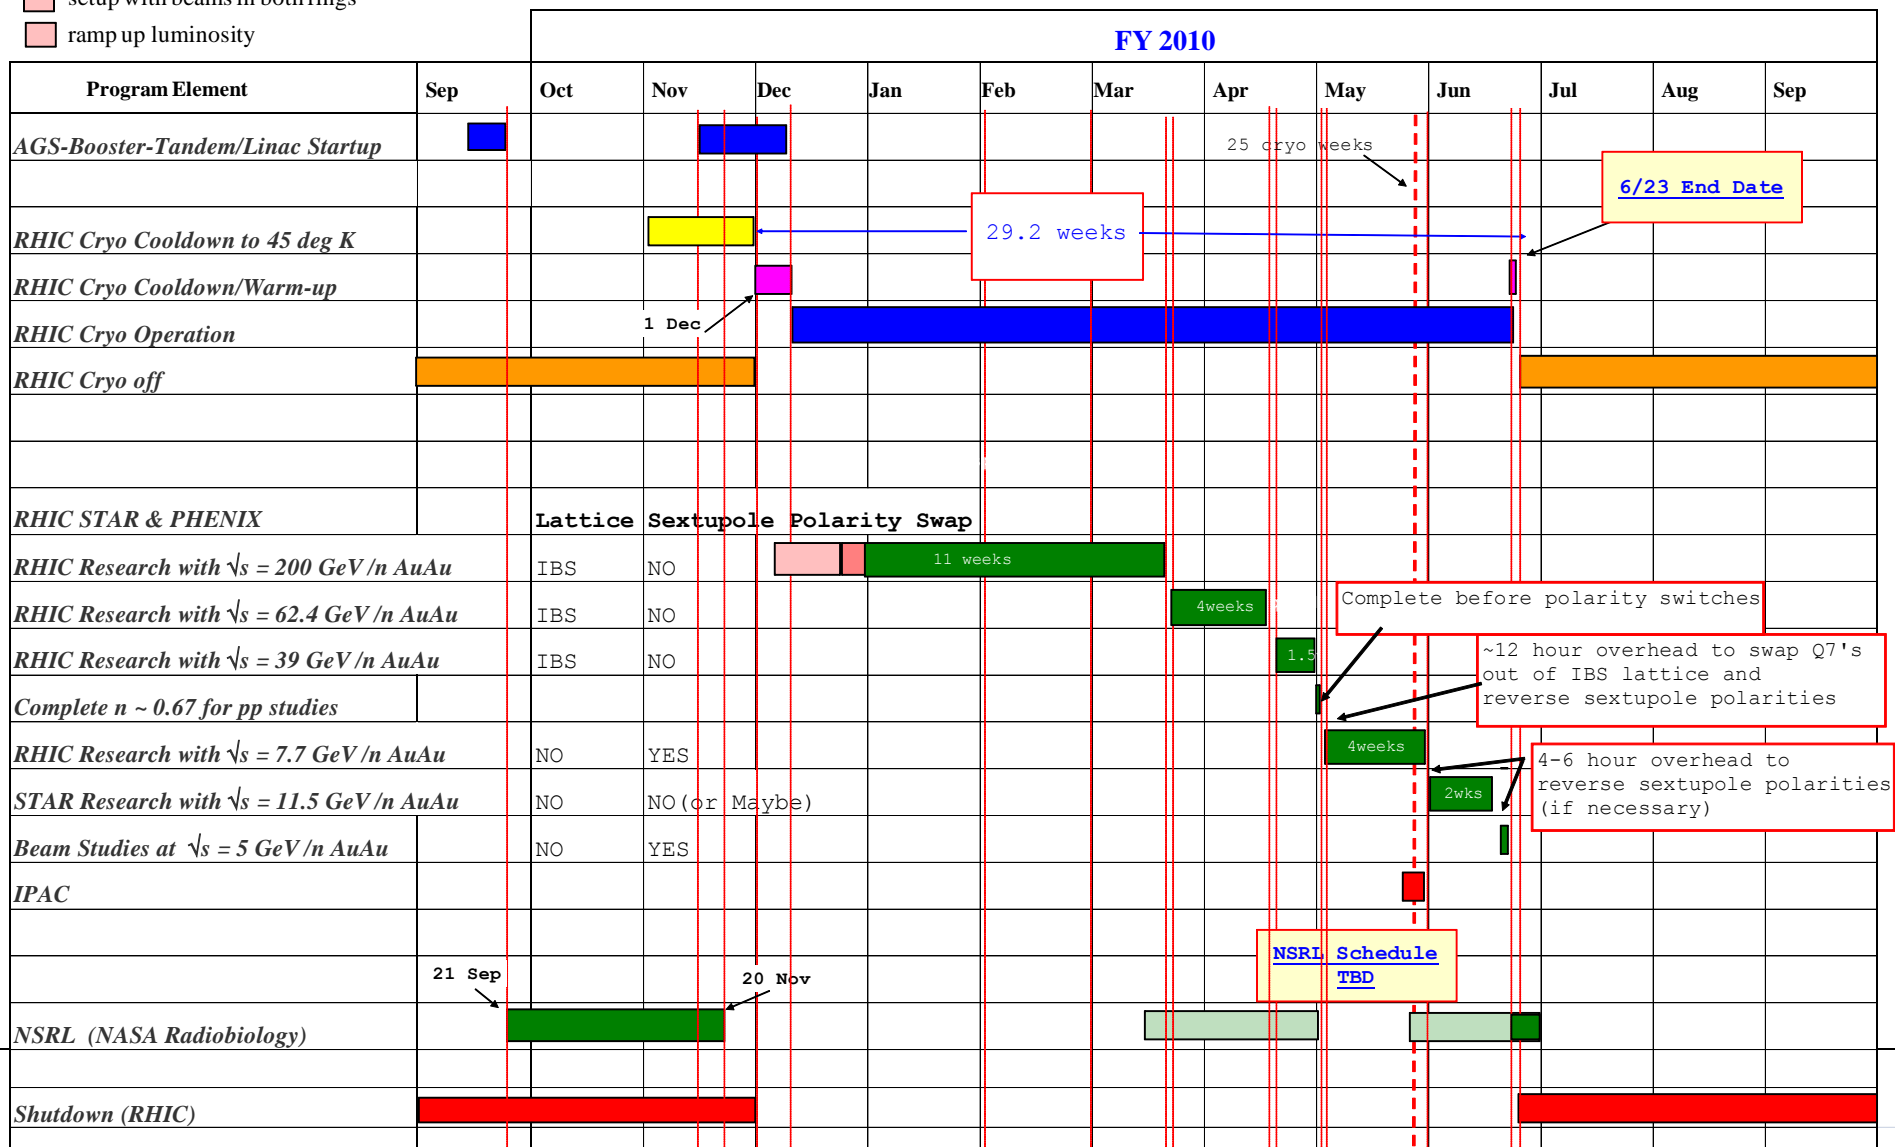


Future Topics

- Toward Smaller β^* - new quad triplets – D. Trbojevic


Archive

First Store Monday, 29 March, Store 12026

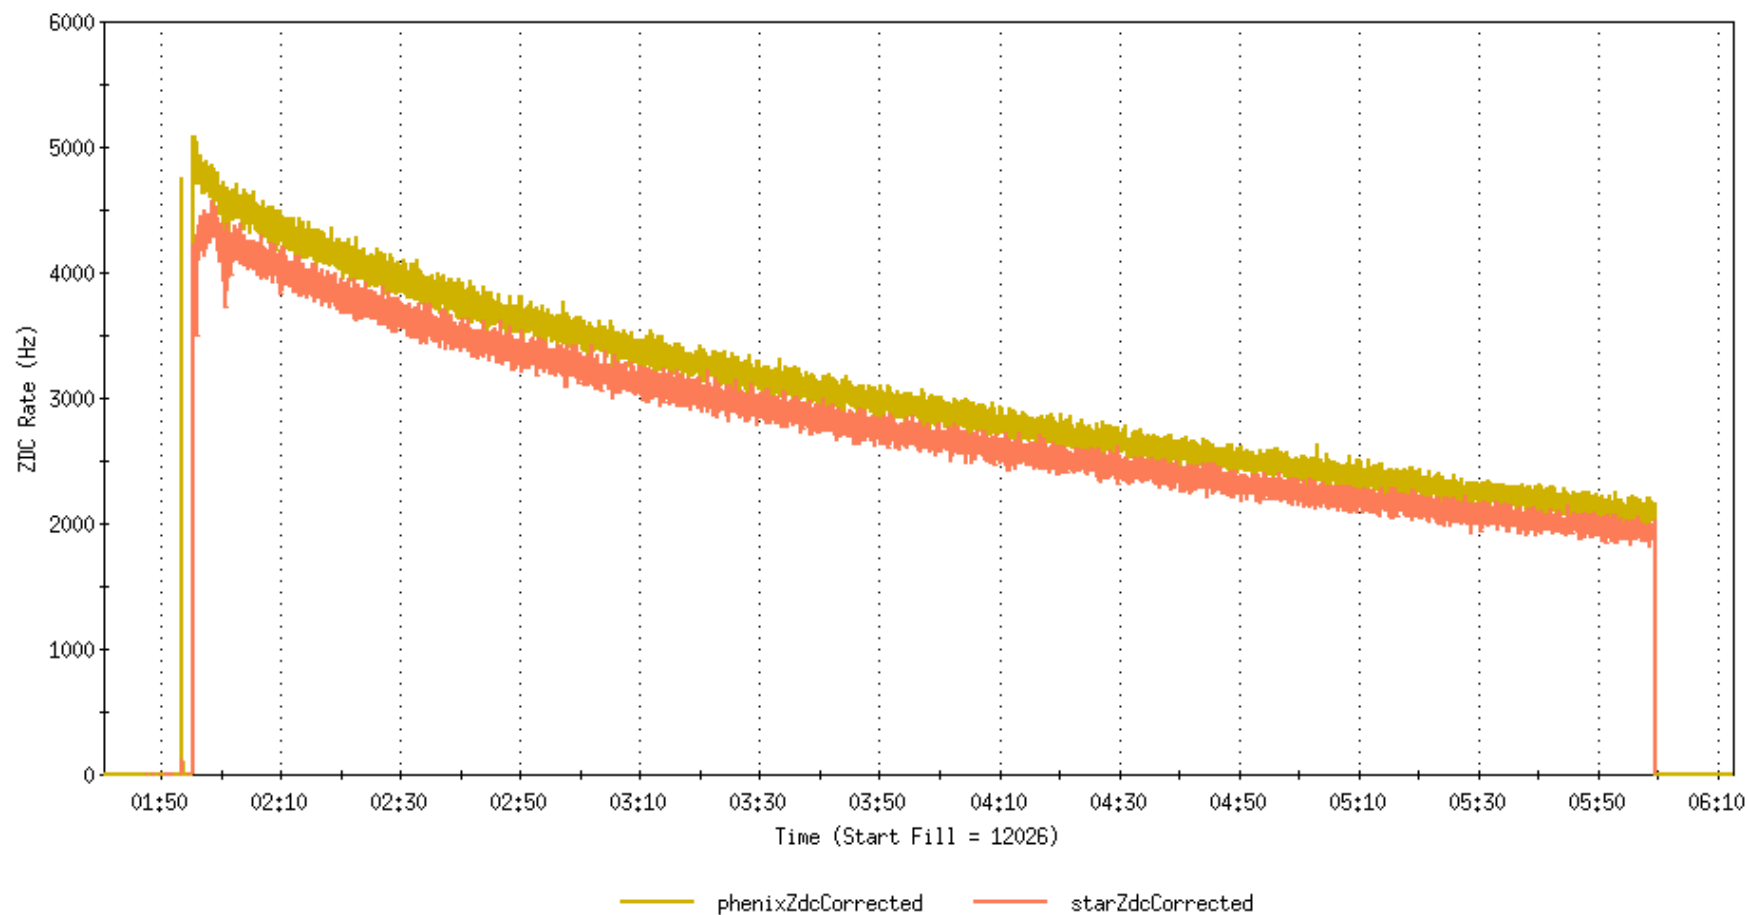


First Store Monday, 29 March, Store 12026


RHIC - DCCT total beam & WCM bunched beam

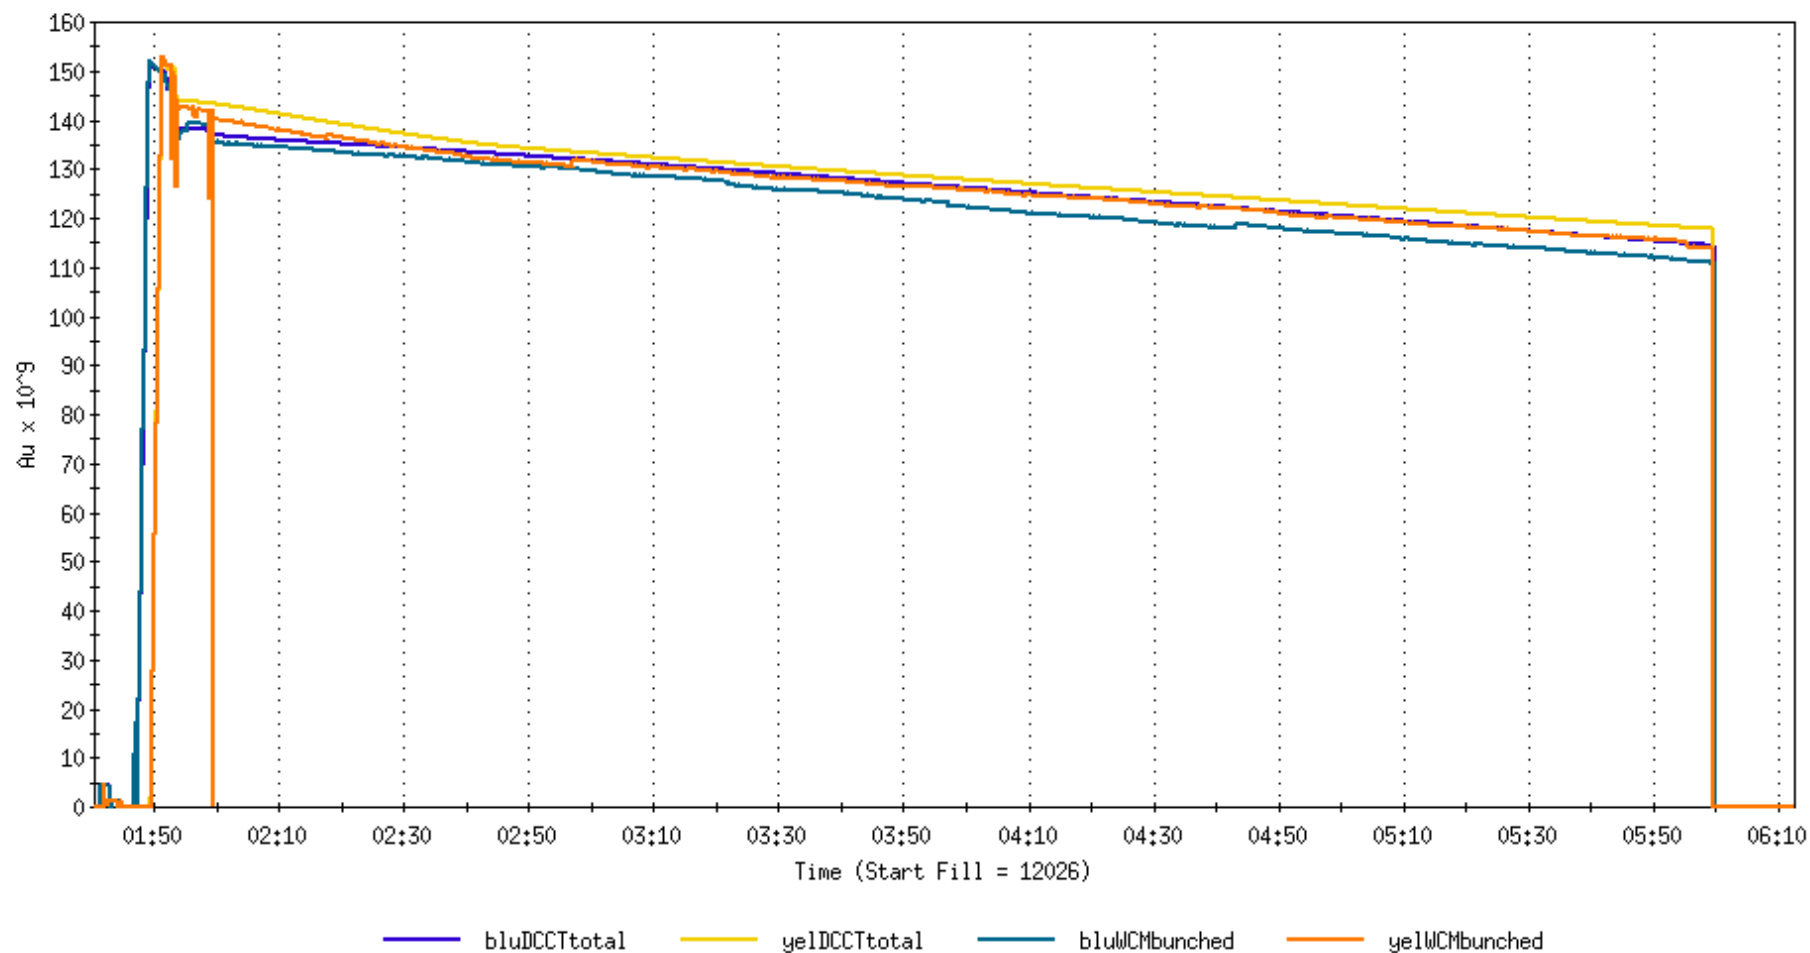


First Store Monday, 29 March, Store 12026

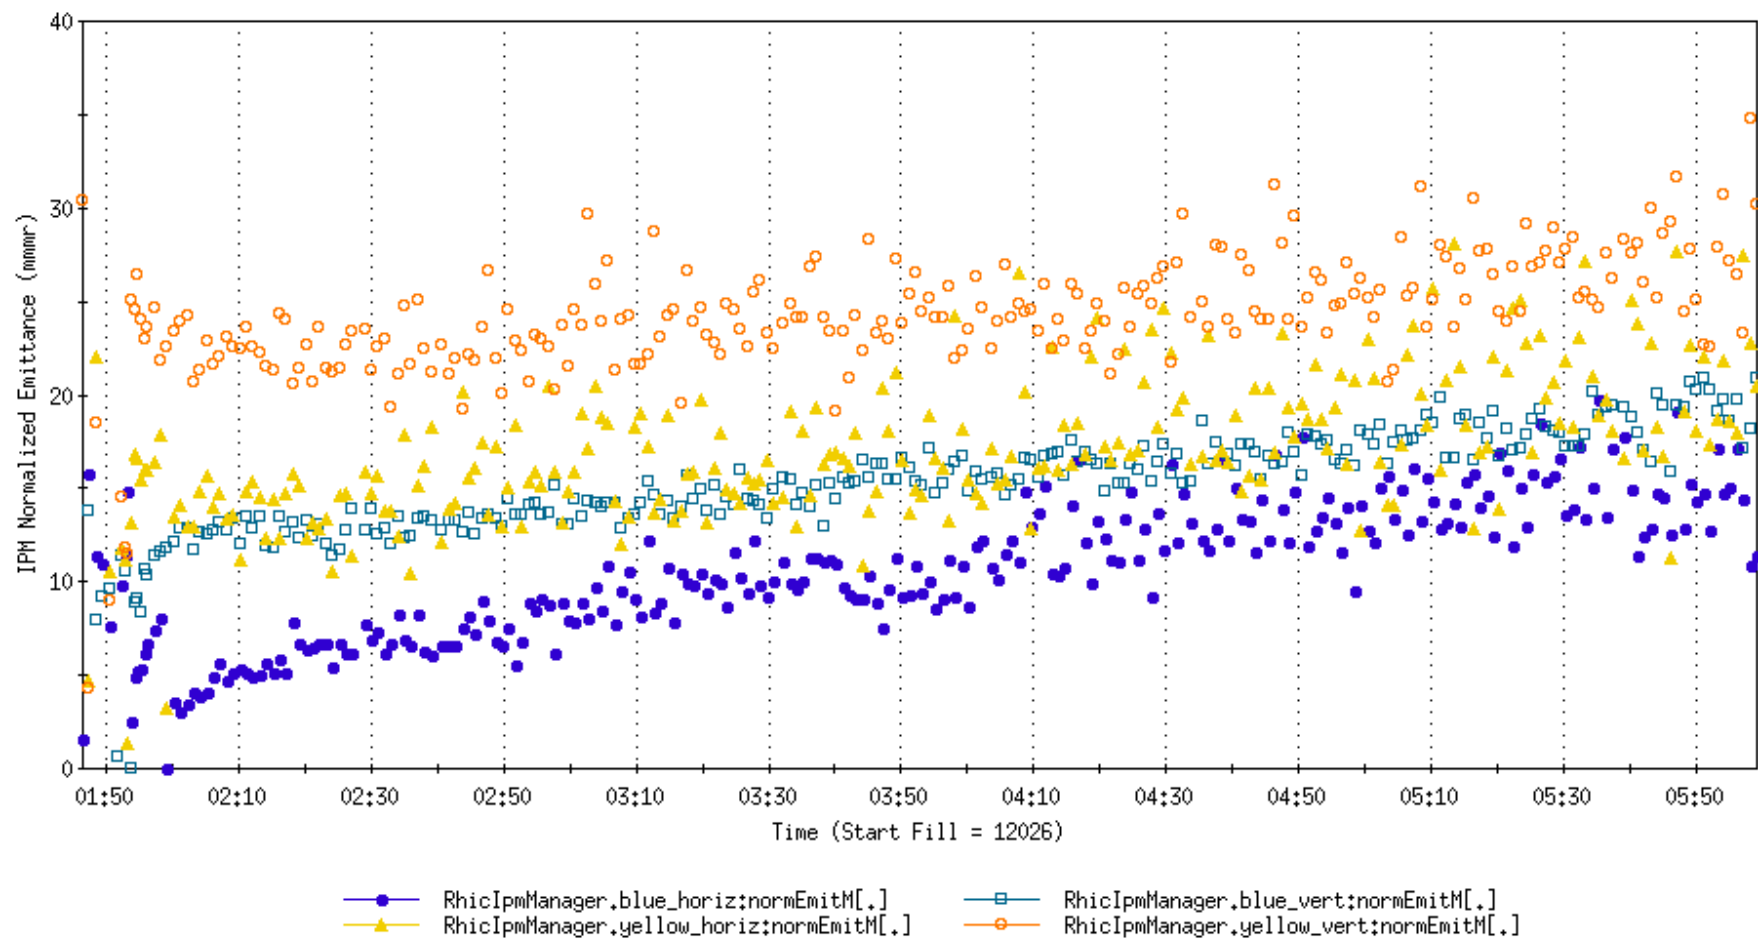

First Store Monday, 29 March, Store 12026

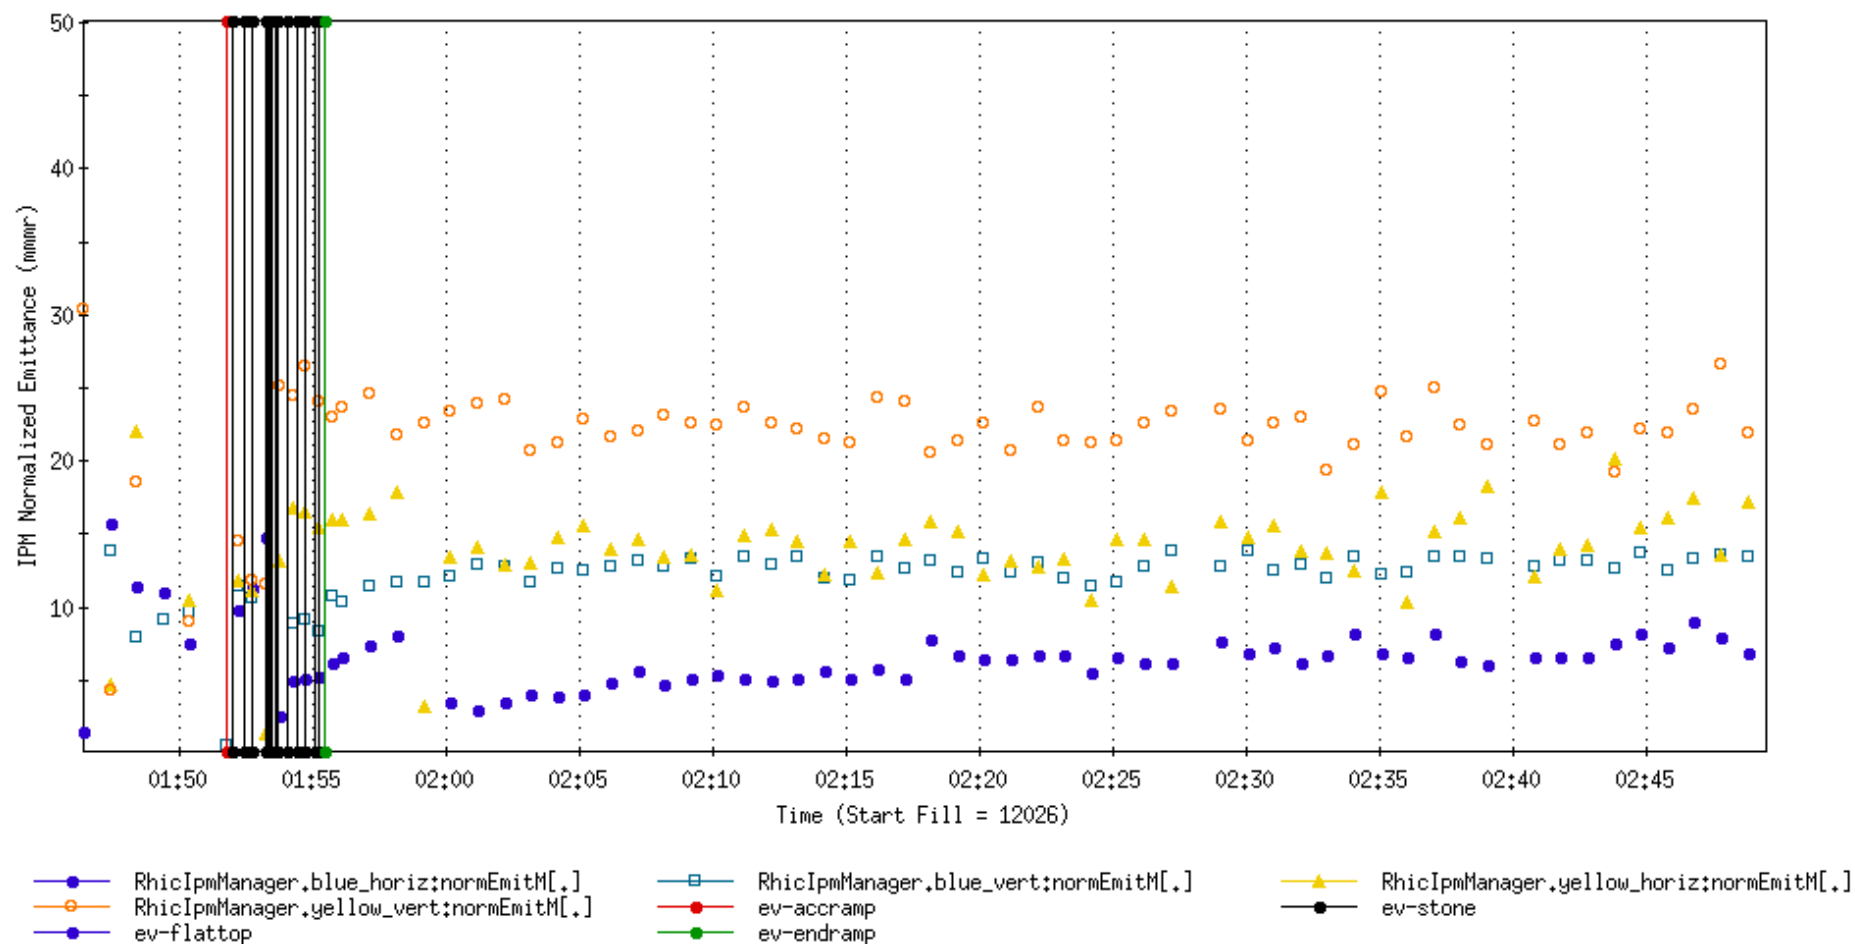


First Store Monday, 29 March, Store 12026

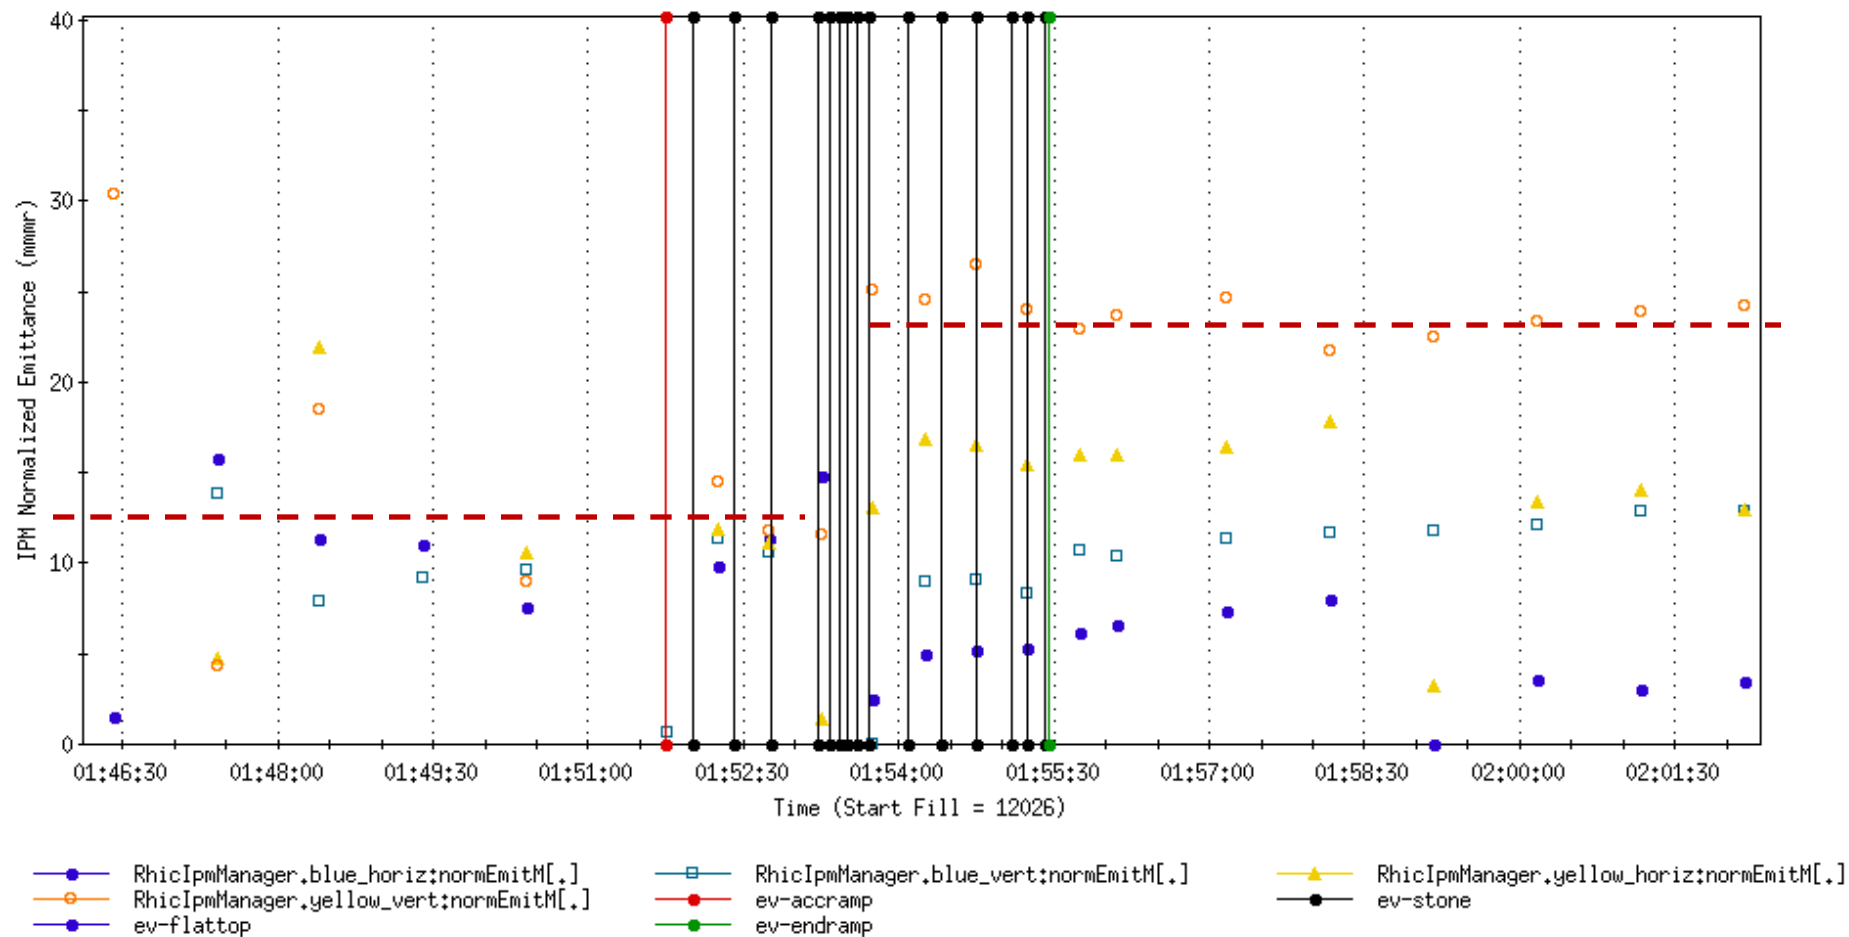


First Store Monday, 29 March, Store 12026


Long Emitt from WCM

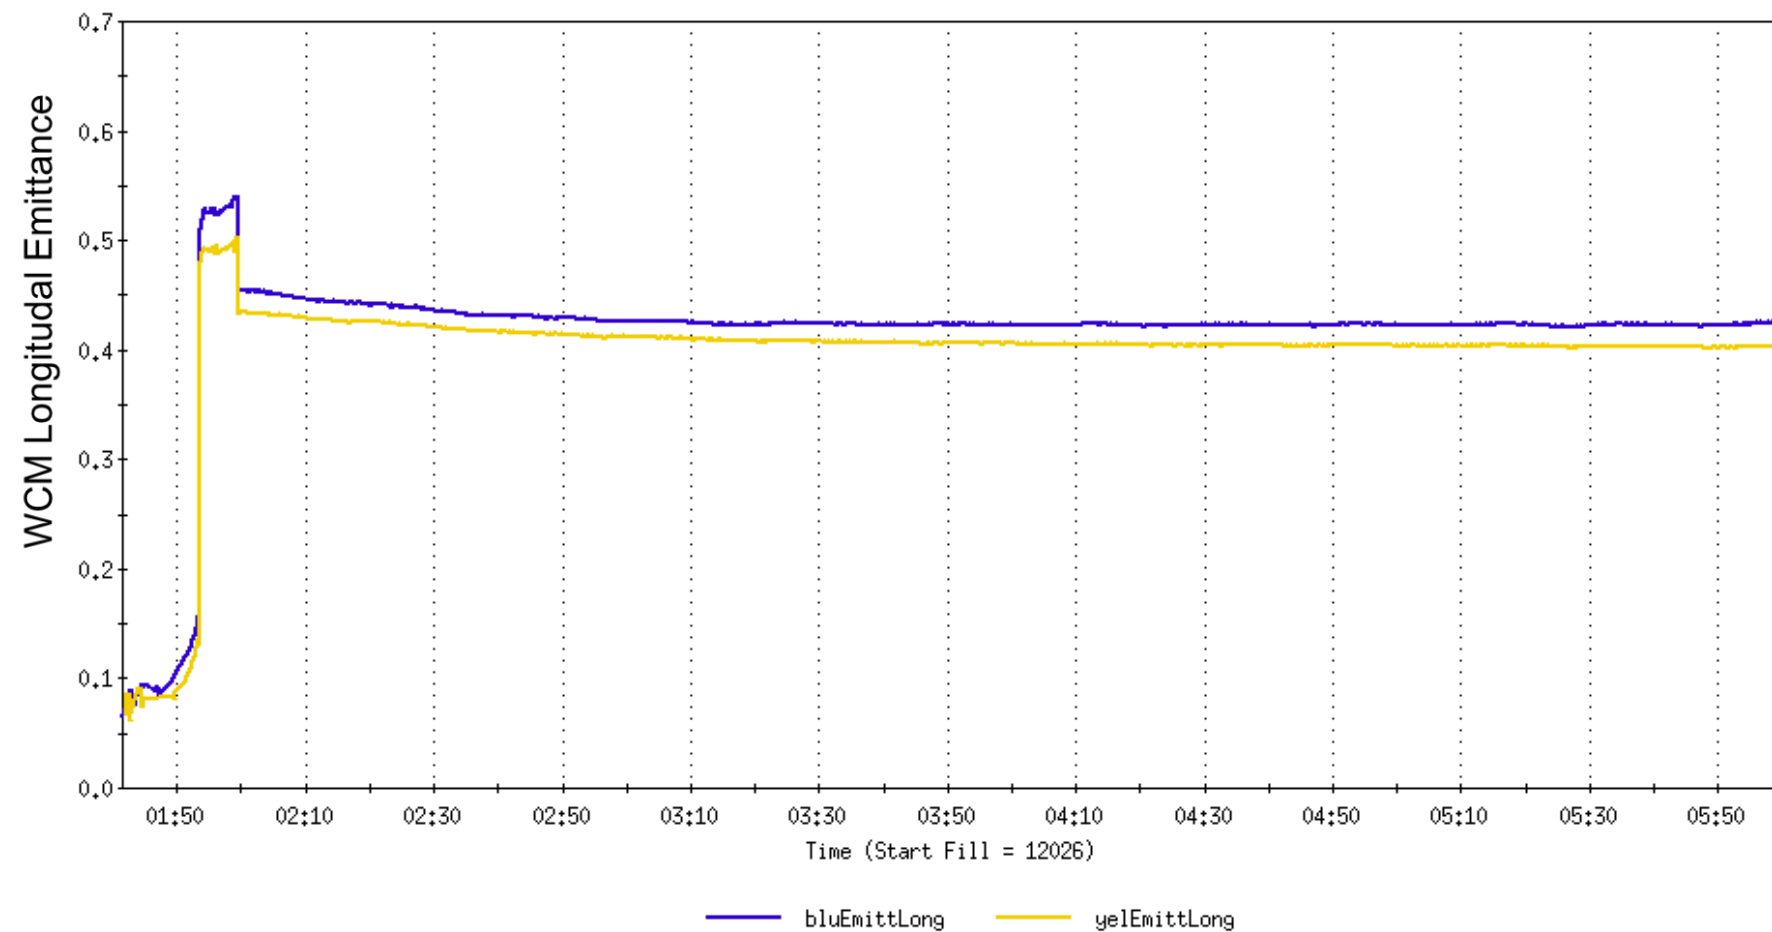

31 x 31 GeV/n Au horiz and vert emittances

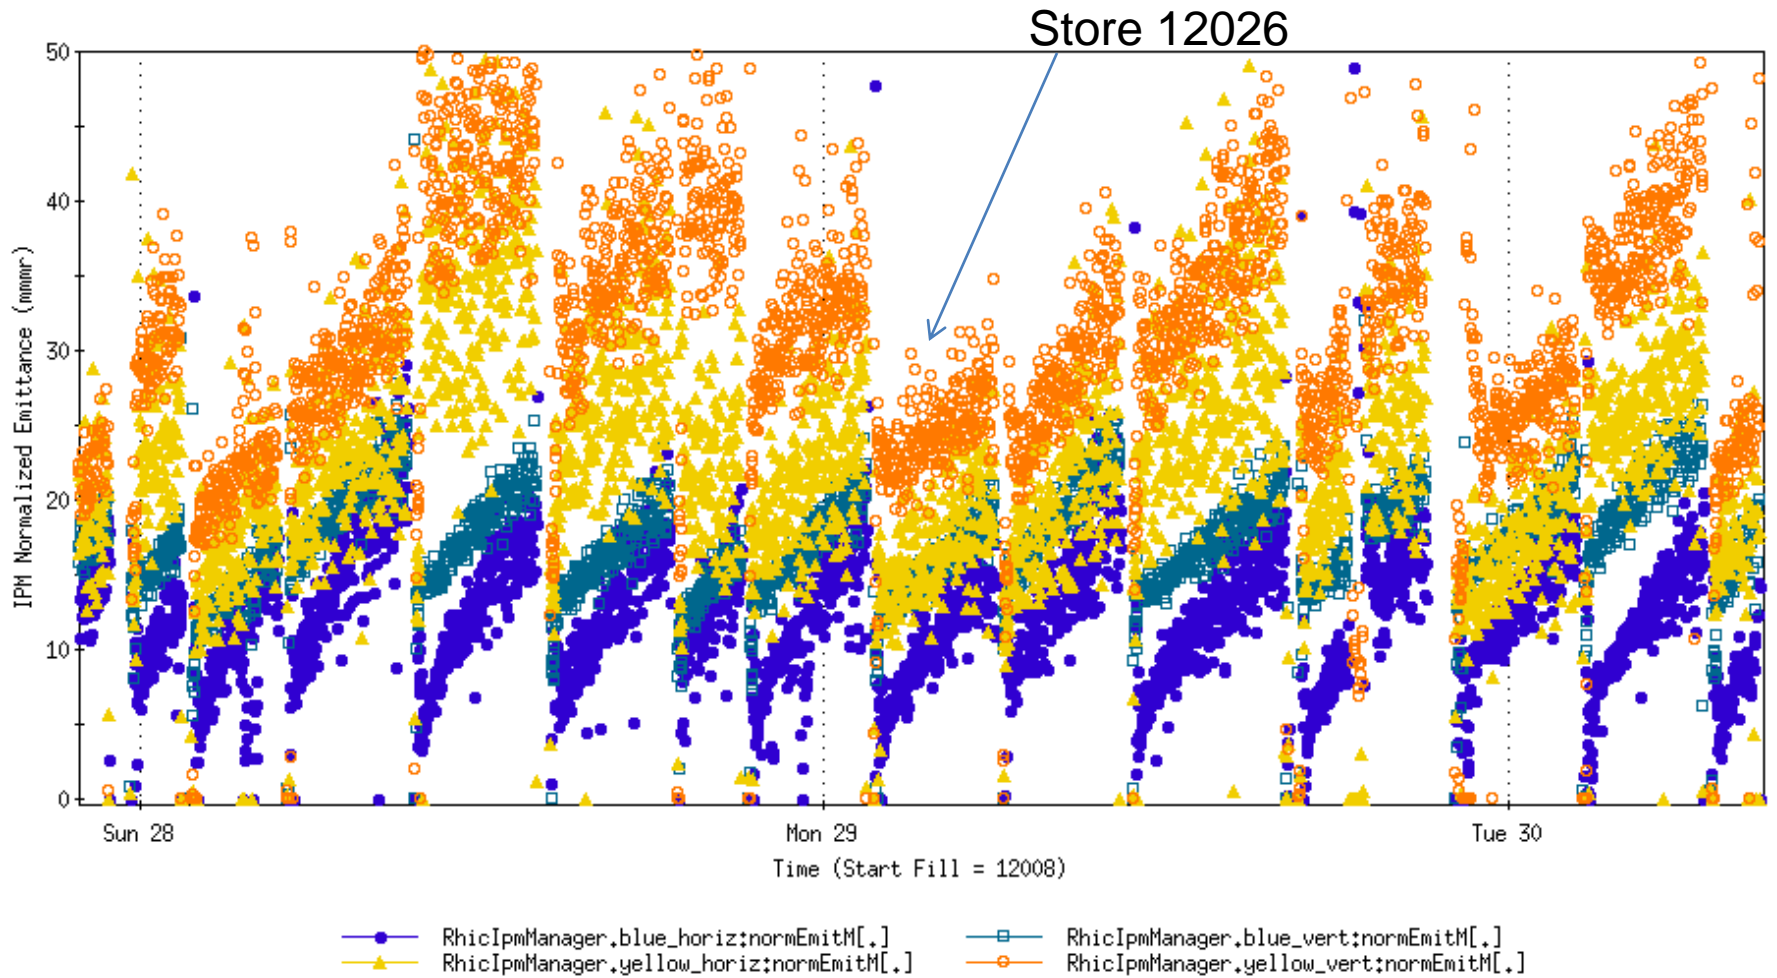


Run 10 100 x 100 GeV/n Au Delivered Luminosity

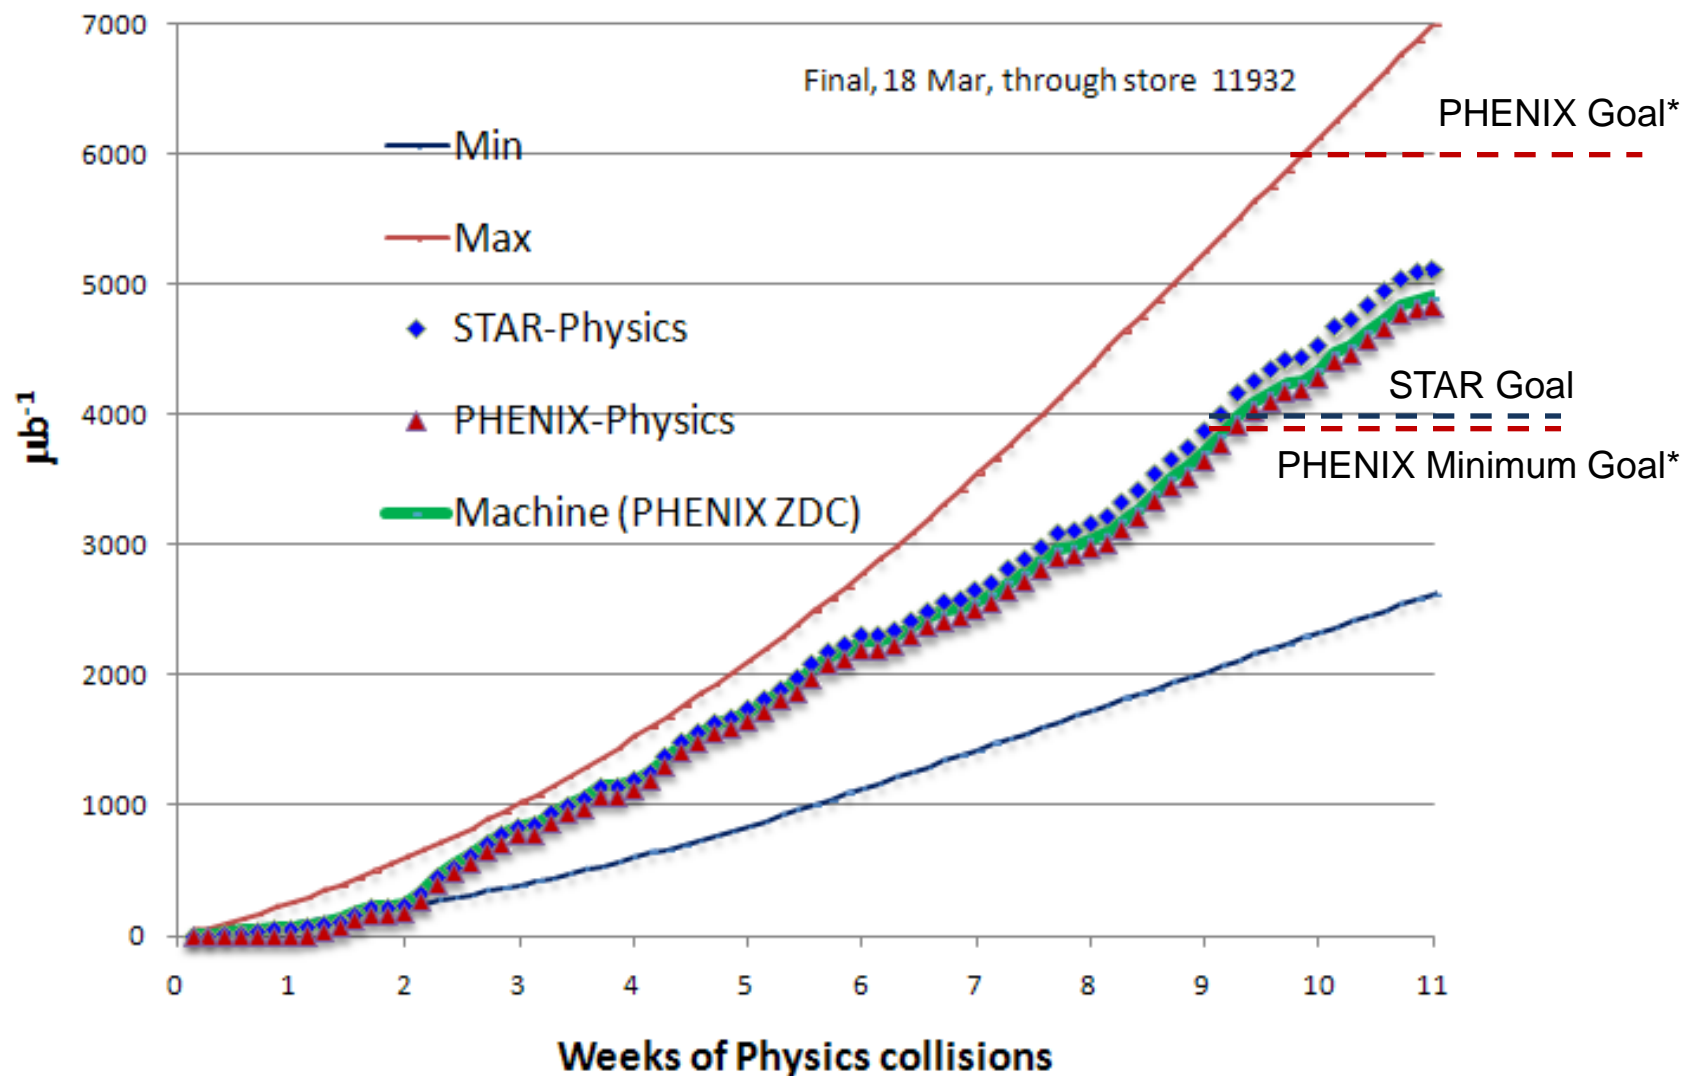


* With 20 cm sigma IR diamond

Run 10 100 x 100 GeV/n Au Delivered Luminosity per day

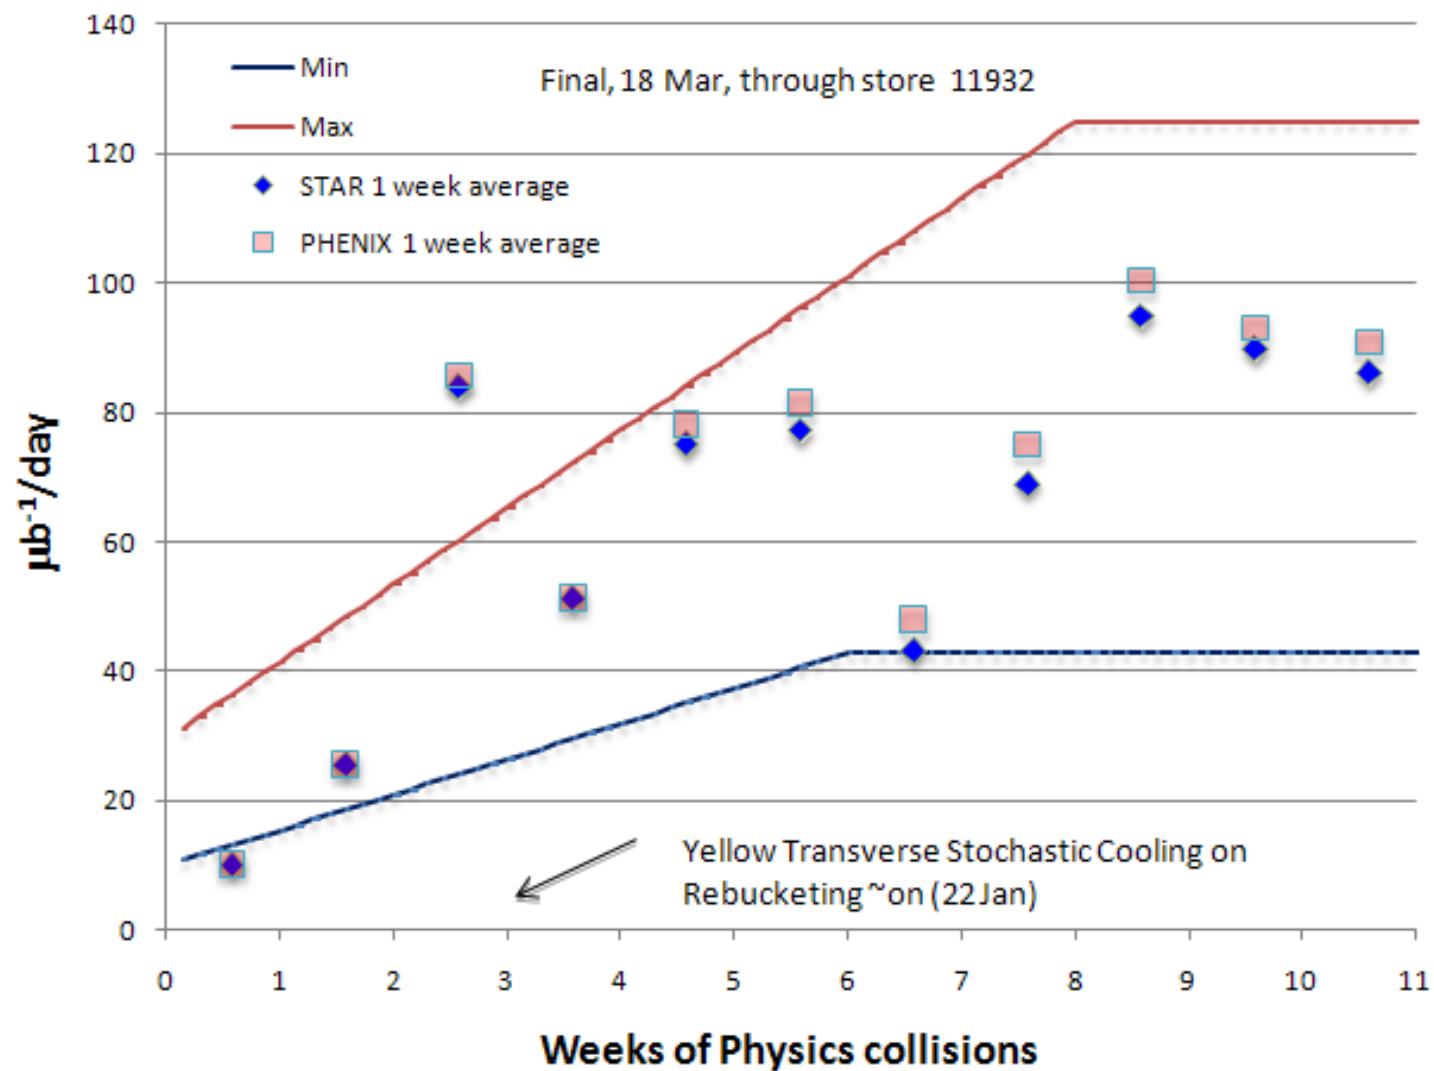


Average hours per week at store = 88.5


Run 10 (AuAu) -- Integrated Luminosity by week

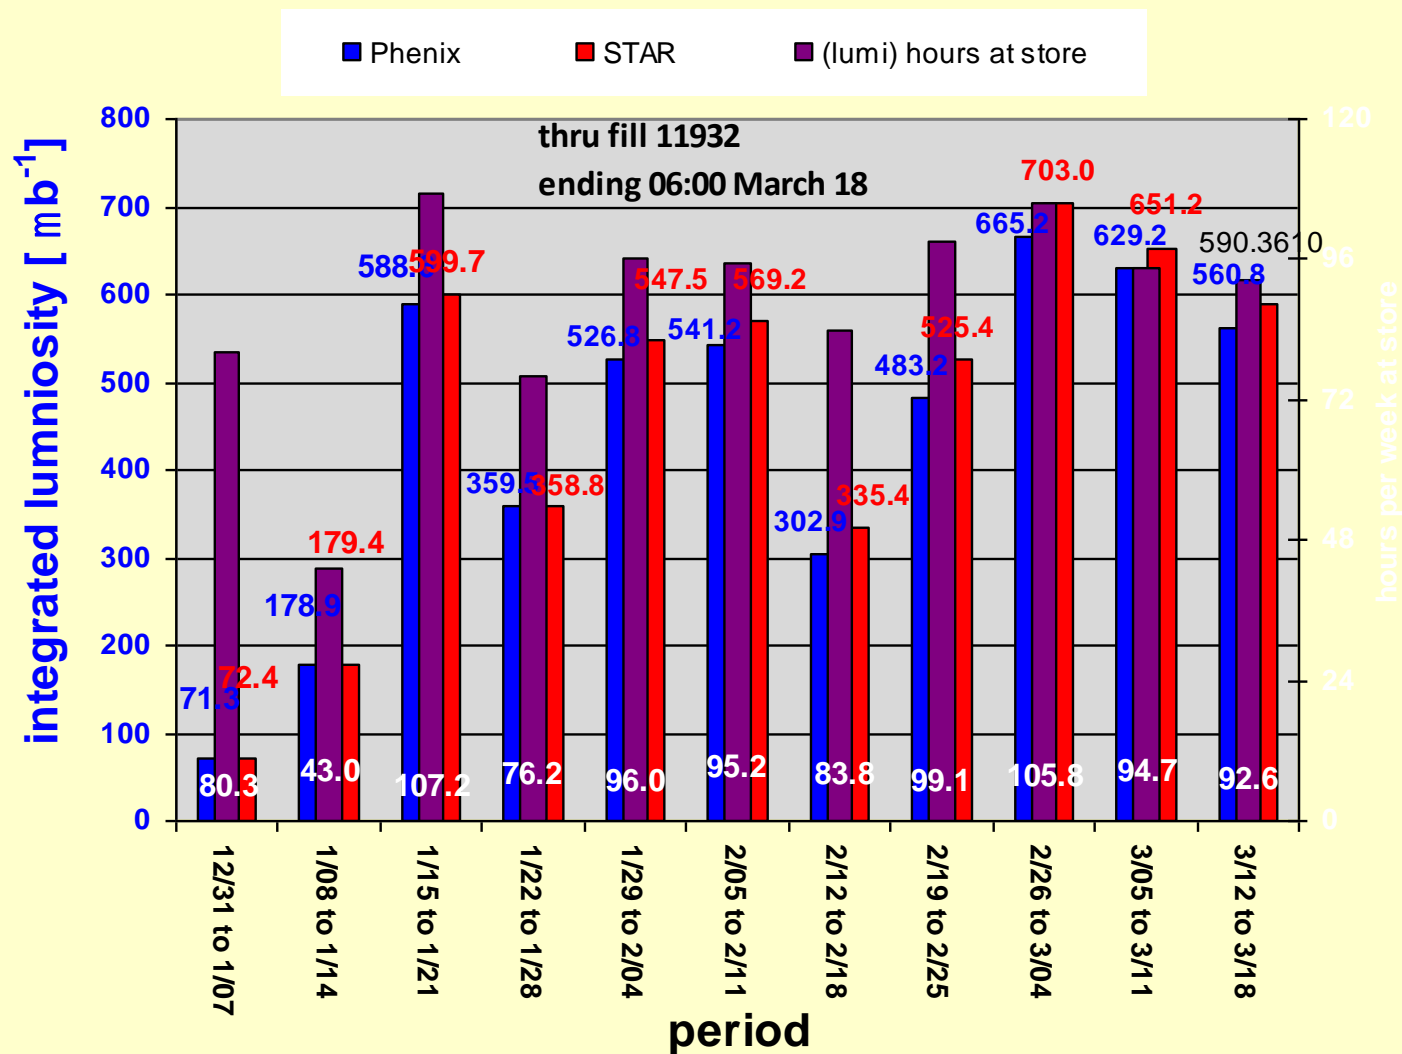

Through Jan 2010

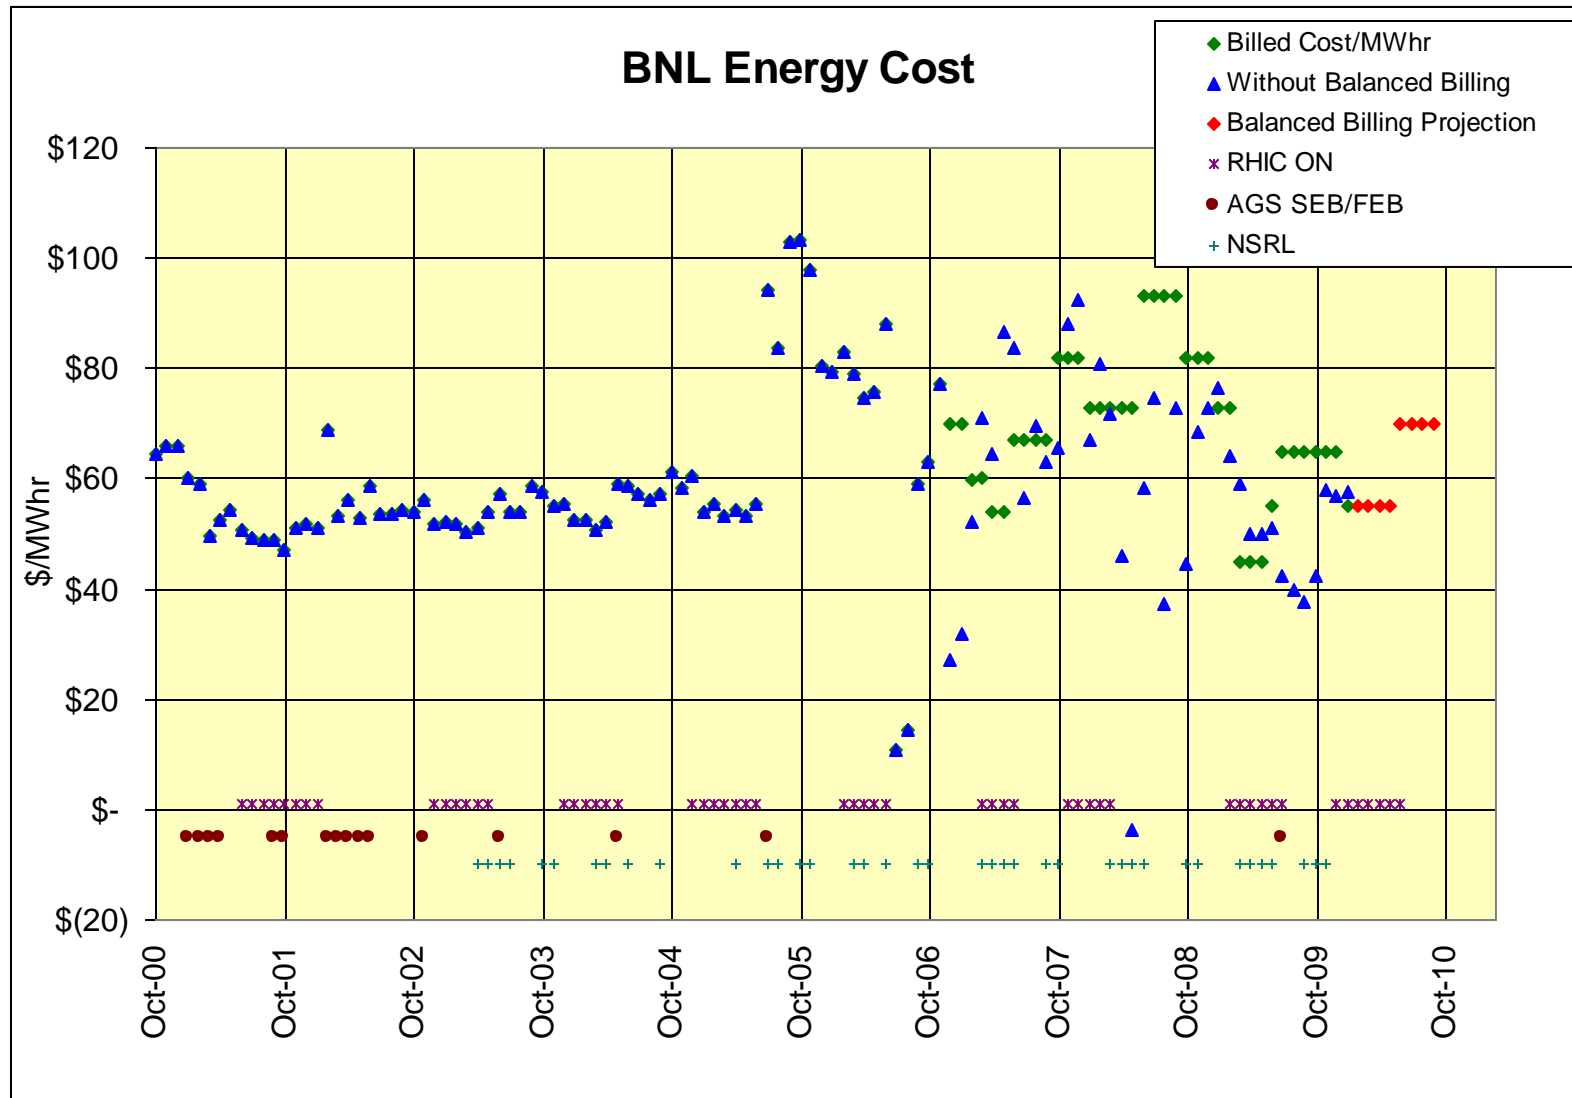

Through 2/28/10

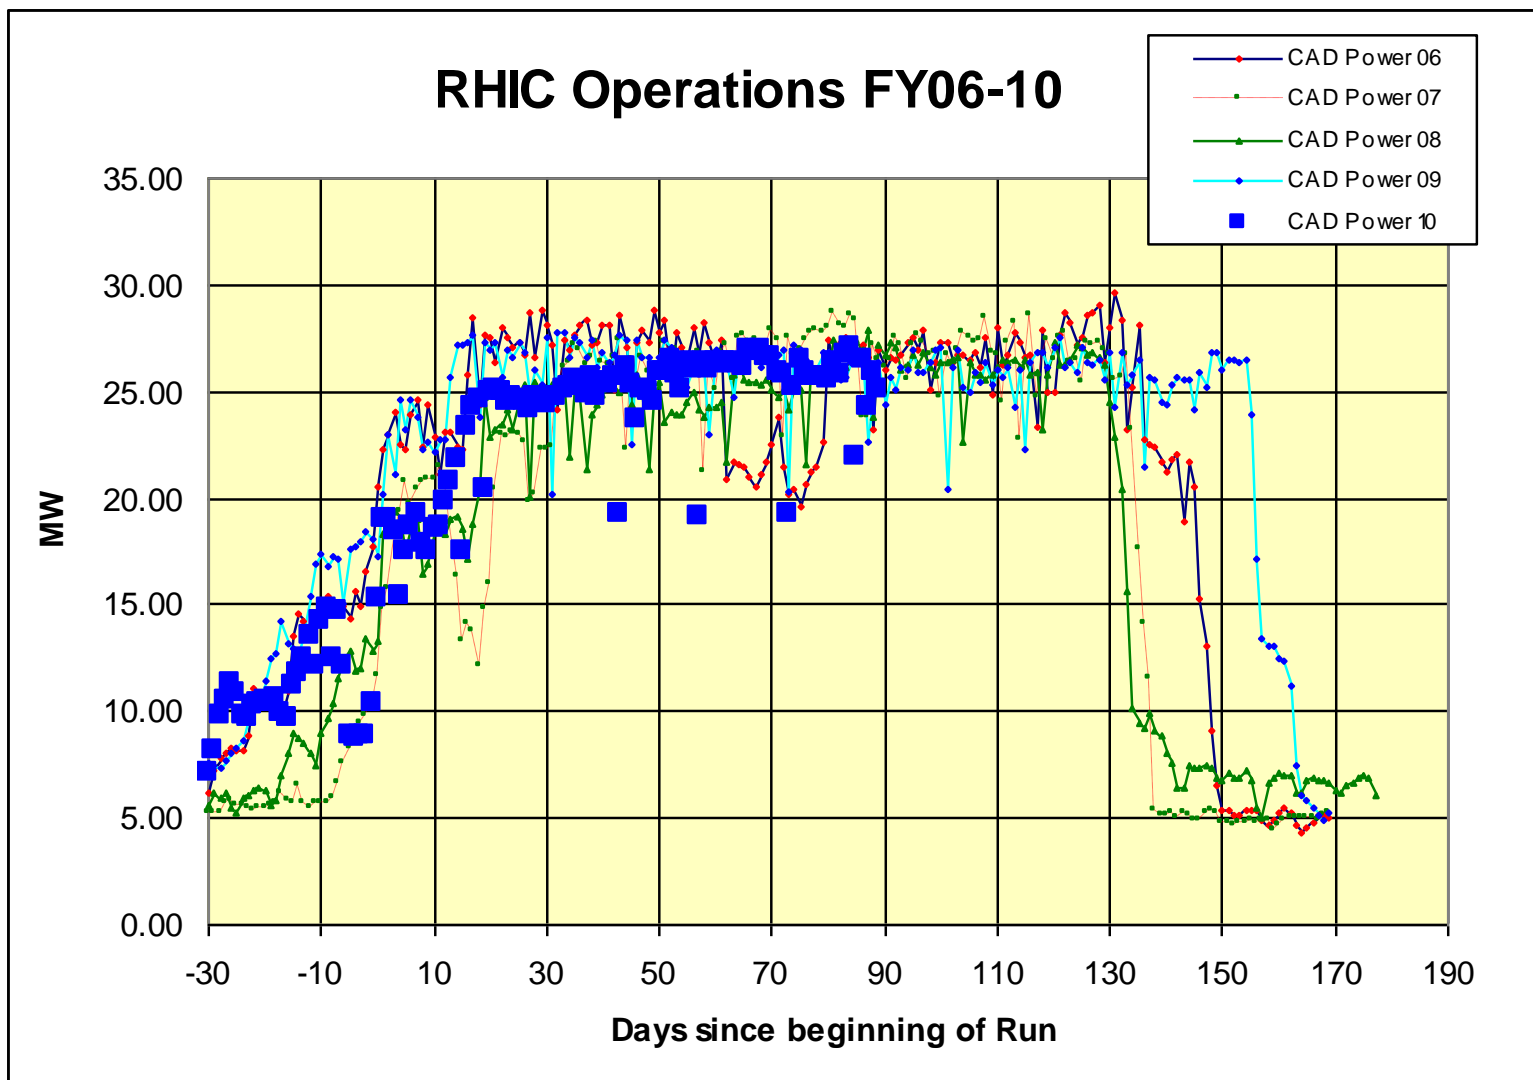

31 Dec 1st Physics Store 11340, 0.6 m β^* No cooling or rebucketing, STAR 3.2 μb^{-1} , 2.6 hr store

Ring	Bunches/Cycles	Avg Bunch in RHIC (10 ⁶ ions)	Avg Efficiency XCBM to RHIC	XCBM to Uxf1	<i>Uxf1 to Wxf</i>	<i>Wxf to Arc</i>	<i>Arc to RHIC</i>
Blue	56/56	909	0.836	1.056	<i>0.963</i>	<i>0.992</i>	<i>0.828</i>
Yellow	56/56	990	0.971	1.085	<i>0.962</i>	<i>0.959</i>	<i>0.970</i>

18 Jan Physics Store 11489, 0.6 m β^* No cooling or rebucketing, STAR 22.6 μb^{-1} , 3.9 hr store

Ring	Bunches/Cycles	Avg Bunch in RHIC (10 ⁶ ions)	Avg Efficiency XCBM to RHIC	XCBM to Uxf1	<i>Uxf1 to Wxf</i>	<i>Wxf to Arc</i>	<i>Arc to RHIC</i>
Blue	111/28	1196	0.911	1.024	<i>0.961</i>	<i>0.999</i>	<i>0.927</i>
Yellow	111/29	1168	0.879	1.023	<i>0.961</i>	<i>0.989</i>	<i>0.905</i>


28 Feb Physics Store 11824, 0.7 m β^* with some cooling and with rebucketing, STAR 32.7 μb^{-1} , 3.9 hr store

Ring	Bunches/Cycles	Avg Bunch in RHIC (10 ⁶ ions)	Avg Efficiency XCBM to RHIC	XCBM to Uxf1	<i>Uxf1 to Wxf</i>	<i>Wxf to Arc</i>	<i>Arc to RHIC</i>
Blue	111/28	1262	0.917	0.975	<i>0.961</i>	<i>1.001</i>	<i>0.977</i>
Yellow	111/28	1246	0.910	0.961	<i>0.964</i>	<i>0.988</i>	<i>0.994</i>

2 Mar Physics Store 11834, 0.7 m β^* with some cooling and with rebucketing, STAR 29.4 μb^{-1} , 3.9 hr store)


Ring	Bunches/Cycles	Avg Bunch in RHIC (10 ⁶ ions)	Avg Efficiency XCBM to RHIC	XCBM to Uxf1	<i>Uxf1 to Wxf</i>	<i>Wxf to Arc</i>	<i>Arc to RHIC</i>
Blue	111/28	1354	0.927	0.990	<i>0.965</i>	<i>1.003</i>	<i>0.968</i>
Yellow	111/28	1377	0.931	0.990	<i>0.964</i>	<i>0.989</i>	<i>0.987</i>

Through 2/28/10

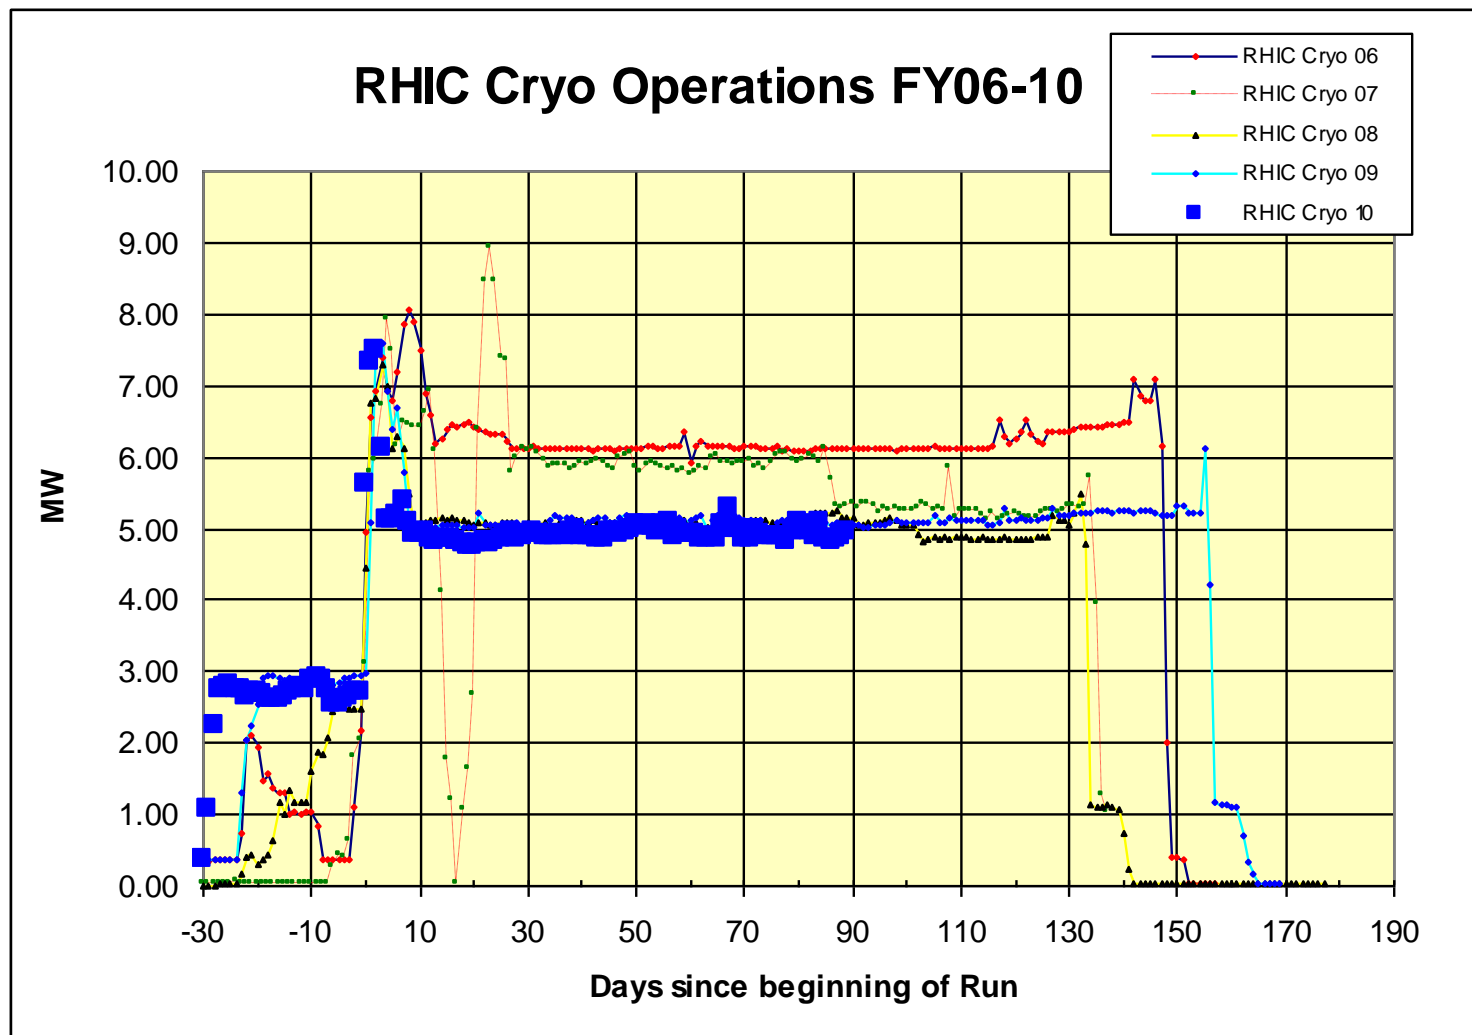

Through 2/28/10

BNL Energy Use FY 2009-10

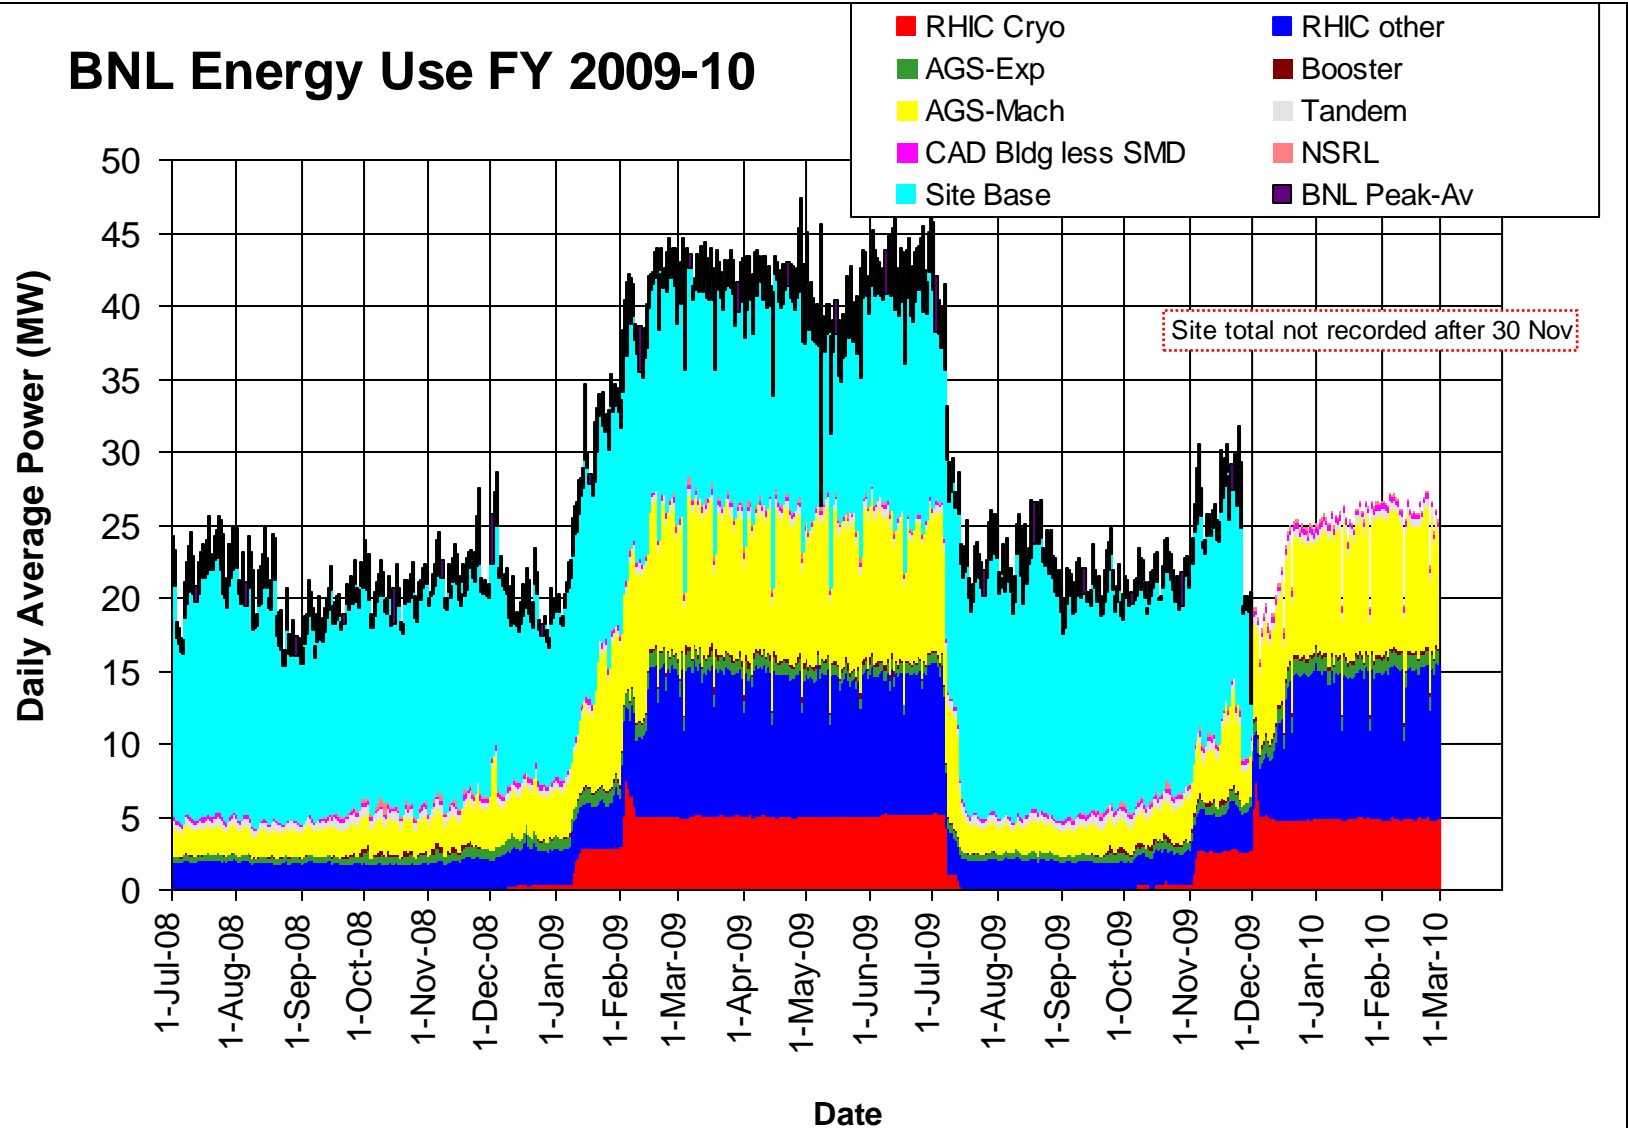

Revised Run 10 Plan, Nov 25, 2009

	Physics production or beam studies weeks	
$\sqrt{s_{NN}}$ (GeV)	25-cryoweeek run	27-cryoweeek run
200	10	10
62.4	4	4
39	1.5	1.5
27	0	0
18	0	0
11.5 @ STAR	0	2
7.7	4	4
Beam studies @ 5 GeV and @ $v \approx 0.67$	0.5	0.5

Run 10 Au-Au Goals

11/19/09

- STAR

- $\sqrt{s} = 200 \text{ GeV/n}$

- Luminosity Sampled/Delivered = 2/4 nb⁻¹
 - 250M Central Events
 - 300M Min-bias events

- PHENIX

- $\sqrt{s} = 200 \text{ GeV/n}$

- Luminosity Recorded/Delivered = 1.4/>6 nb⁻¹
 - Minimum Goal:
 - Luminosity Recorded/Delivered = 1.1/3.9 nb⁻¹

Time from start of 4.5 deg cooldown to Physics

