

Run 13 RHIC Machine/Experiments Meeting

30 April 2013

Agenda:

- Status Reports
- Arguments for/against low energy Au run

Run 13 plan based on 17 weeks cryo operation


- ✓ 11 Feb, Begin cool-down to 4.5K
- ✓ 15 Feb, Cool-down to 4.5K in Blue and Yellow Ring complete, begin magnet setup
- ✓ 26 Feb, first collisions
- ✓ 15 Feb -1 Mar, RHIC $\sqrt{s} = 510$ GeV pp machine setup
- ✓ 1-8 Mar, machine ramp-up with 8 hr/night for experiment setup
- ✓ 9 Mar (store 17201), begin $\sqrt{s} = 510$ GeV pp physics run

today, 30 Apr...


- decision time for switch to $\sqrt{s} = 15$ GeV/n AuAu.



if decide to run AuAu for 2.5 weeks (2 weeks physics)

- 20 May (Monday), switch to 15 GeV/n AuAu – begin ½ week AuAu setup
- 24 May (Friday), begin 15 GeV/n AuAu physics
- 7 June (Friday), end ~2.0 week $\sqrt{s} = 15$ GeV/n AuAu physics run or 13.0 week $\sqrt{s} = 510$ GeV pp physics run, begin cryo warm-up
- 10 June, cryo warm-up ~complete (17.0 cryo-weeks)

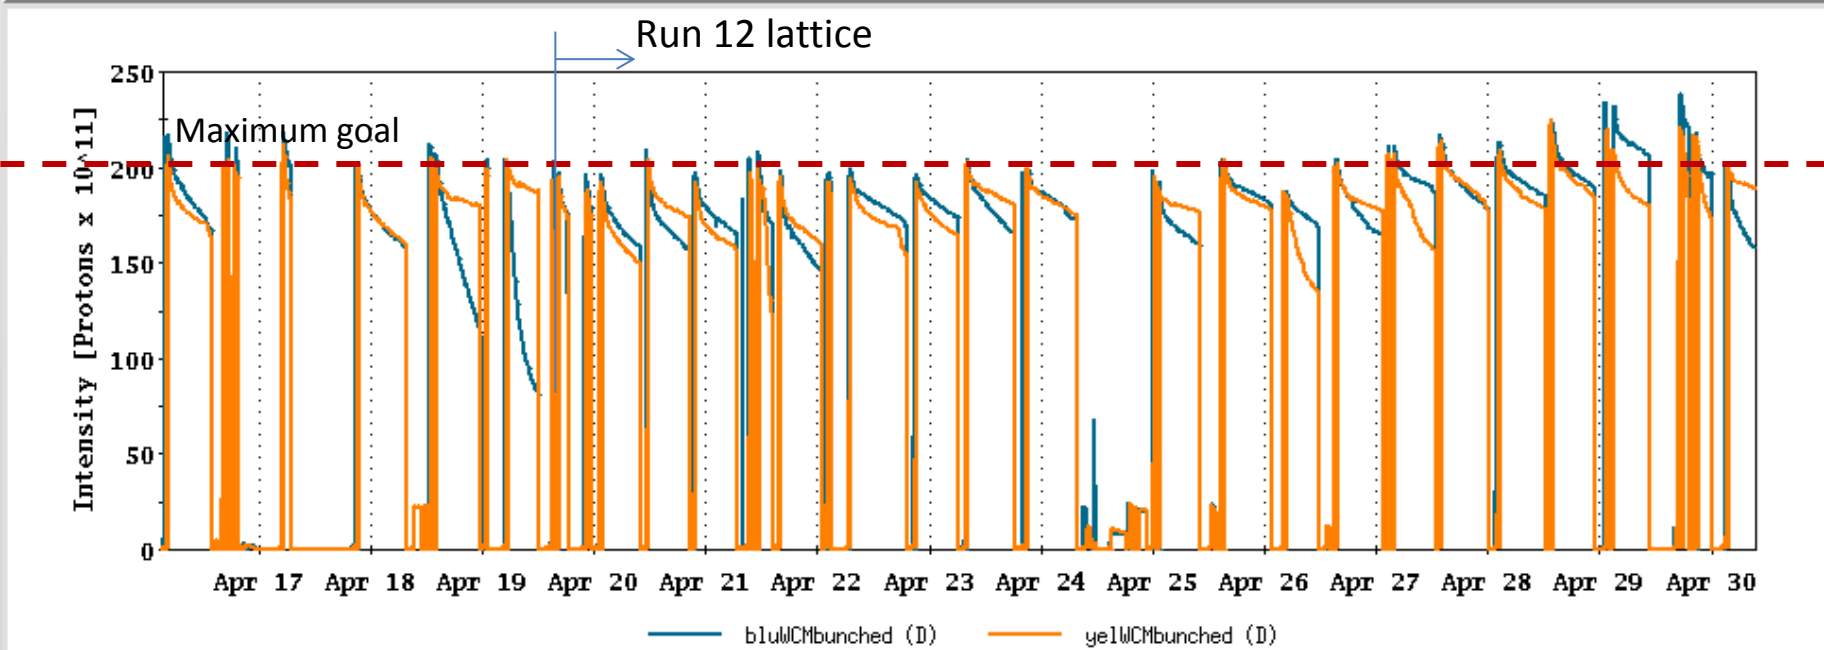

PREVIOUS RECORD

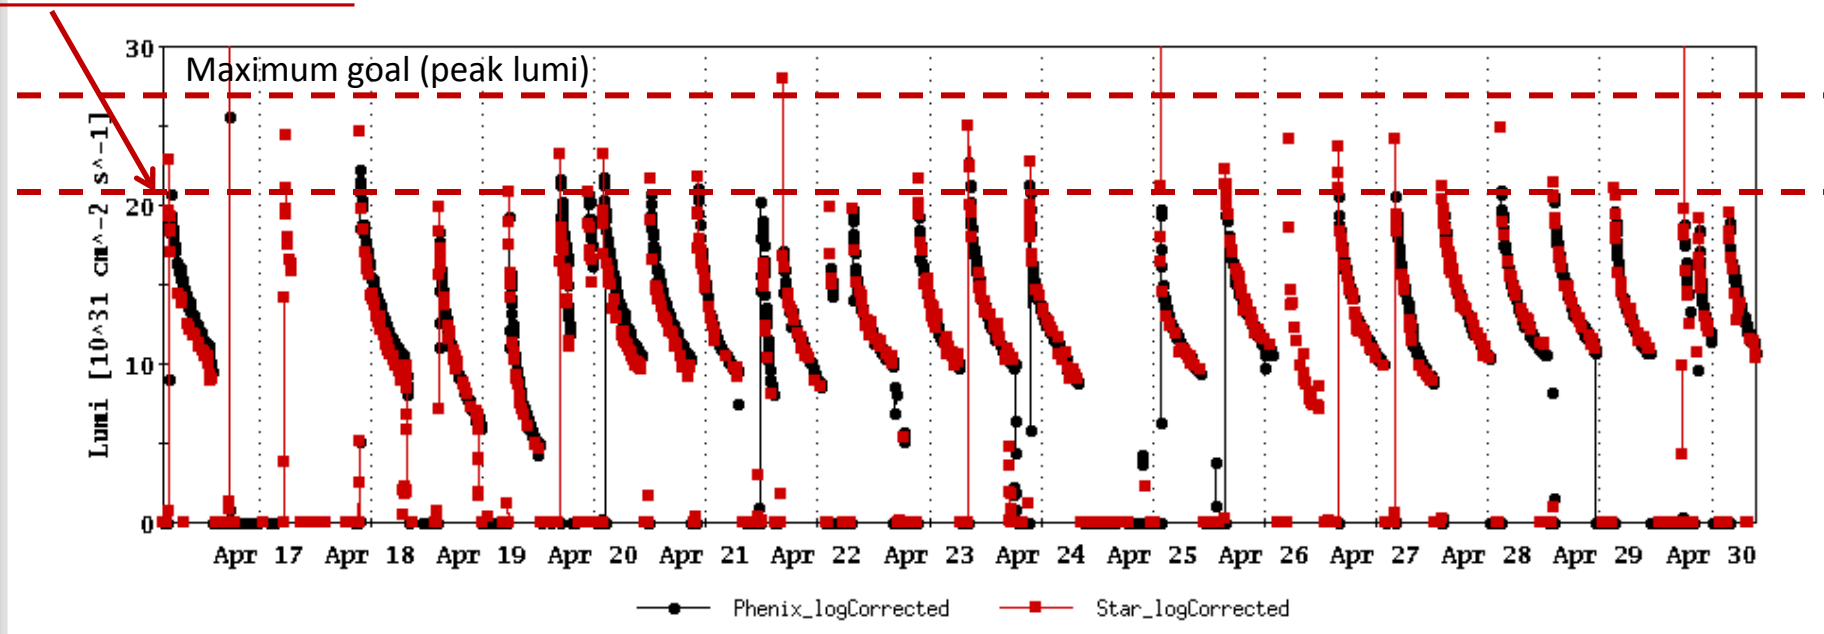


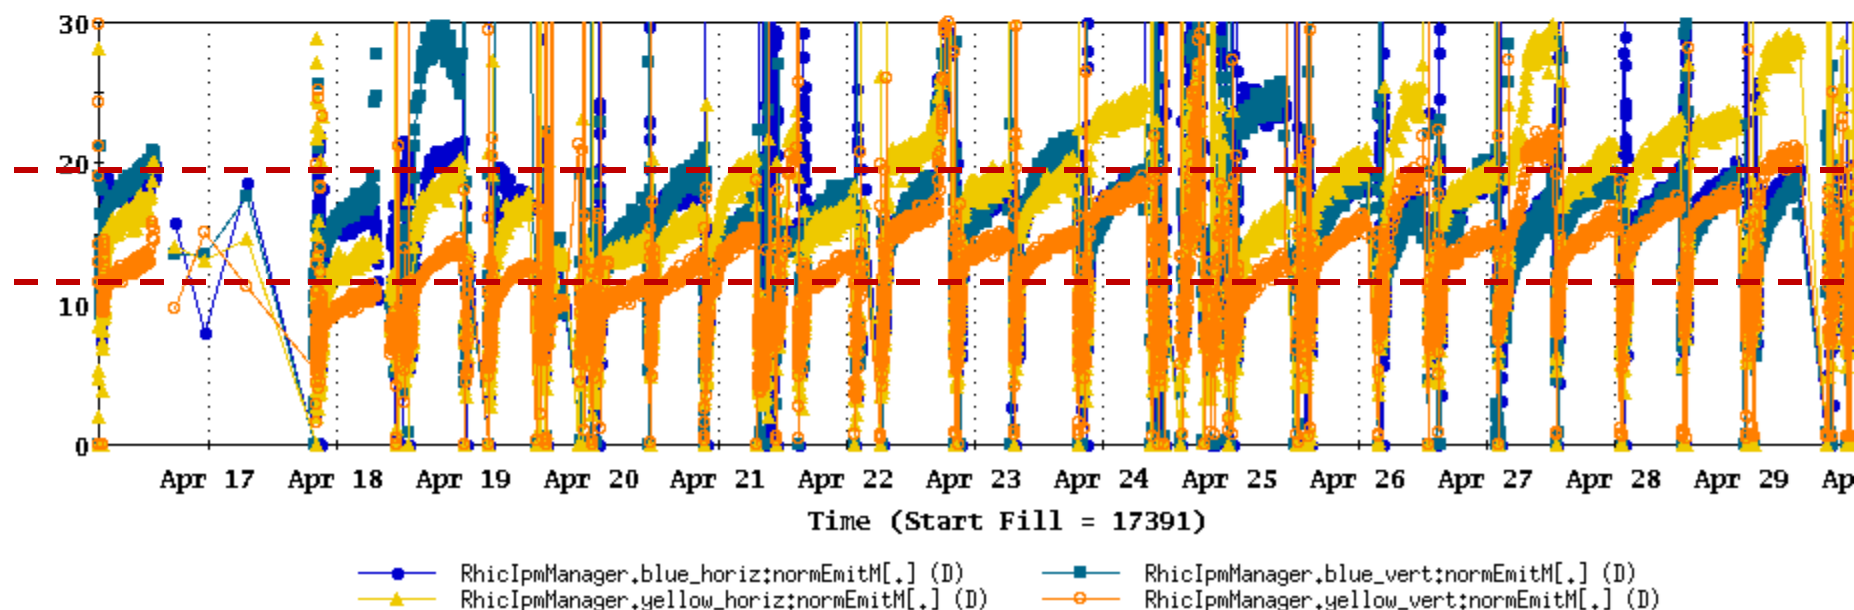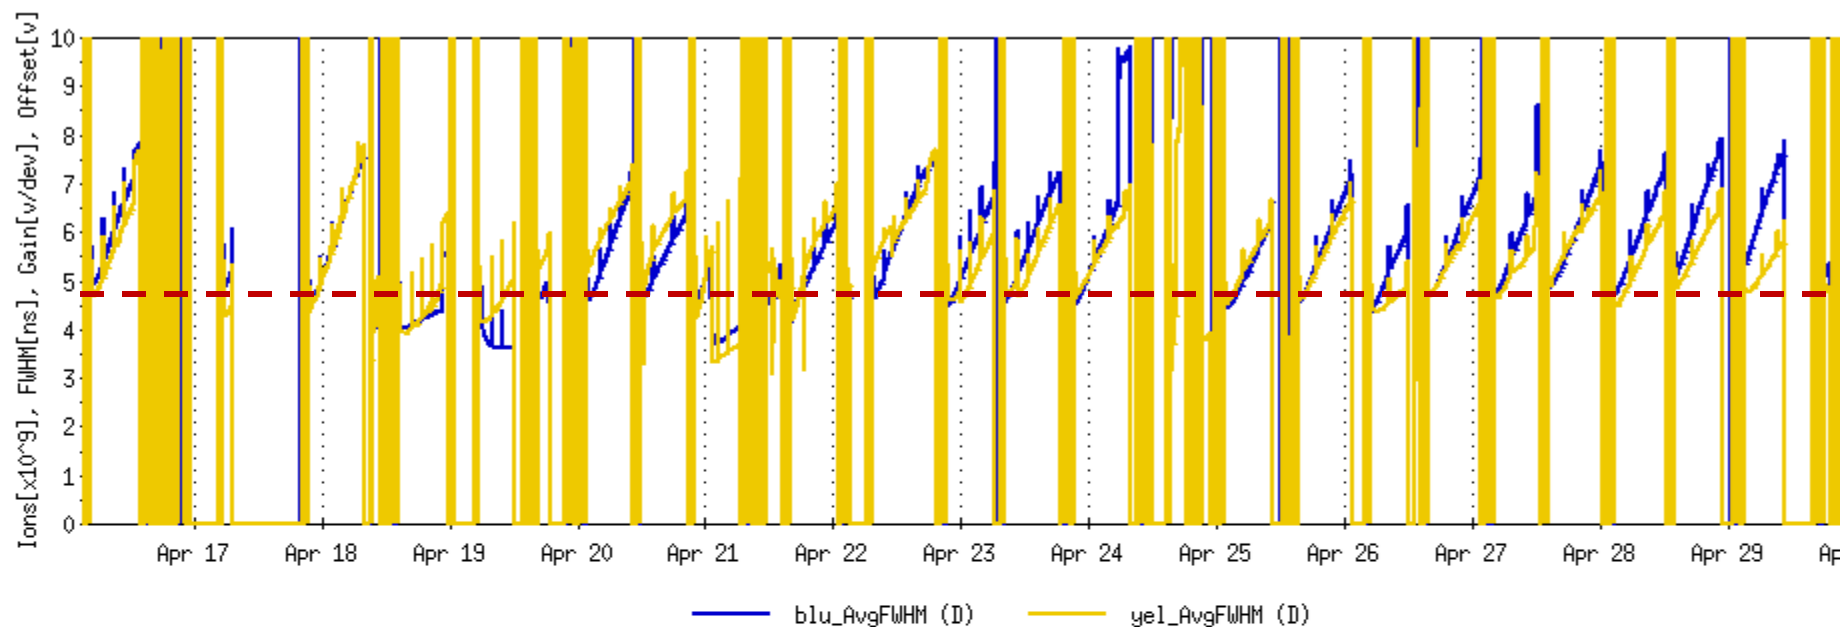

Preliminary, with Run 13 cross sections, PHENIX and STAR **log based singles correction**


PHENIX Goal, 250 pb⁻¹ recorded, 750 pb⁻¹ delivered, ≥ 55% polarization

STAR Goal, 165 pb⁻¹ recorded, 275 pb⁻¹ delivered, ≥ 55% polarization

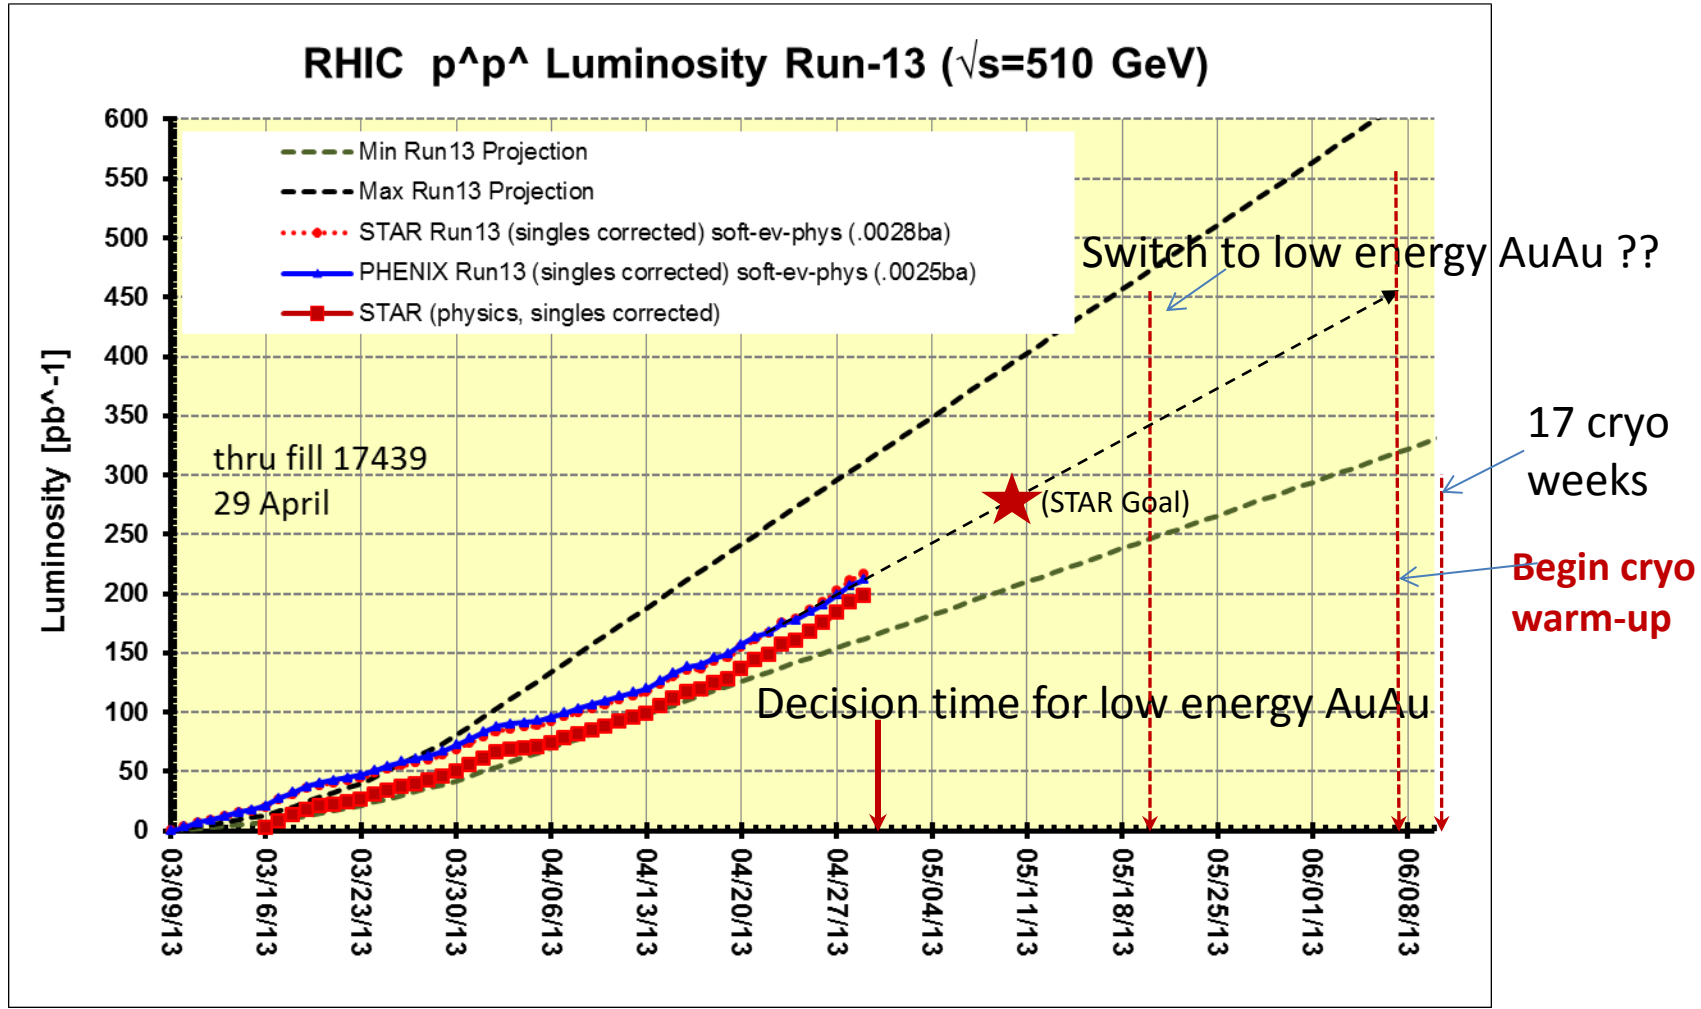


Preliminary, with Run 13 cross sections, singles corrected

Preliminary, with Run 13 cross sections, PHENIX and STAR log based singles correction

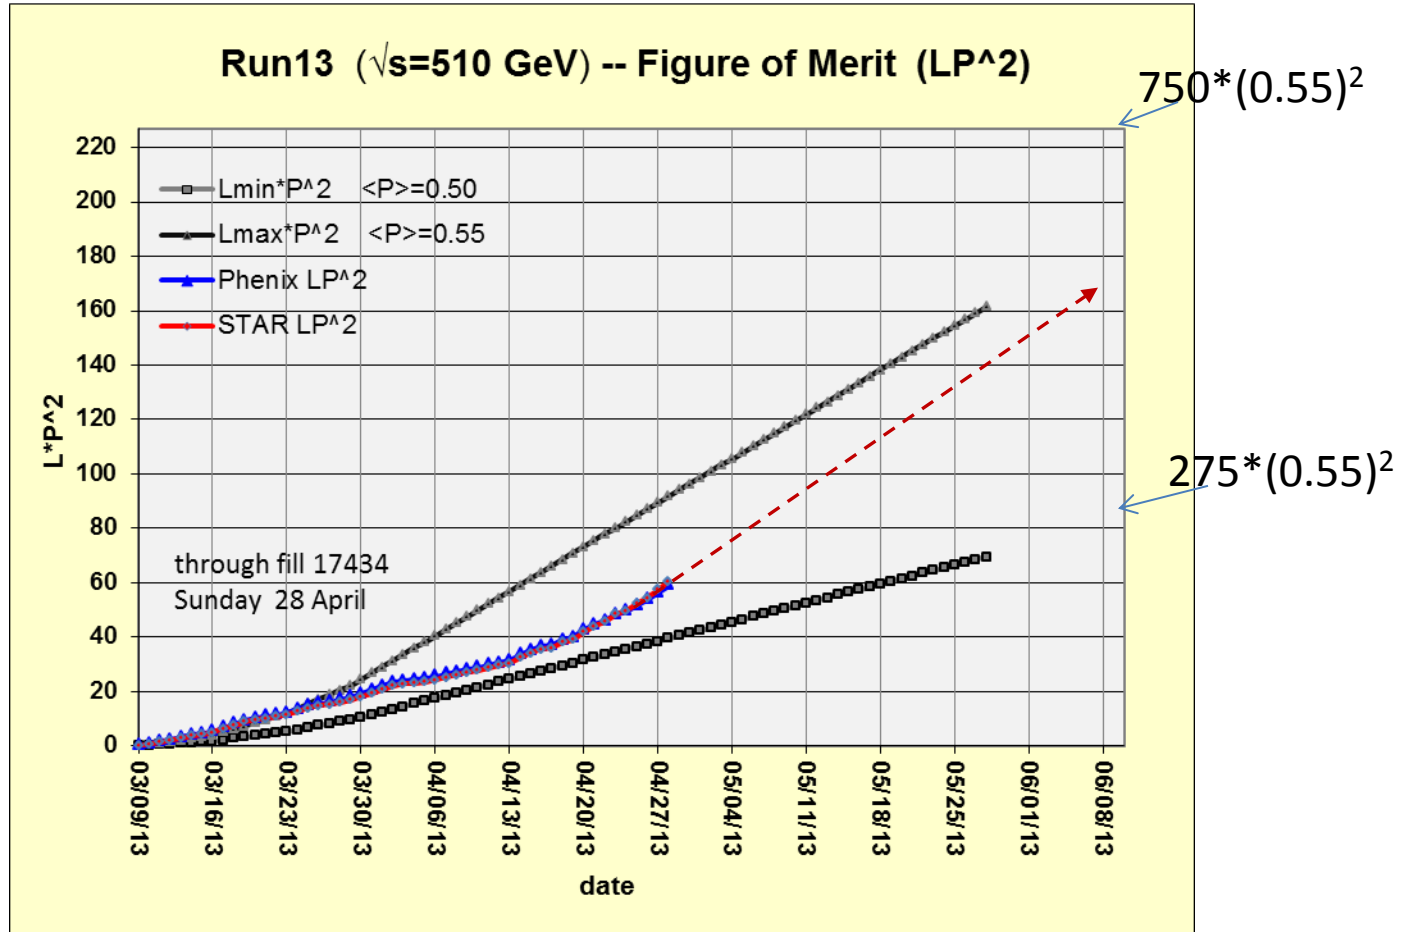

Using average polarizations from CNI polarization from <http://www.phy.bnl.gov/cnipol/fills/>

Preliminary, with Run 13 cross sections, PHENIX and STAR log based singles correction

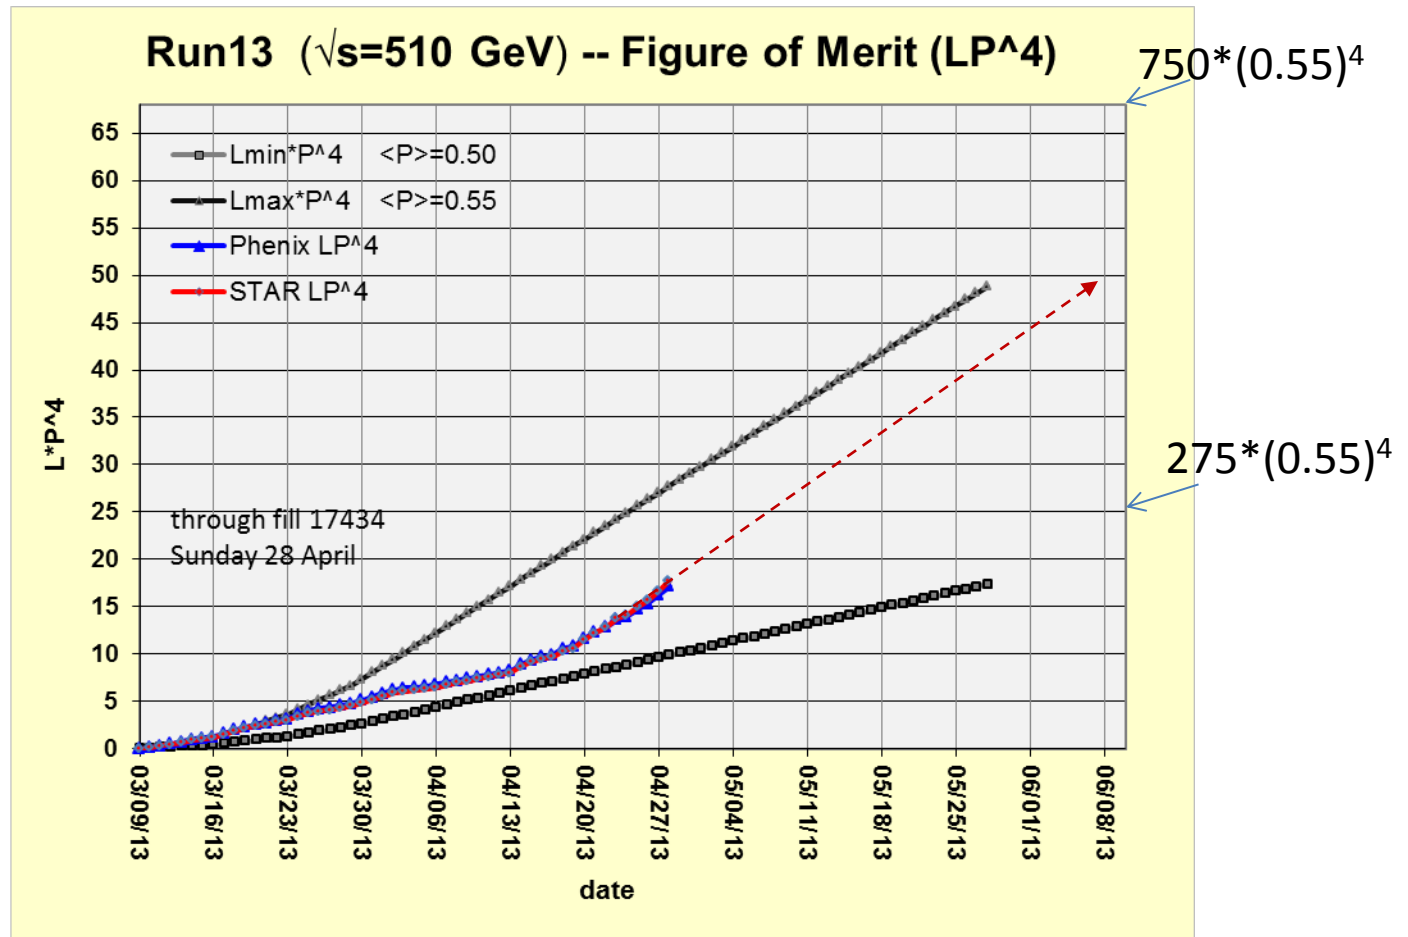

Using average polarizations from CNI polarization from <http://www.phy.bnl.gov/cnipol/fills/>

Yellow average = $44.3 \pm 0.8\%$

Blue average = $47.7 \pm 0.7\%$

Average = 46.0%


stores 17201-17322 (eLens lattice)

Yellow average = $54.7 \pm 0.6\%$

Blue average = $48.9 \pm 0.5\%$

Average = 51.8%


stores 17328 – 17439 (Run 12 lattice)

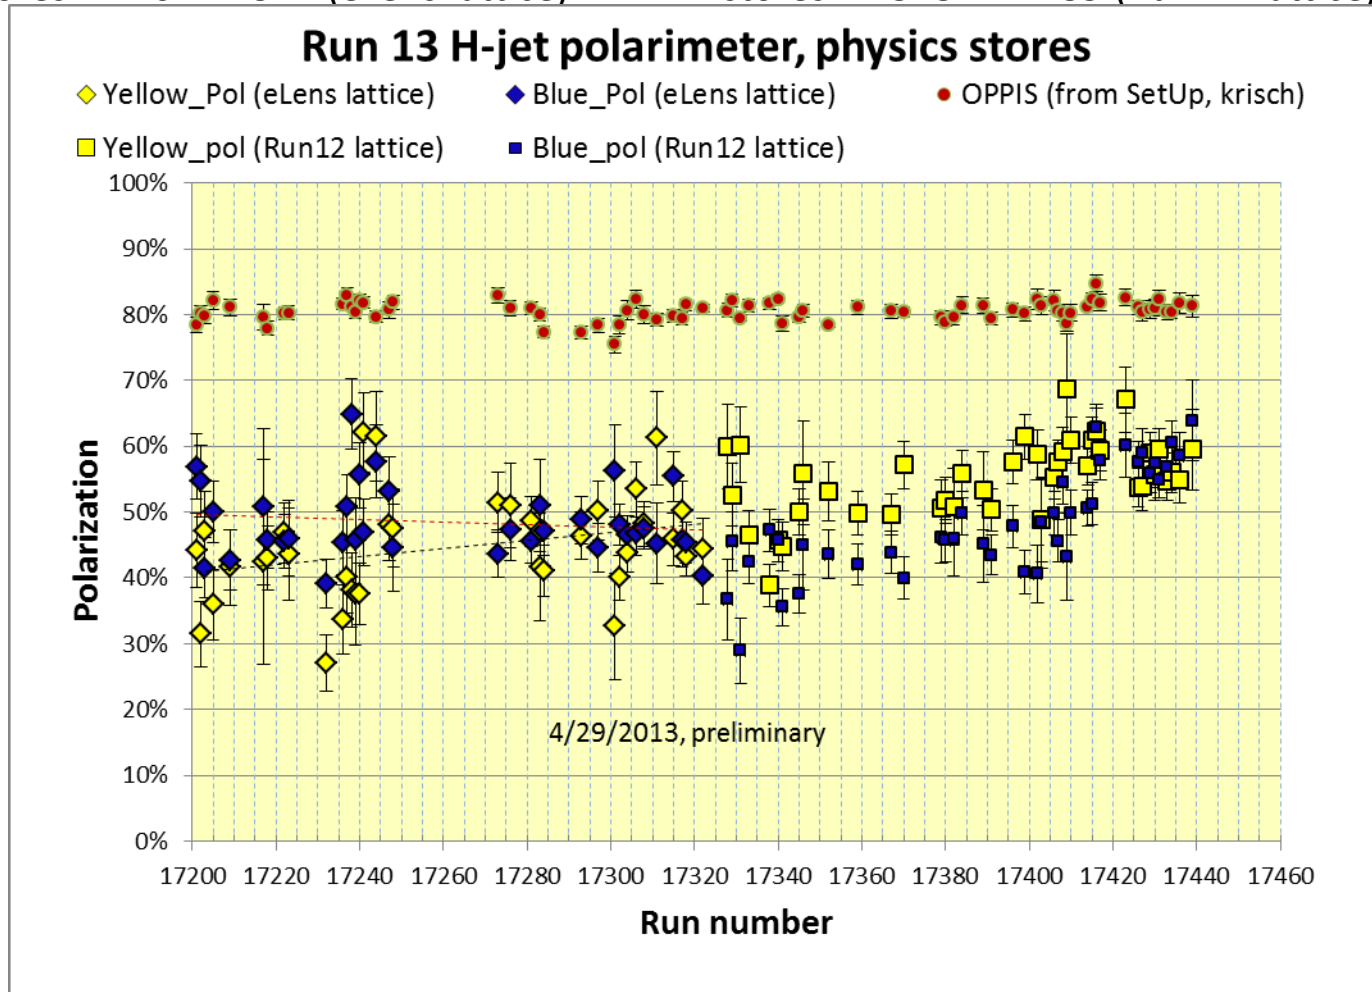

<https://wiki.bnl.gov/rhicspin/Polarimetry/H-jet/Run13>


Yellow average = $52.5 \pm 0.6\%$
Blue average = $53.4 \pm 0.7\%$
Average = 53.0%
stores 17201-17322 (eLens lattice)

Yellow average = $55.0 \pm 0.4\%$
Blue average = $54.3 \pm 0.5\%$
Average = 54.7%
stores 17328-17434 (Run 12 lattice)

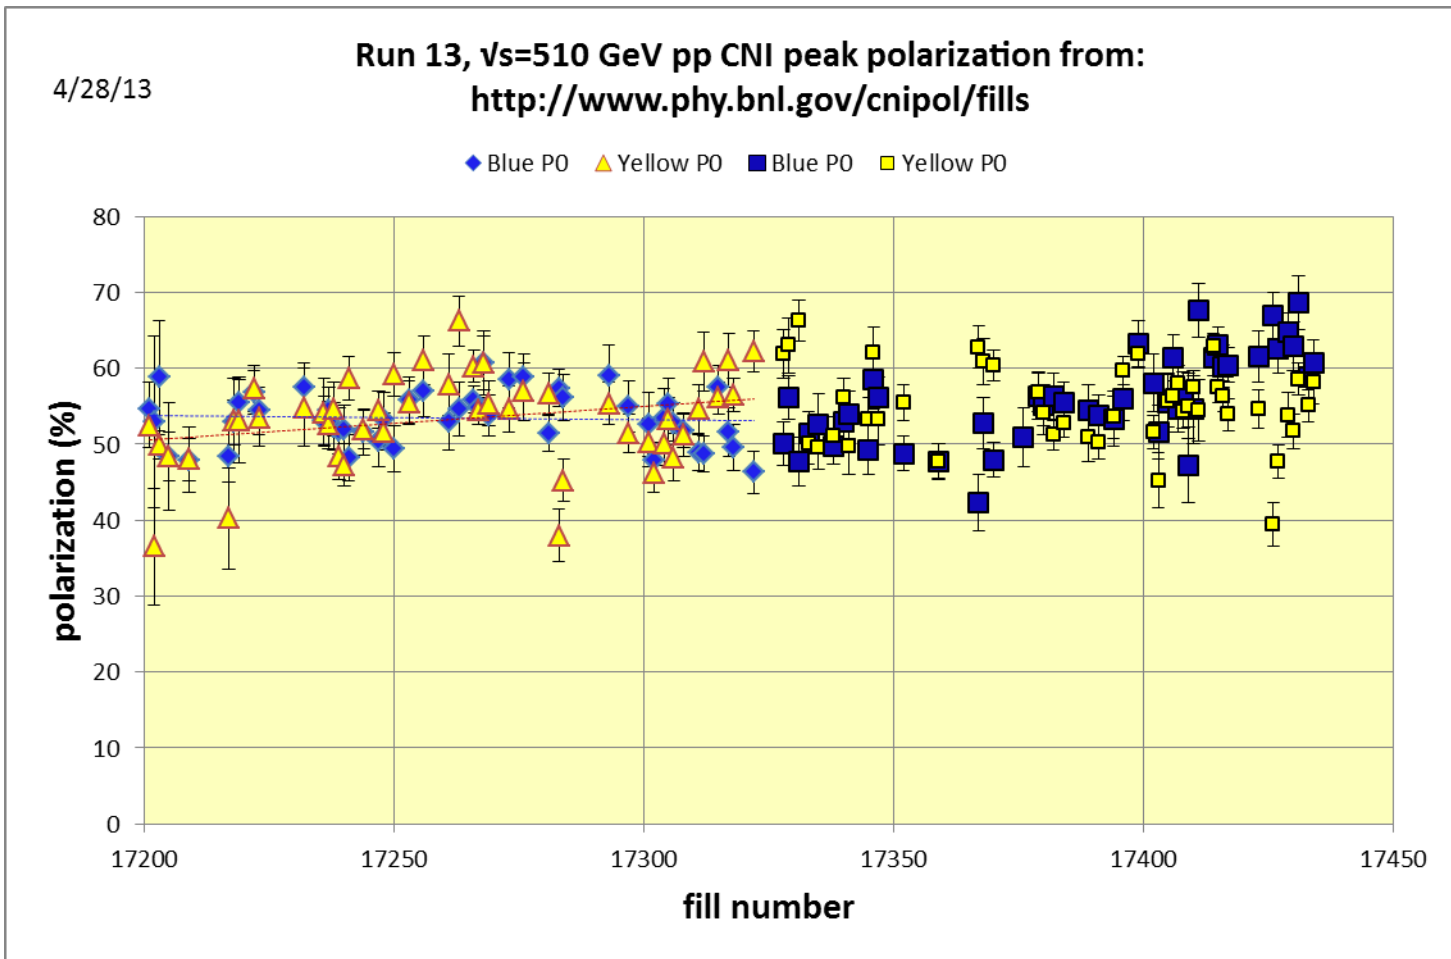


4/28/13

Run 13, $\sqrt{s}=510$ GeV pp CNI polarization loss at store, from: <http://www.phy.bnl.gov/cnipol/fills>

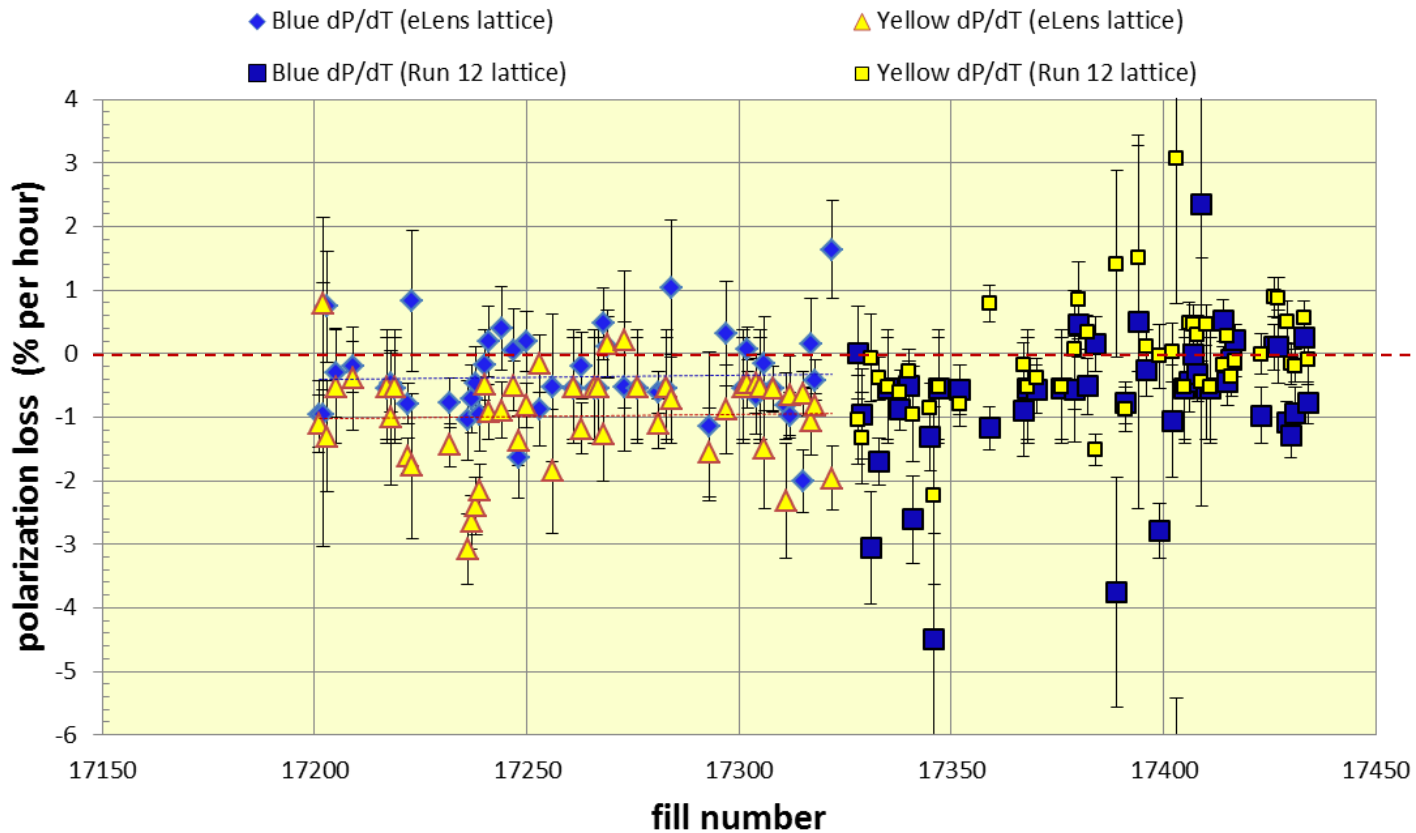

+\$1,086K in BNL bank through Mar 2013 (~\$450K should come back to CAD)

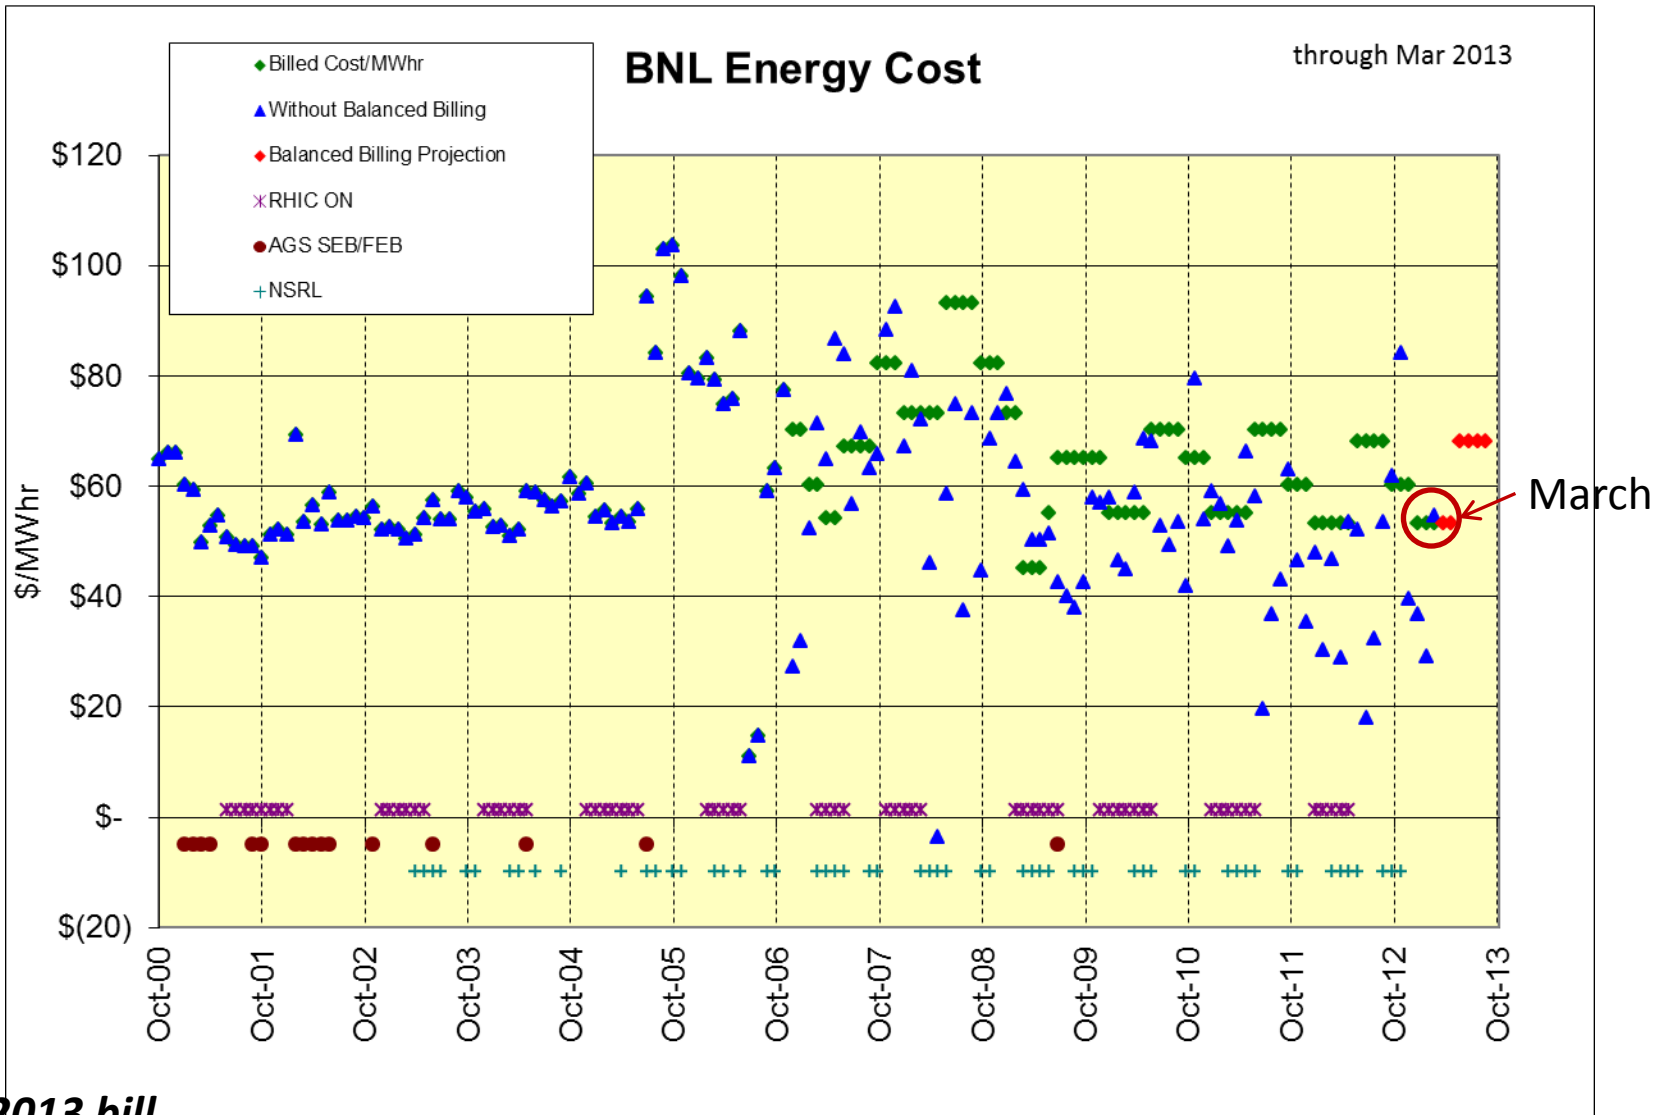


Mar 2013 bill



\$54.39 actual

billed at \$53/Mwhr



BNL Electricity Cost

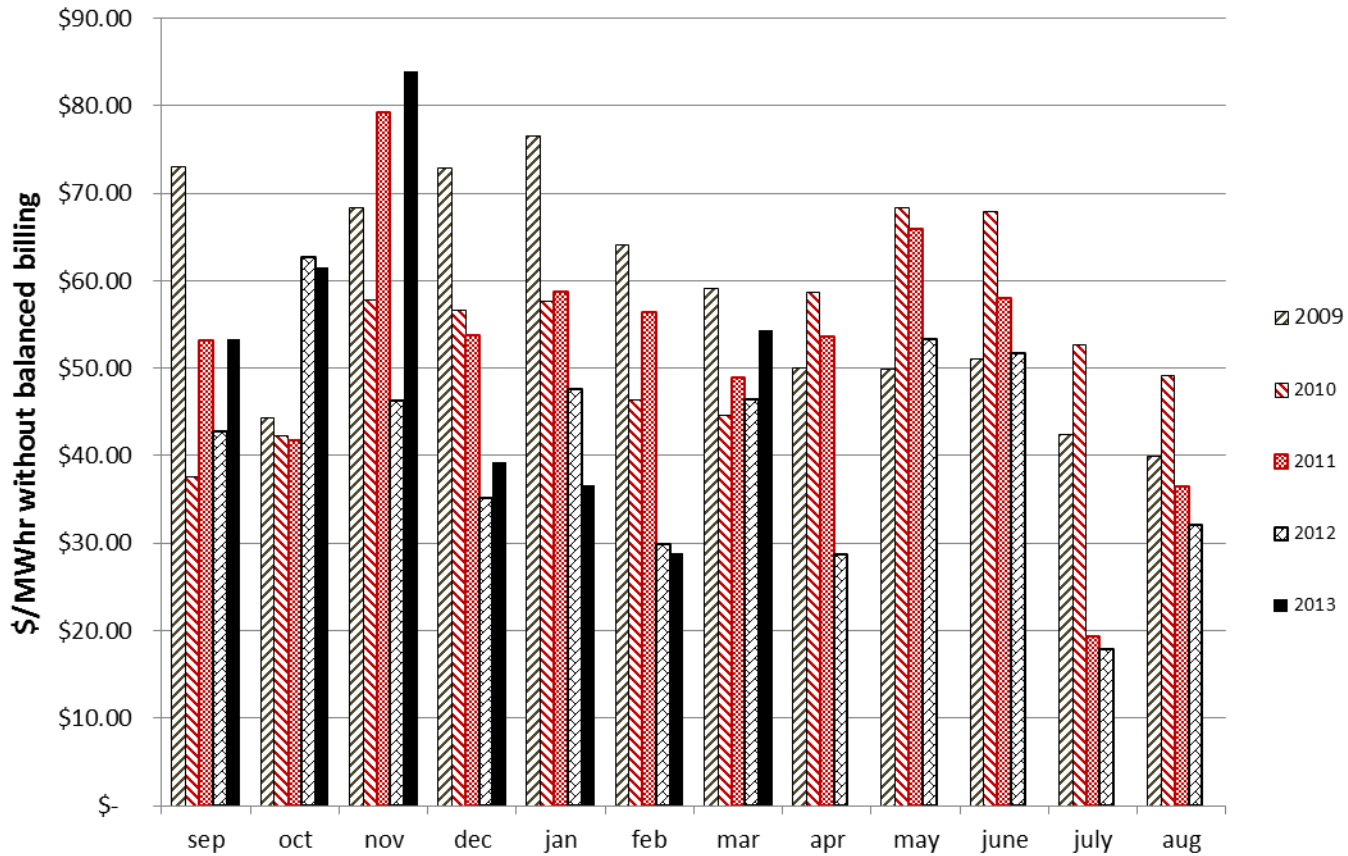

Additional Information

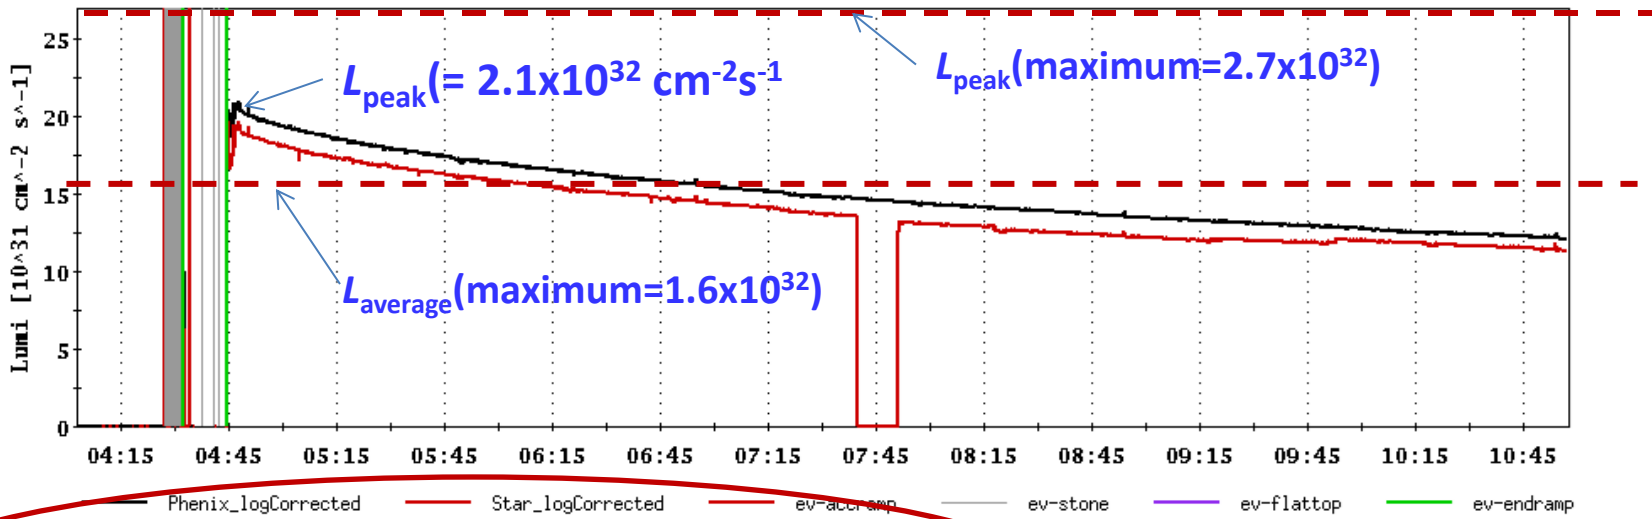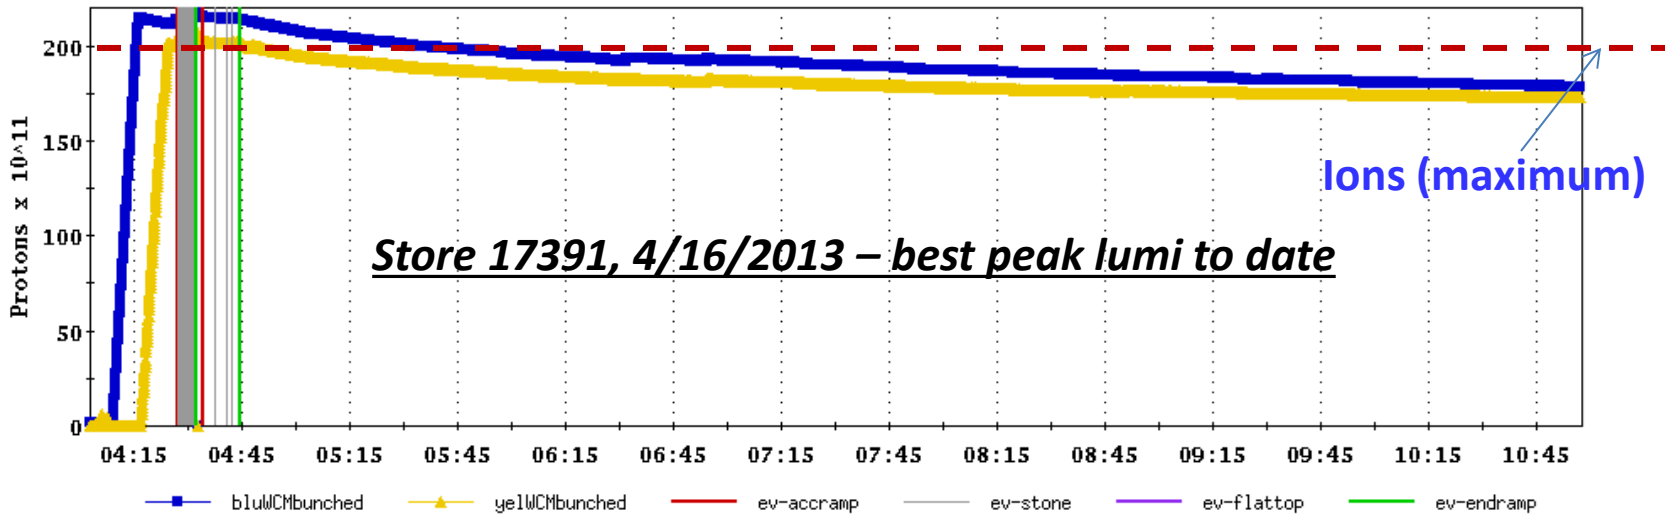

Time = Tue Apr 16 04:47:24 2013+0ms, bluWCMbunched = 212.643
 Time = Tue Apr 16 04:47:32 2013+0ms, yelWCMbunched = 200.528
 Time = Tue Apr 16 04:46:59 2013+5ms, Phenix_logCorrected = 20.7117

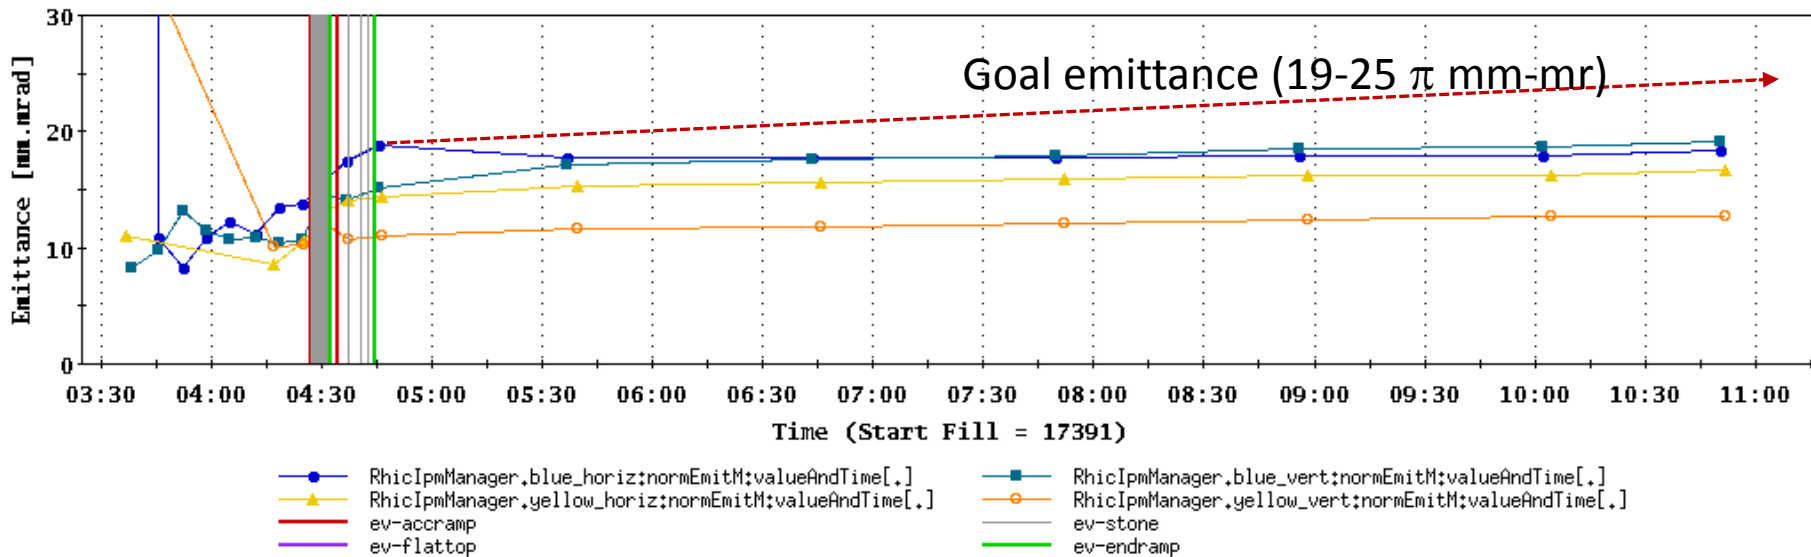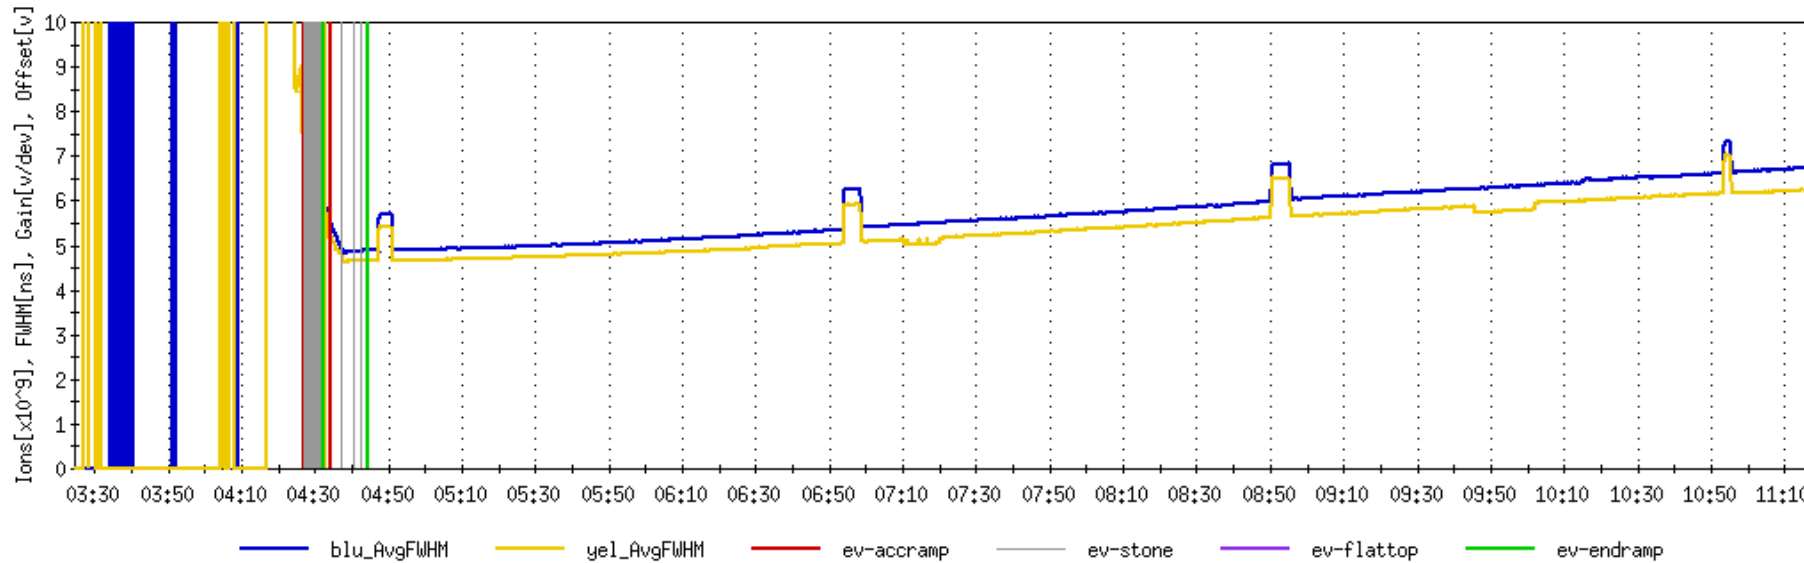

Run 13 plan based on 20 weeks cryo operation

and Fischer et.al. RHIC Collider Projections (FY 2013 – FY 2017), 27 Sep 2012


- ✓ 11 Feb, Begin cool-down to 4.5K
- ✓ 15 Feb, Cool-down to 4.5K in Blue and Yellow Ring complete, begin magnet setup
- ✓ 26 Feb, first collisions
- ✓ 15 Feb -1 Mar, RHIC $\sqrt{s} = 510$ GeV pp machine setup
- ✓ 1-8 Mar, machine ramp-up with 8 hr/night for experiment setup
- ✓ 9 Mar (store 17201), begin $\sqrt{s} = 510$ GeV pp physics run

today, 23 Apr...

- 27 May, end 15 cryo weeks
- 6 Jun, switch to $\sqrt{s} = 15$ GeV/n AuAu if pp goals are met and end 12.7 week $\sqrt{s} = 510$ GeV pp physics run
- 27 Jun, end ~ 2.5 week $\sqrt{s} = 15$ GeV/n AuAu physics run or 15.9 week $\sqrt{s} = 510$ GeV pp physics run, begin cryo warm-up
- 30 June, cryo warm-up \sim complete (19.9 cryo-weeks)

See <http://www.rhichome.bnl.gov/AP/Spin2013/> for the Run Coordinator's detailed plan


Preliminary, with Run 13 cross sections, PHENIX and STAR **log based singles correction**

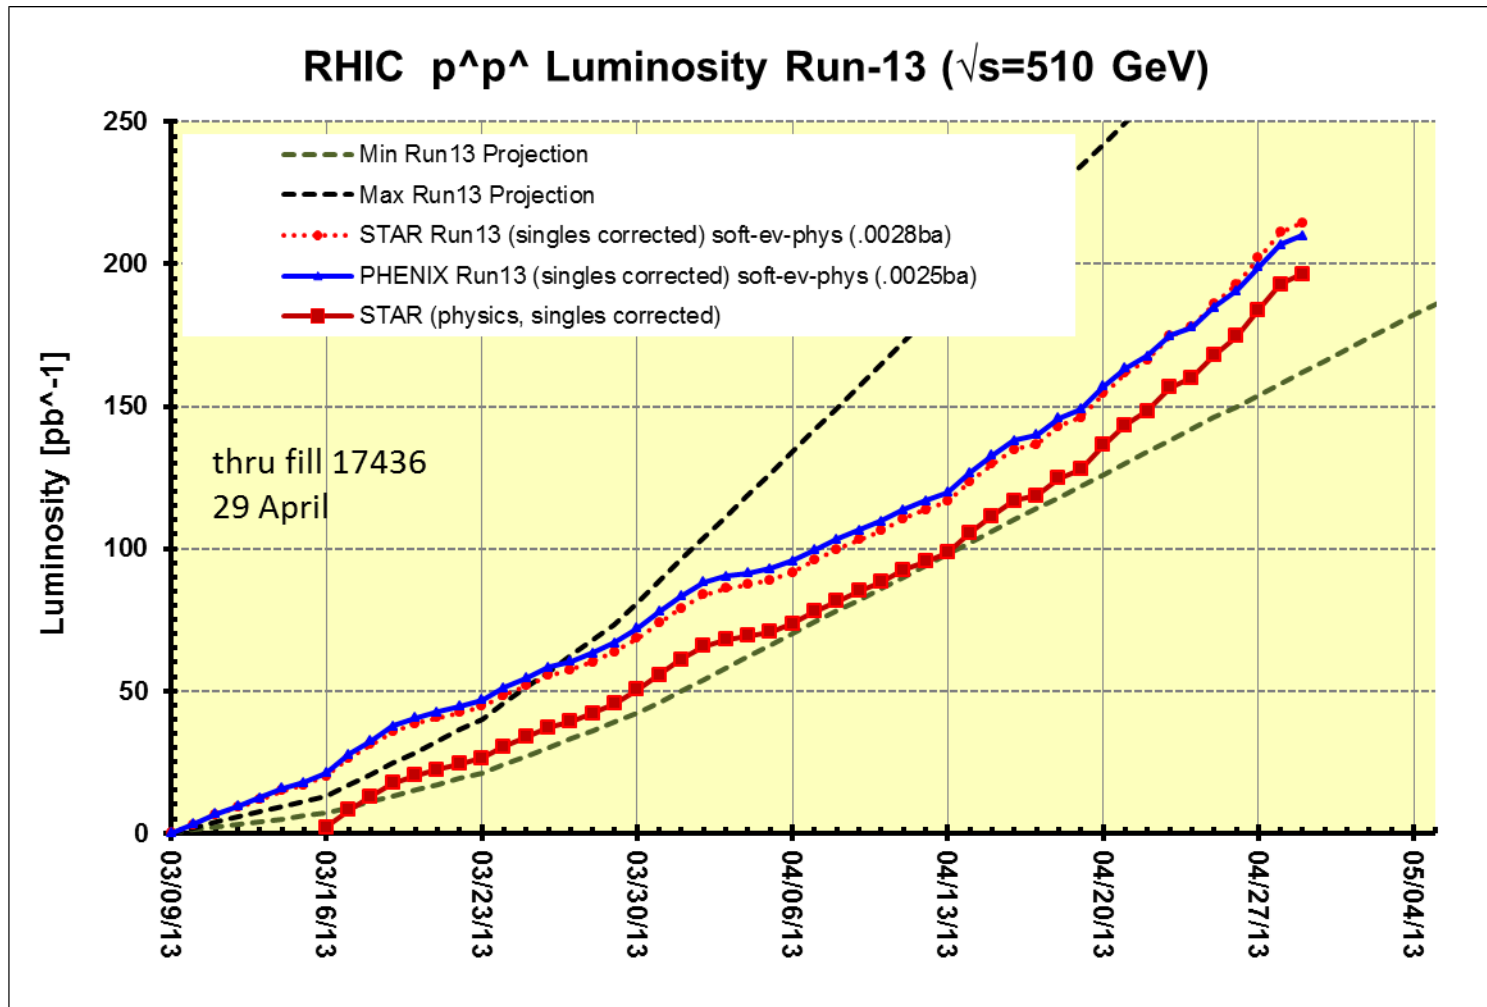

Preliminary, with Run 13 cross sections, PHENIX and STAR **log based singles correction**


PHENIX Goal, 250 pb⁻¹ recorded, 750 pb⁻¹ delivered, ≥ 55% polarization

STAR Goal, 165 pb⁻¹ recorded, 275 pb⁻¹ delivered, ≥ 55% polarization

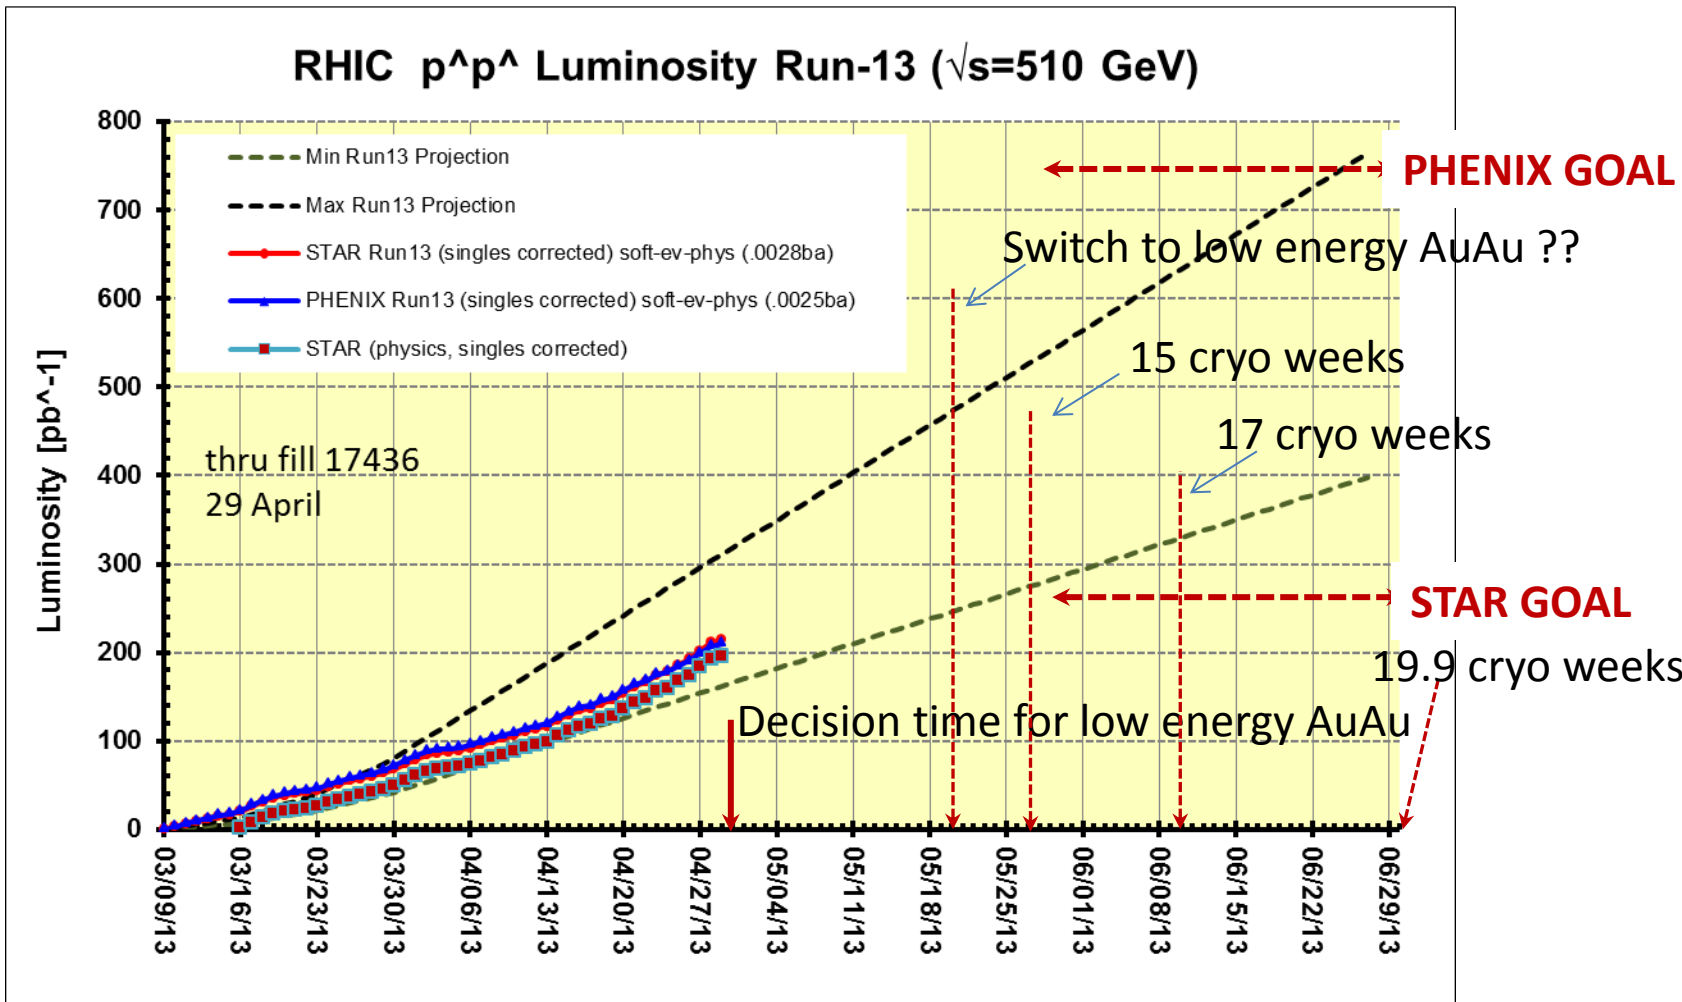


Preliminary, with Run 13 cross sections, singles corrected


Example Store for STAR (17340) with "physics" time cuts

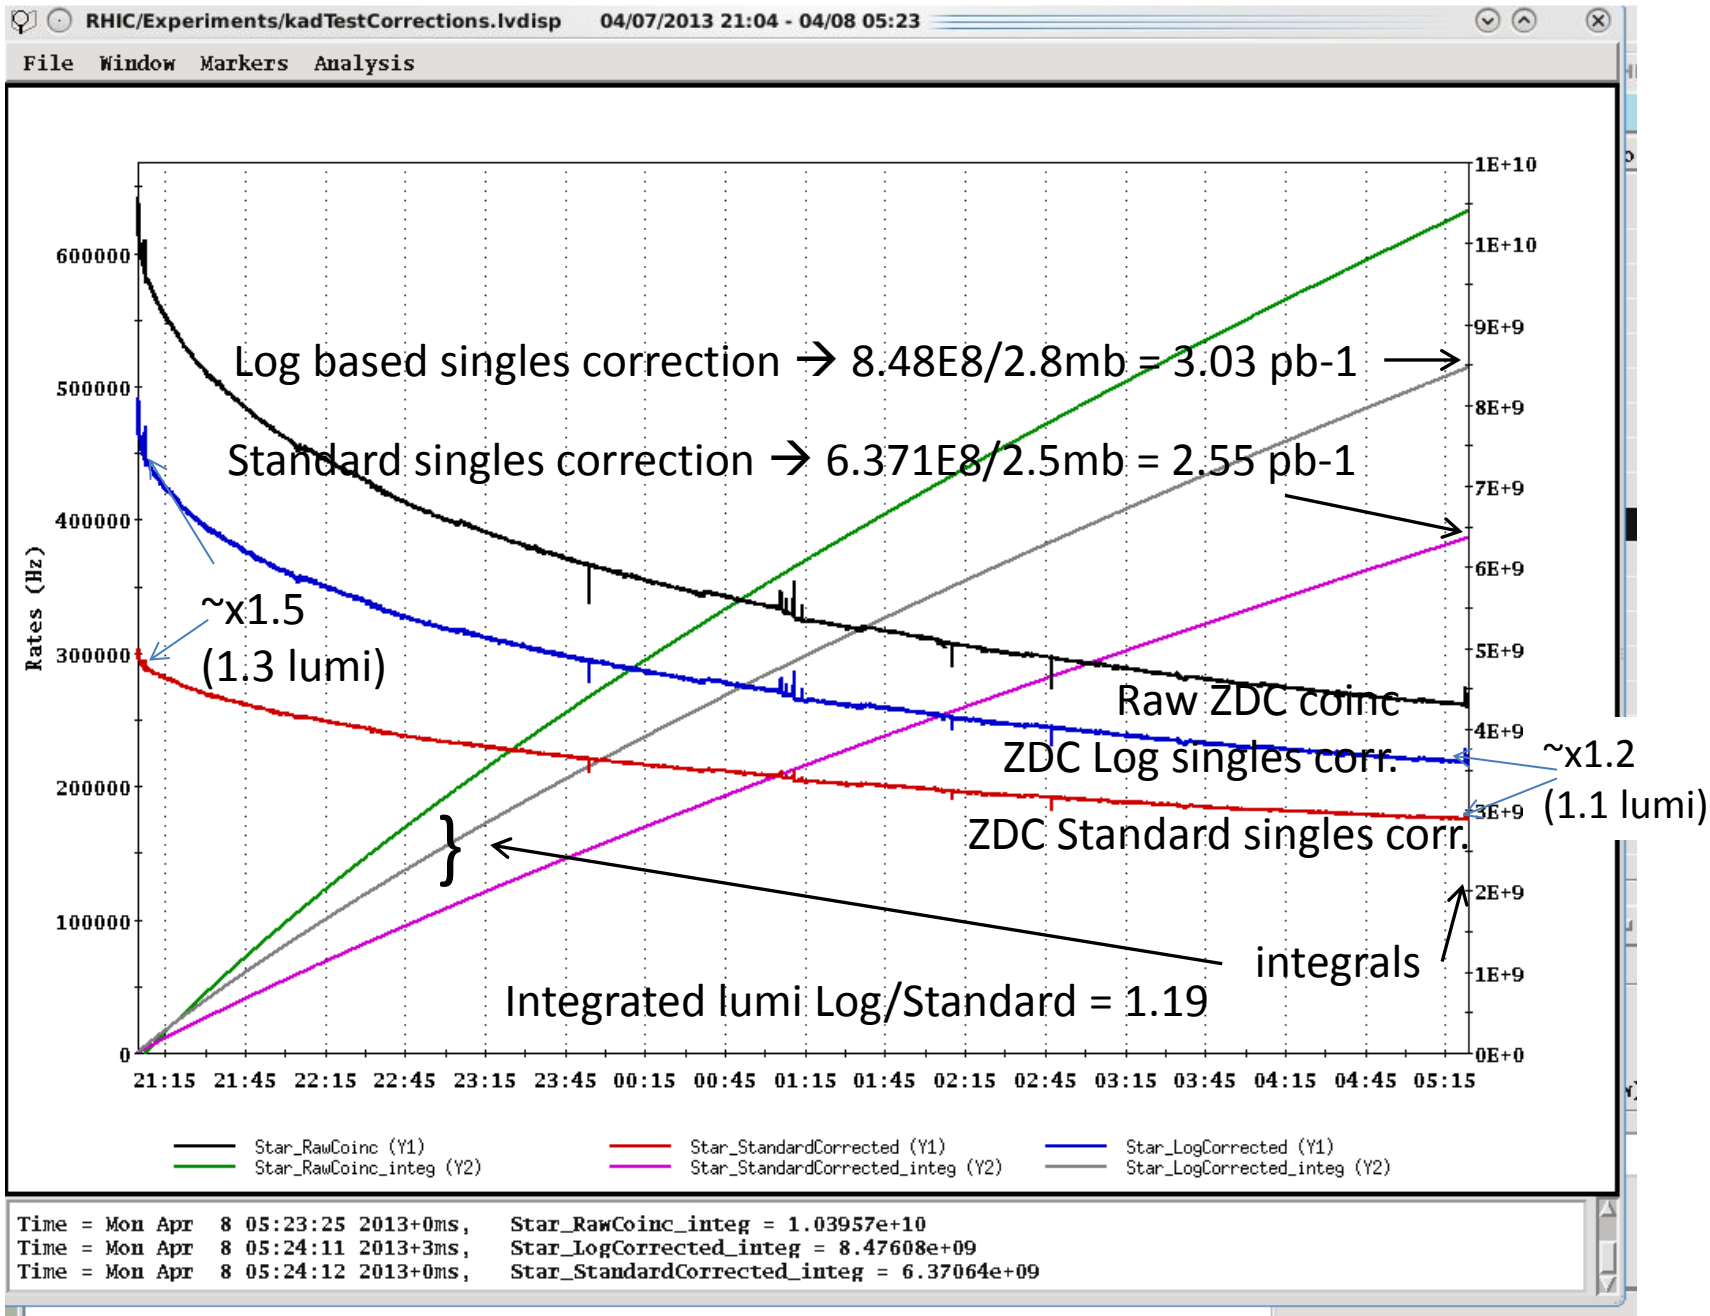



Physics stores

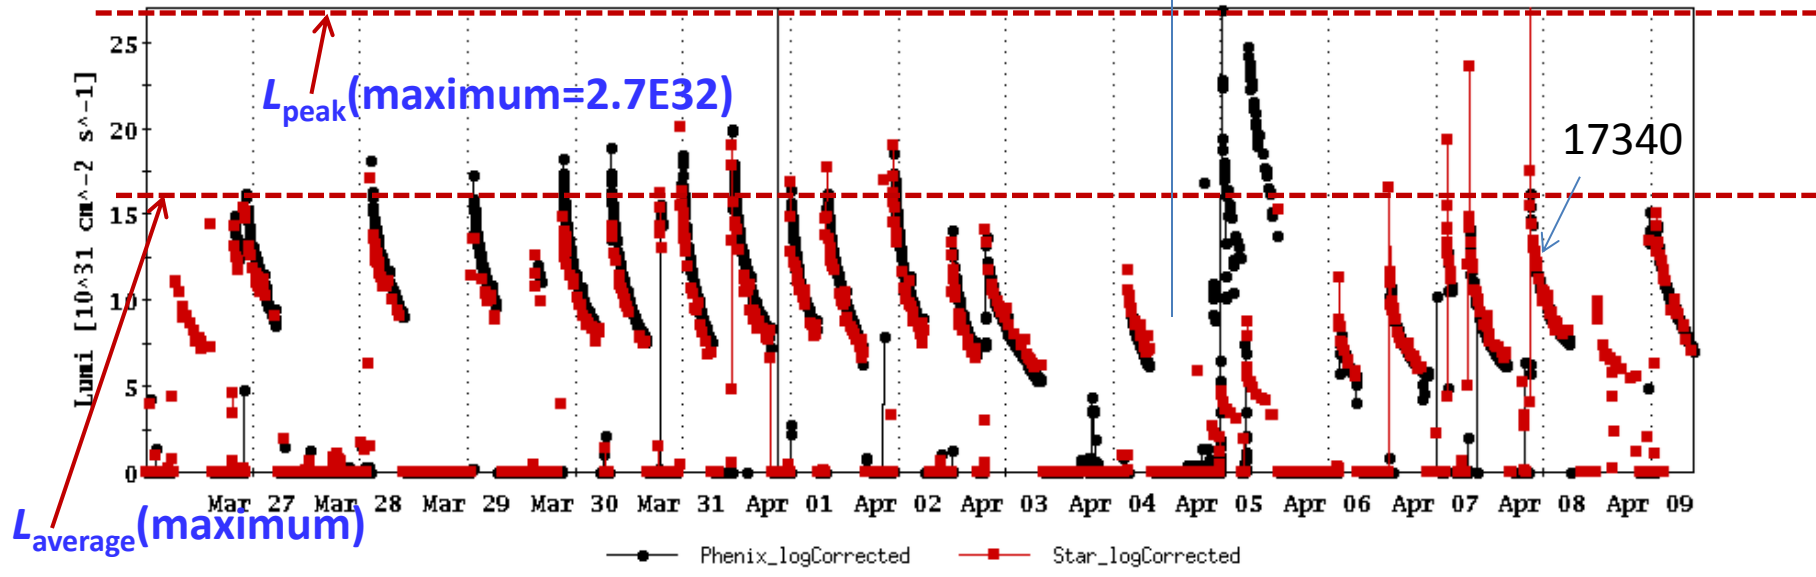

Using Run 13 cross sections with log based singles correction

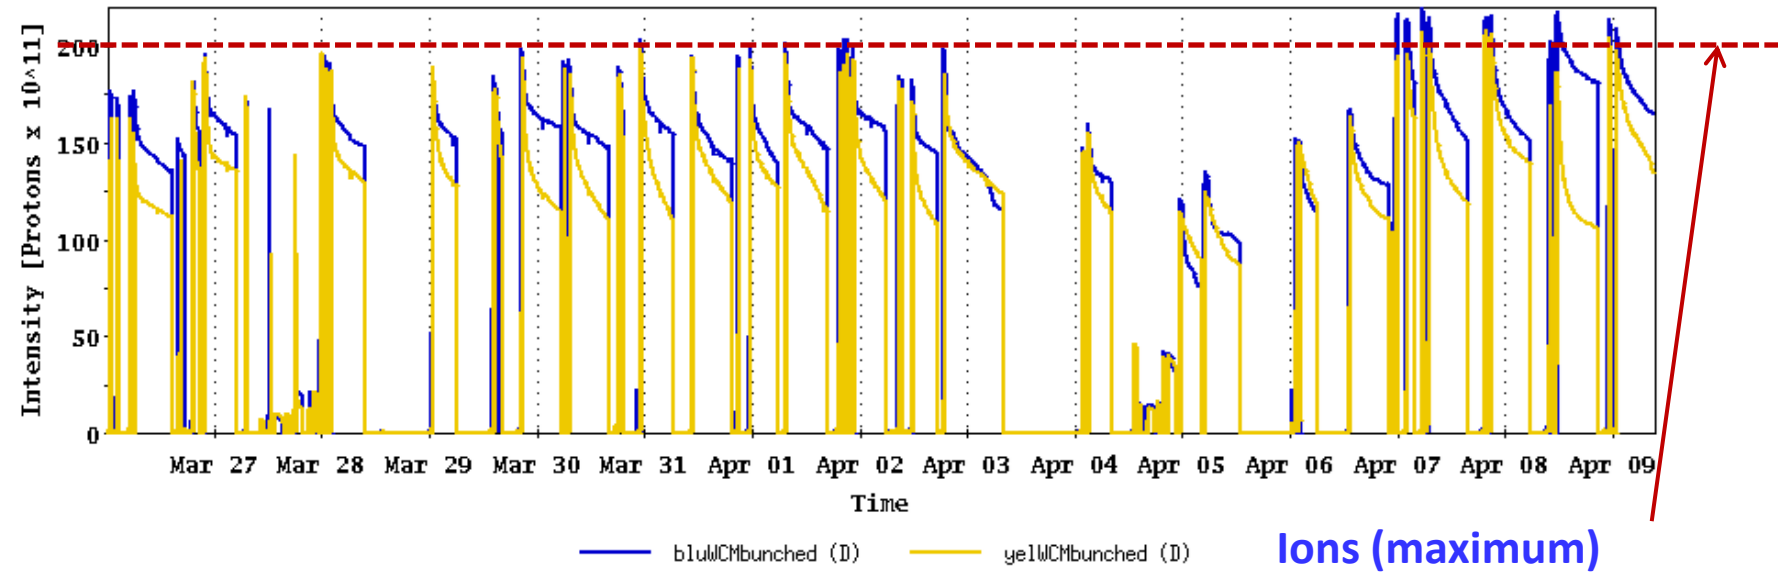


Past 2 Weeks

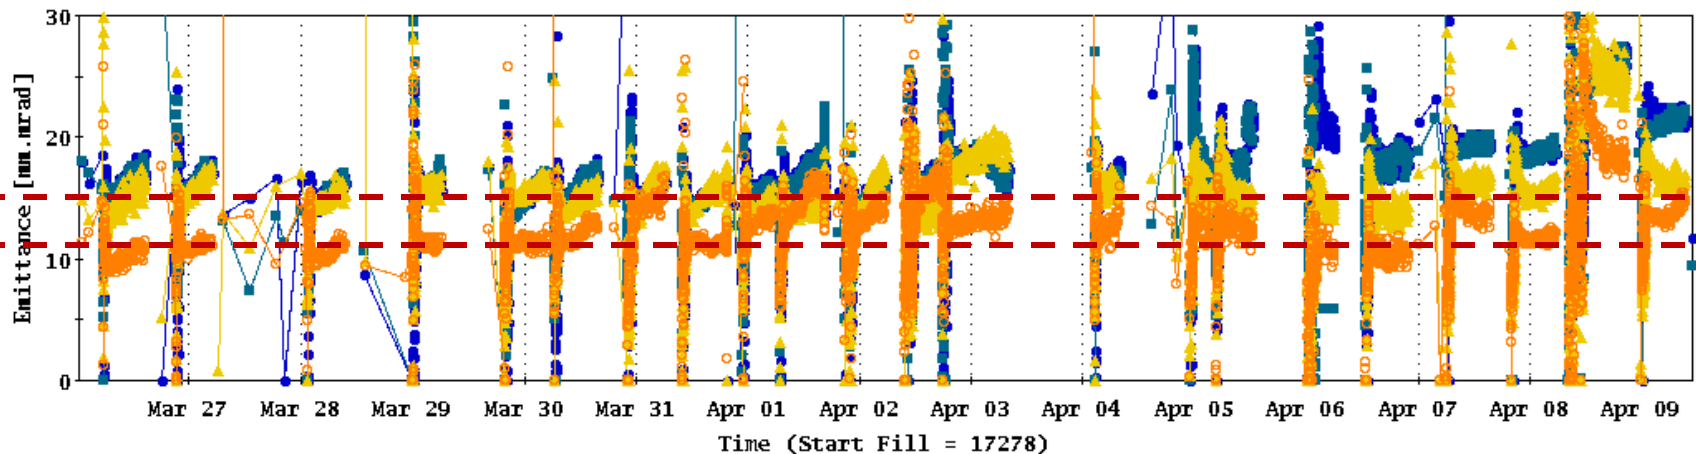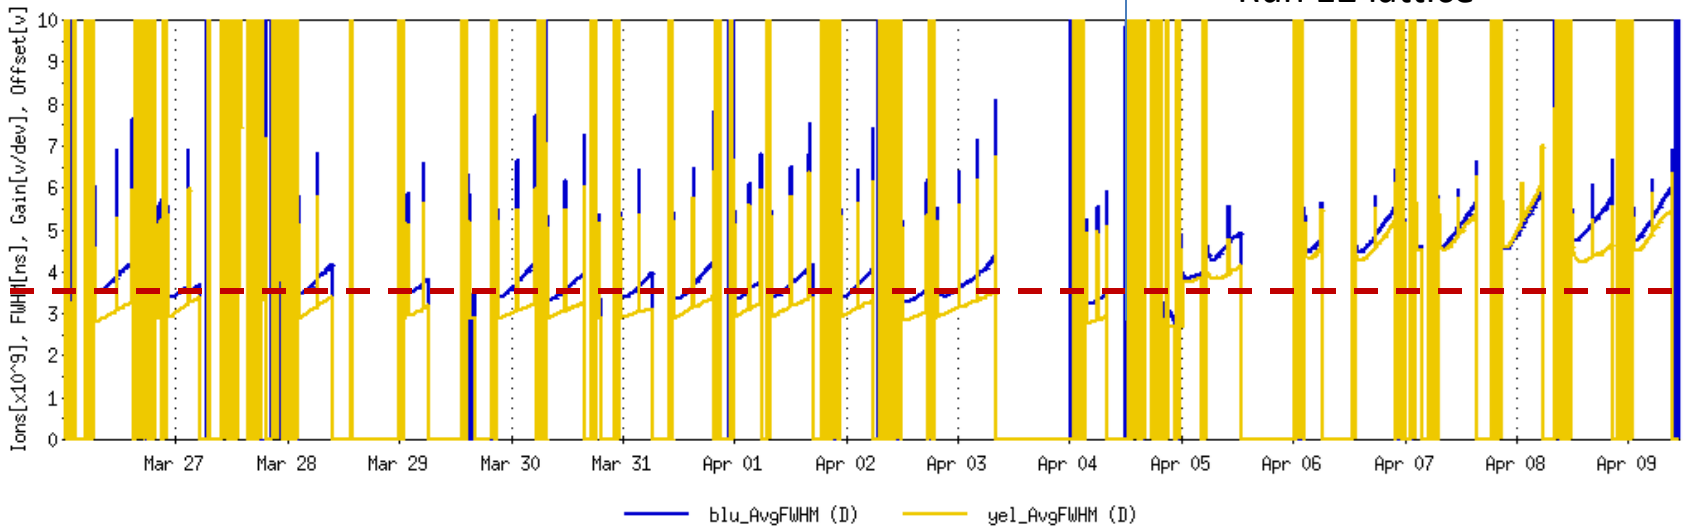

Yellow average = $48.12 \pm 0.4\%$

Blue average = $53.1 \pm 0.5\%$

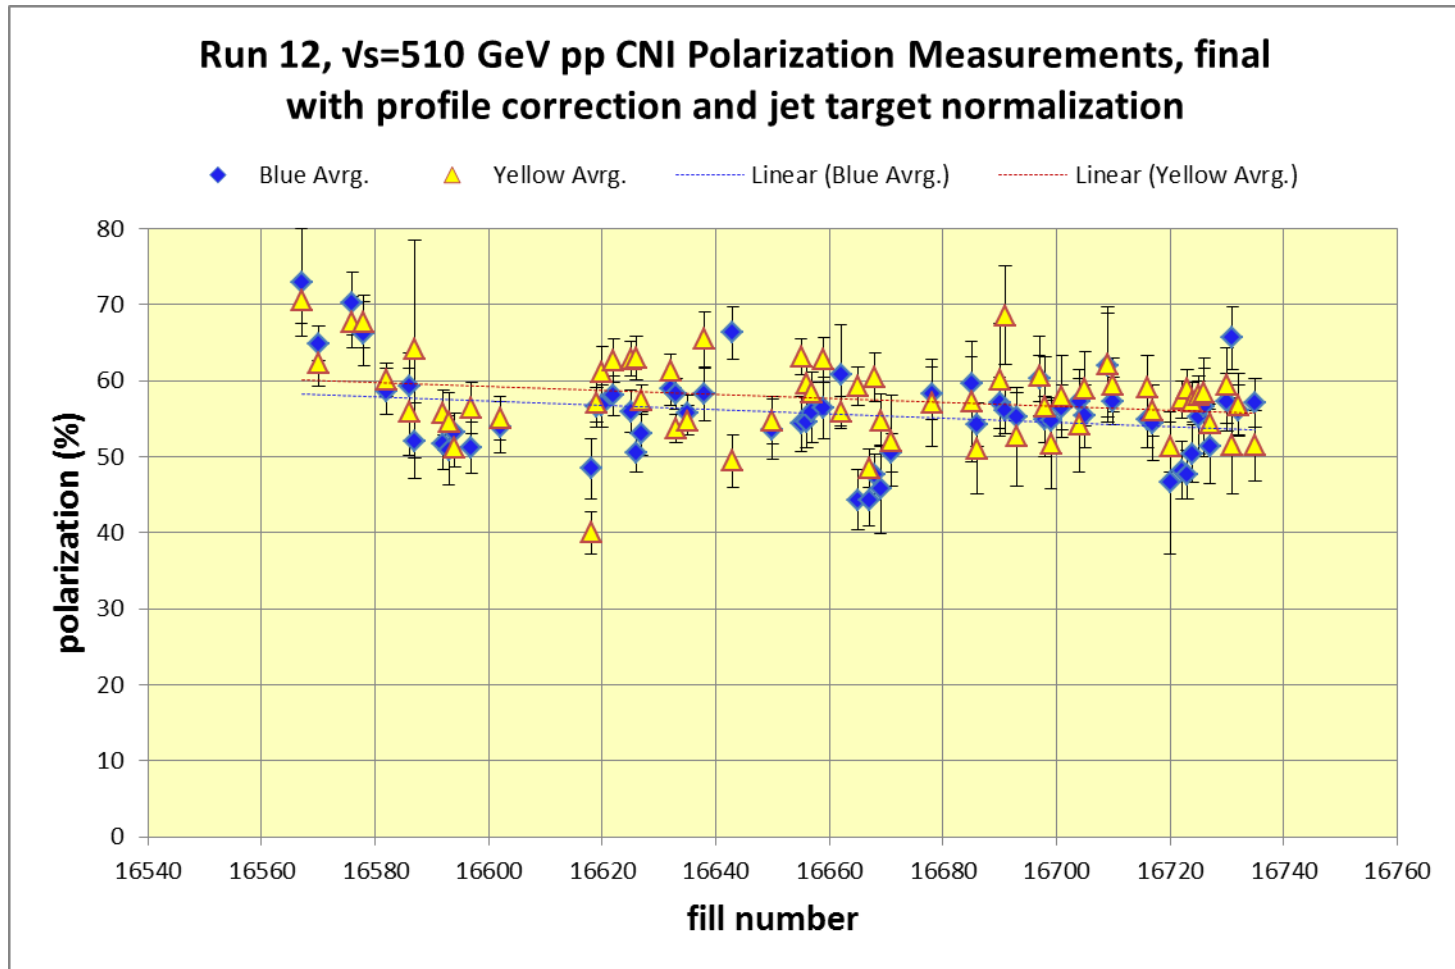


<http://www.phy.bnl.gov/cnipol/fills/>

Yellow average = $57.7 \pm 0.4\%$


Blue average = $55.9 \pm 0.4\%$

Average = 56.8%

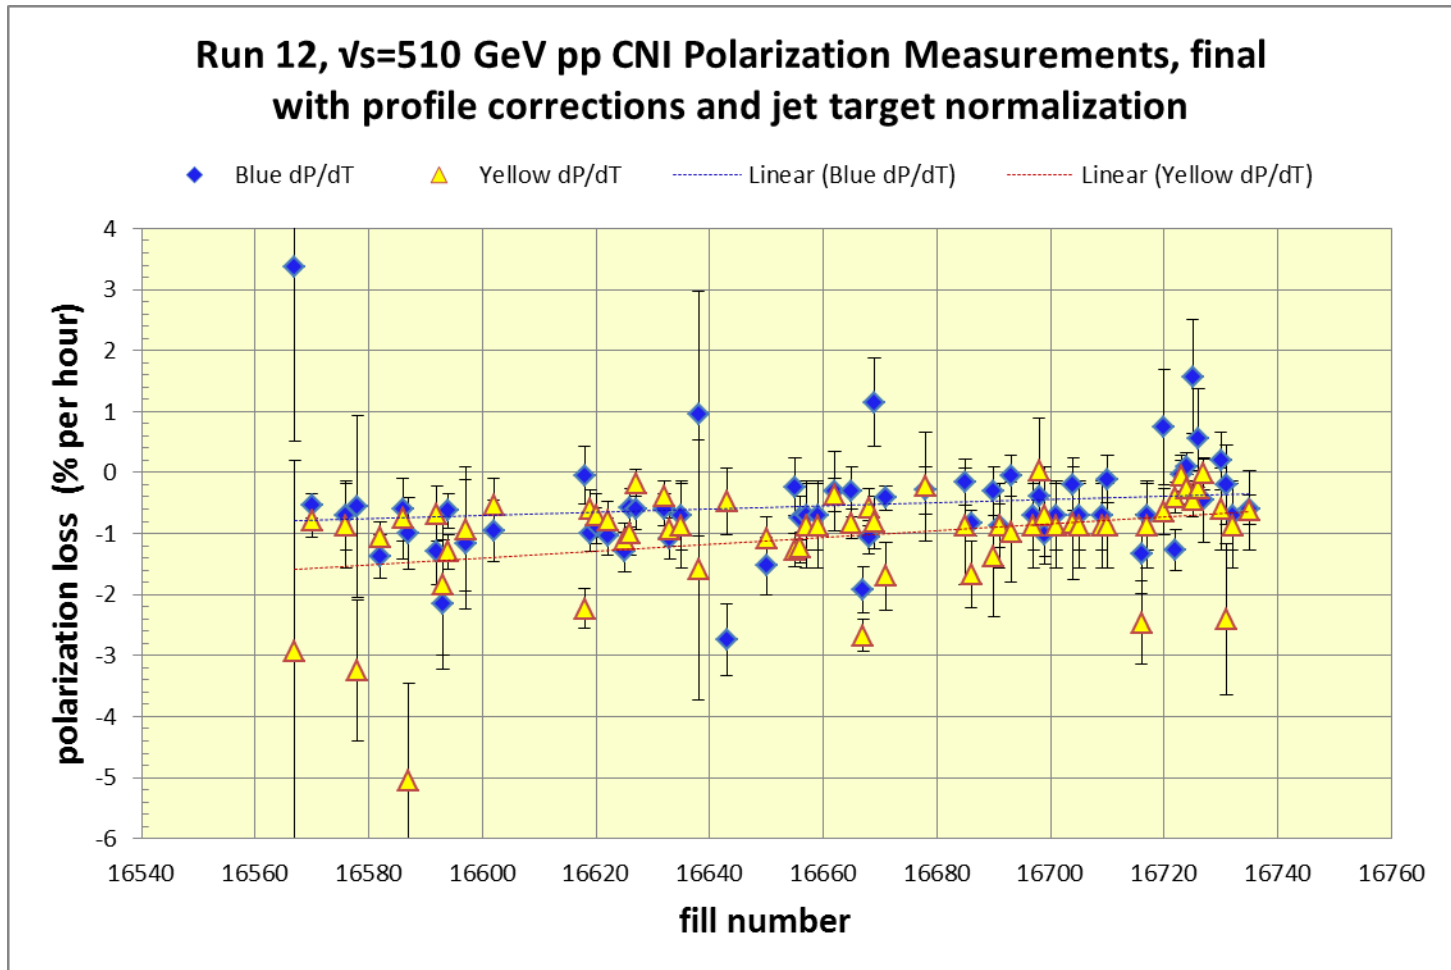

<http://www.phy.bnl.gov/cnipol/fills/>

Run12 255 x 255 Gev pp Jet target Polarization final results

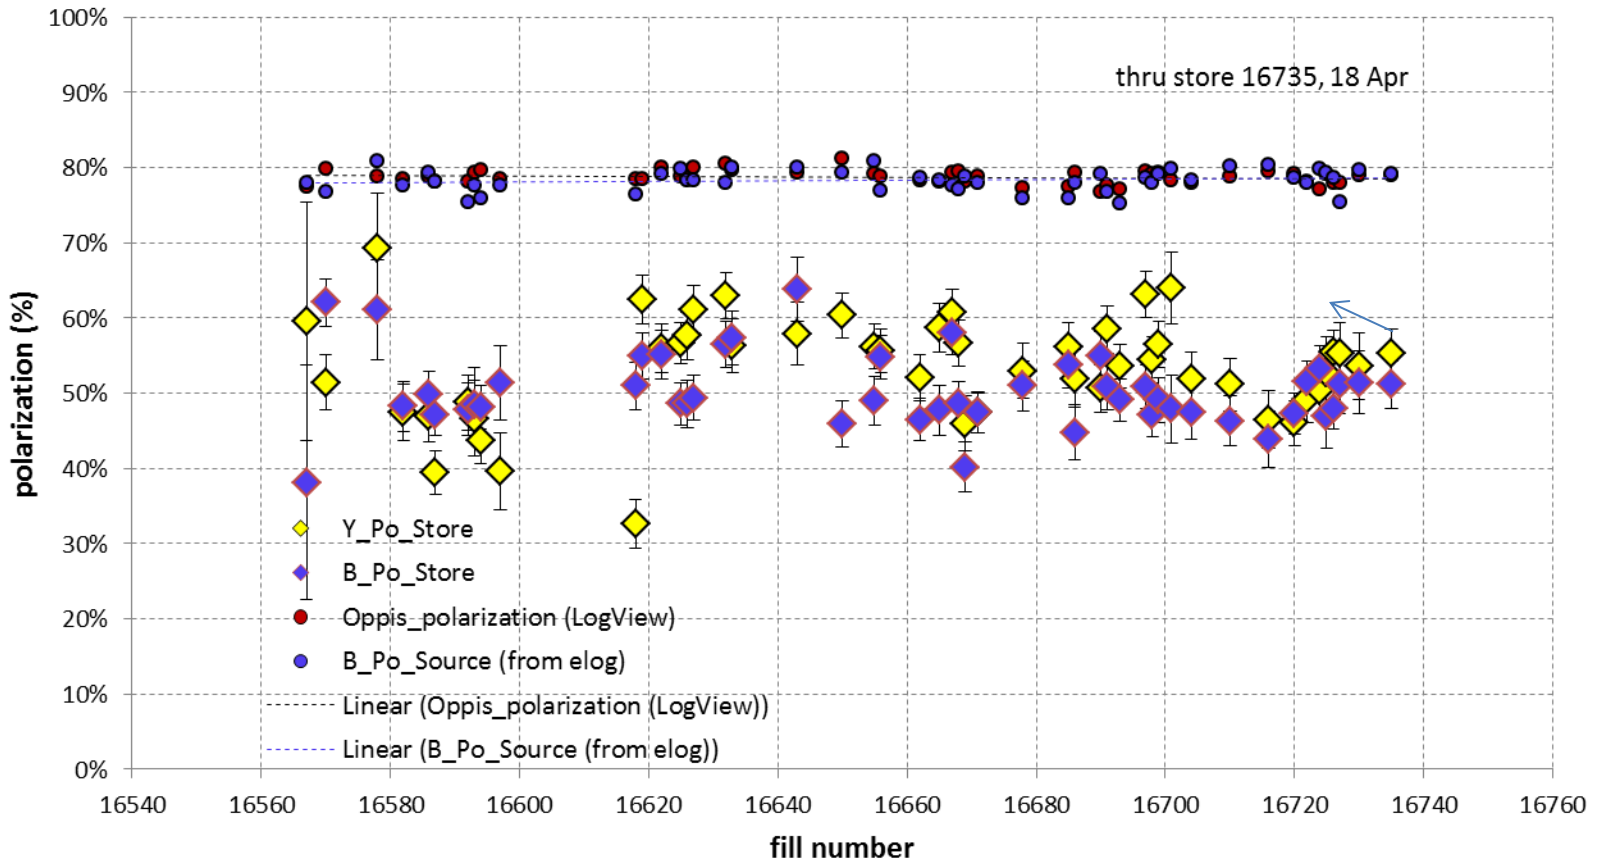


And Yellow beam at injection jet target Run 12 result = $63.0 \pm 4.4\%$

Blue jet target weighted average = $50.3\% \pm 0.5\%$

Yellow jet target weighted average = $53.4\% \pm 0.5\%$


Yellow average = $53.4 \pm 0.5\%$

Blue average = $50.3 \pm 0.5\%$

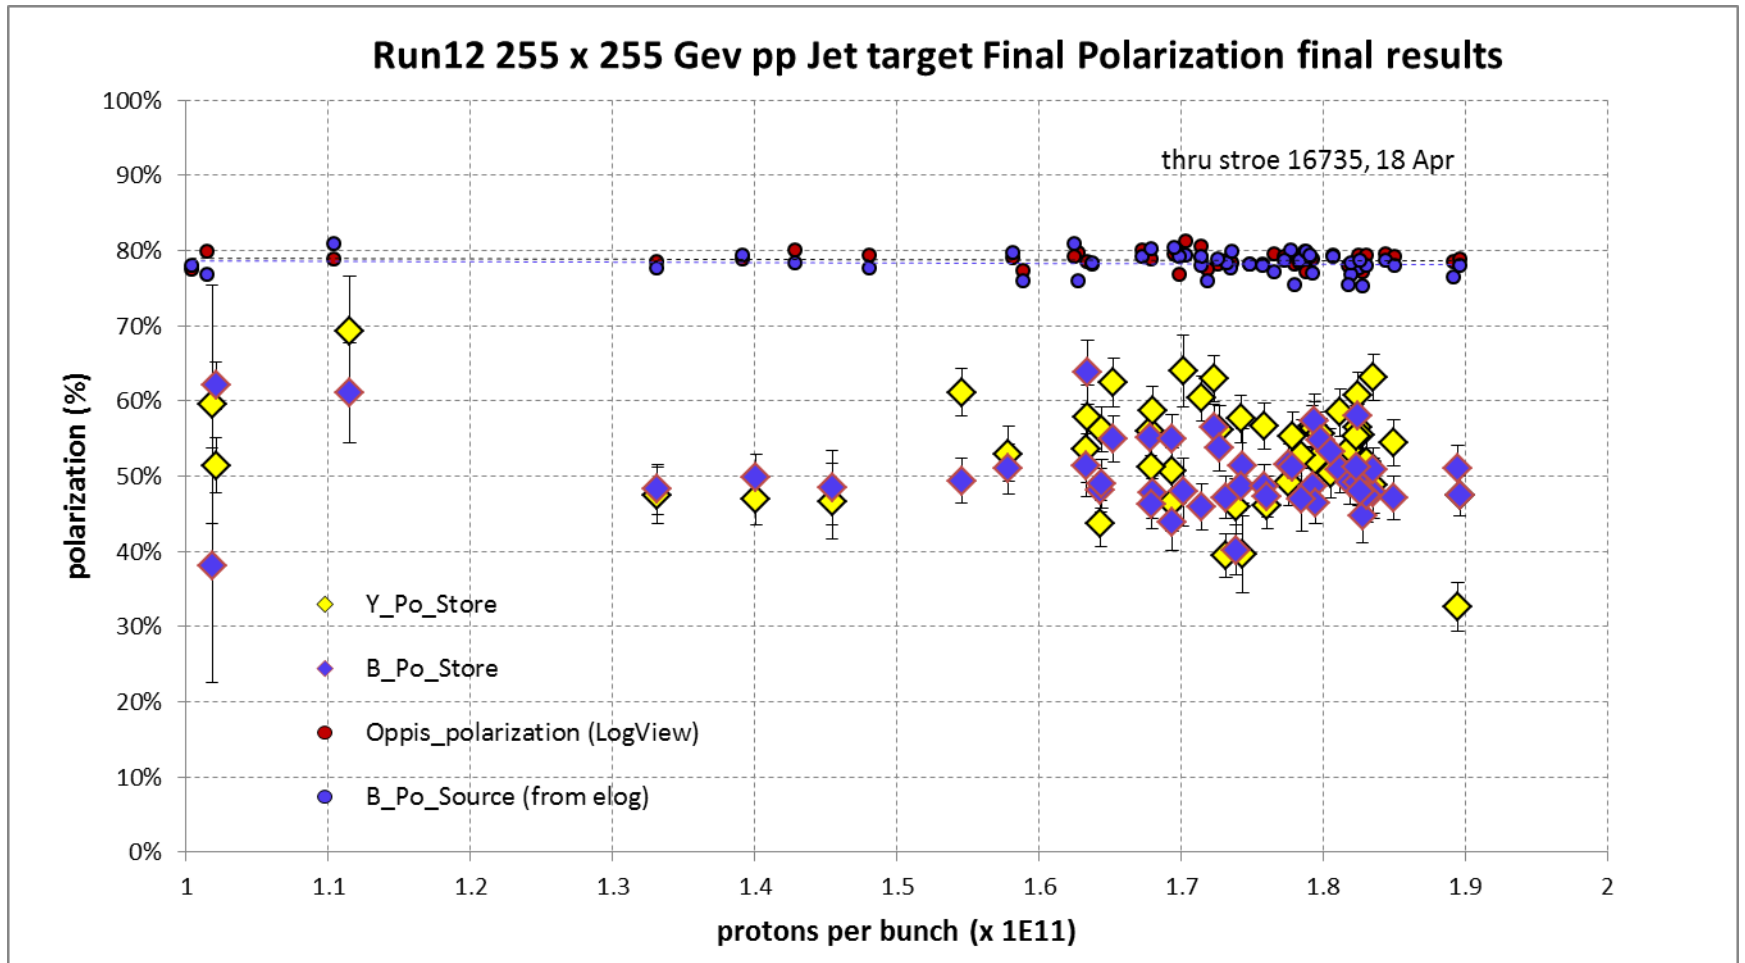


BNL Energy Use FY 2010-13

as of 18 Mar 2013

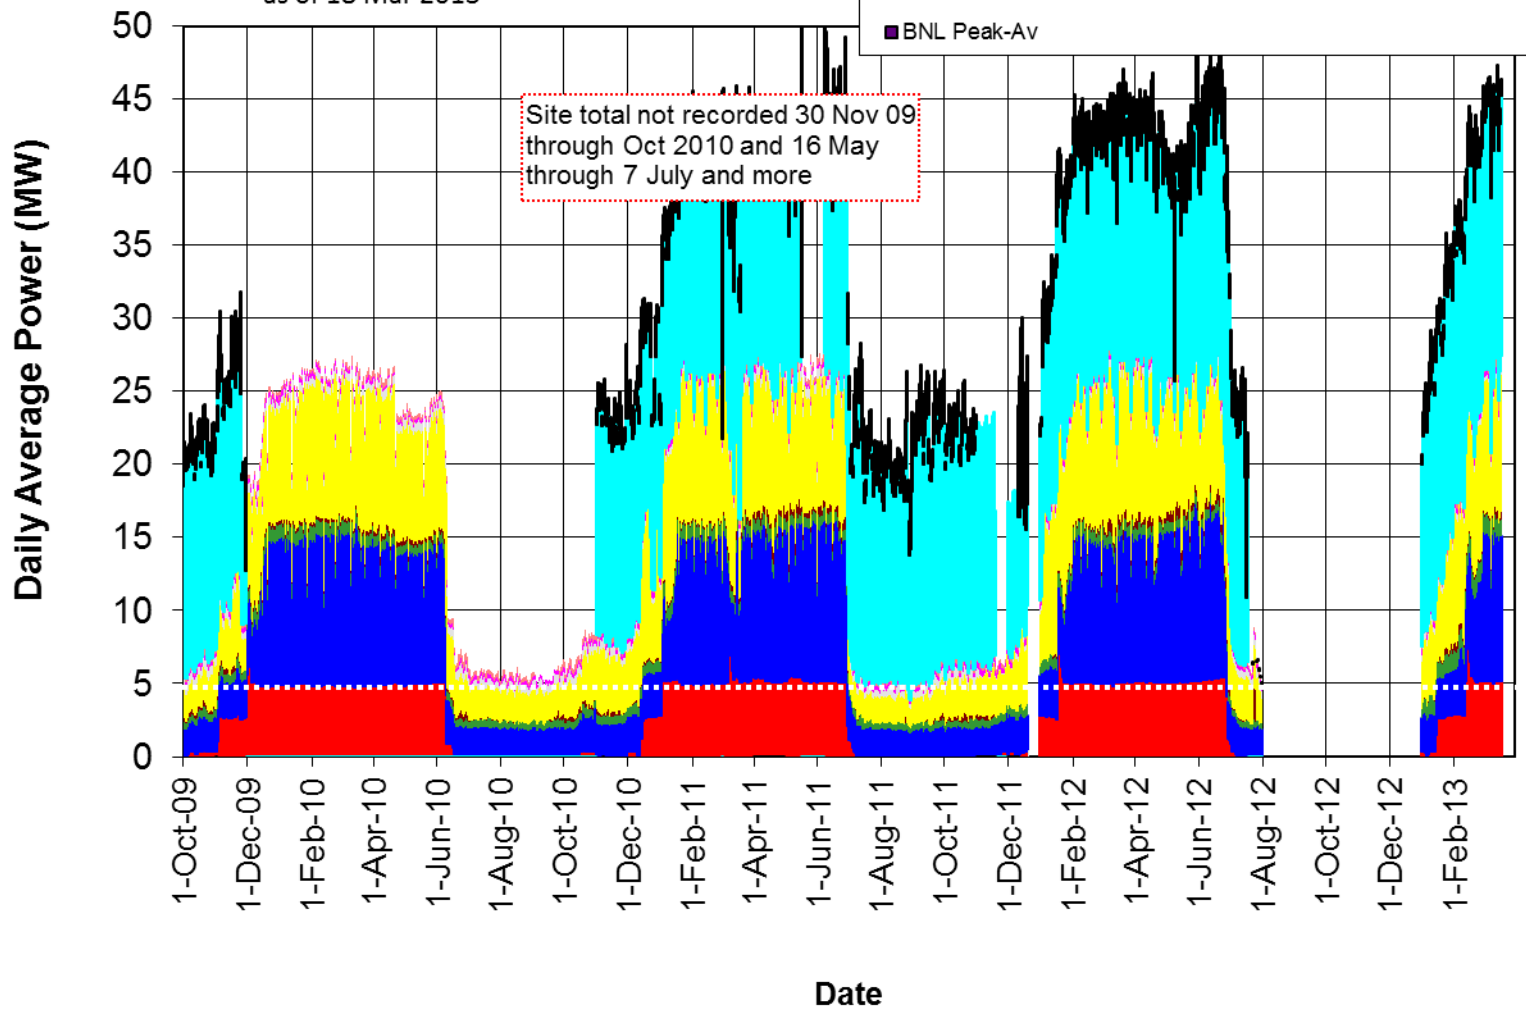


as of 18 Mar

RHIC Operations FY10-13

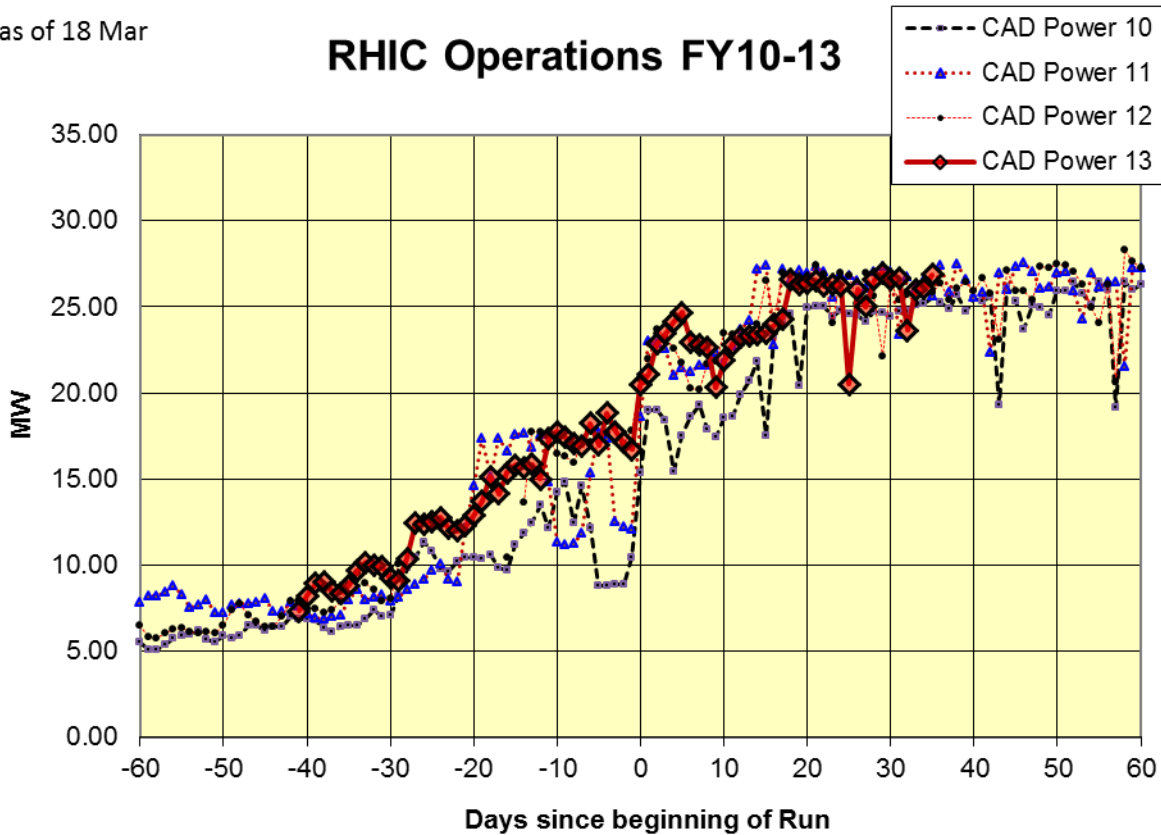


as of 18 Mar

RHIC Cryo Operations FY10-13

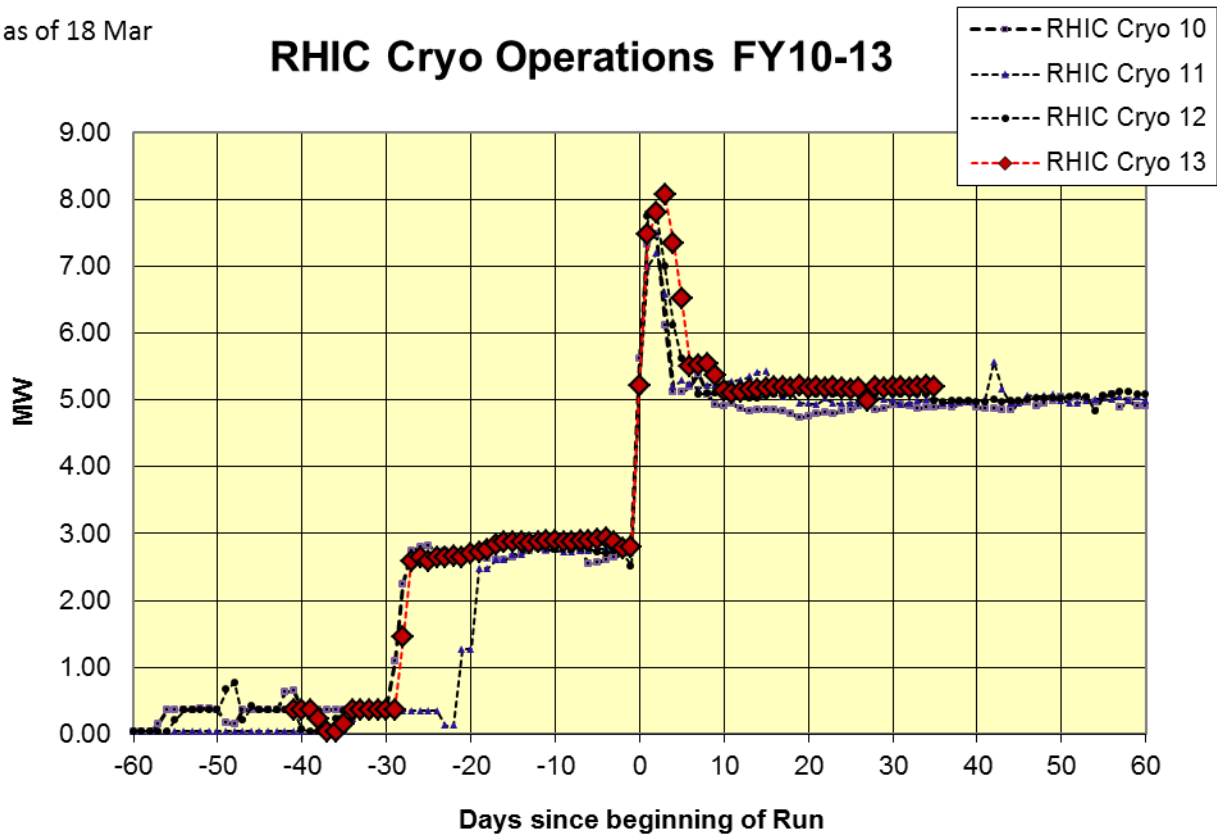

as of 18 Mar 2013

C-AD Energy Use FY 2002-13

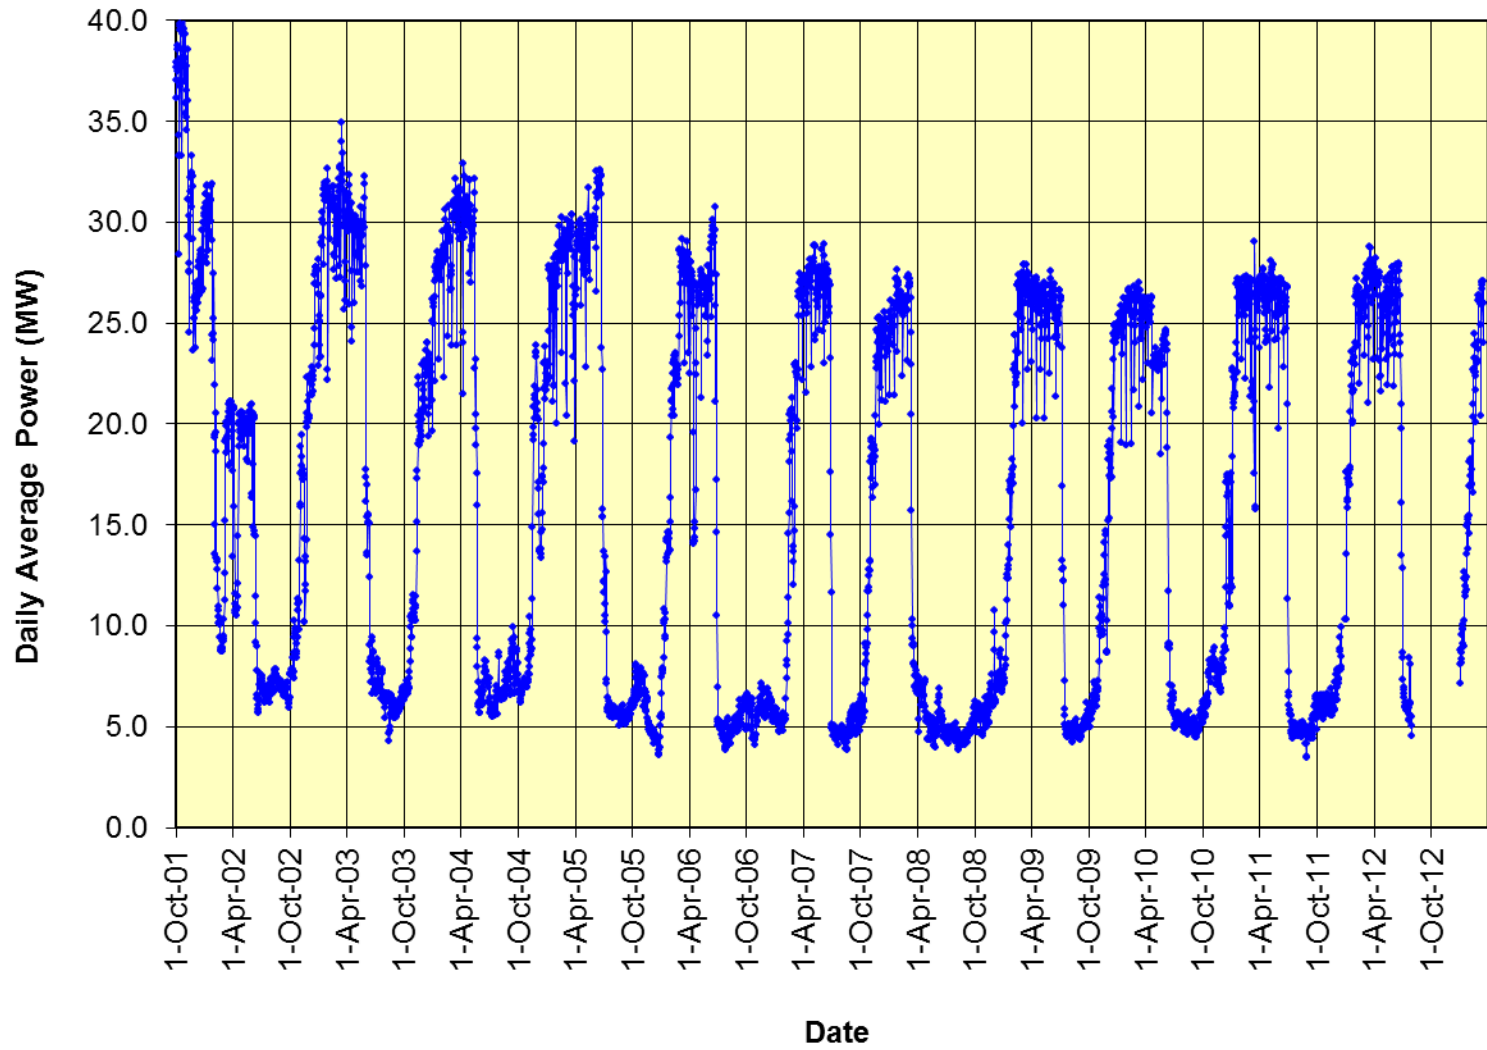


Cryogenic Blue & Yellow Rings (14 days)


[Ring Summary \(1 day\)](#) [Sector Plots \(1 day\)](#) [Sector Plots \(14 days\)](#)

File Window Markers Analysis

Blue Cryo Temperatures

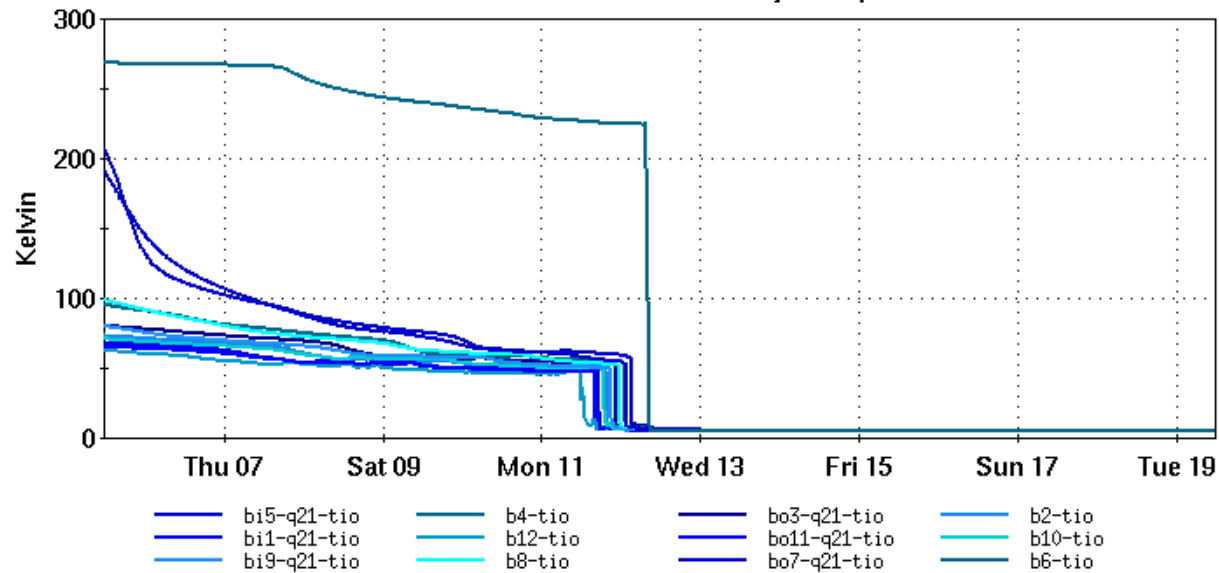

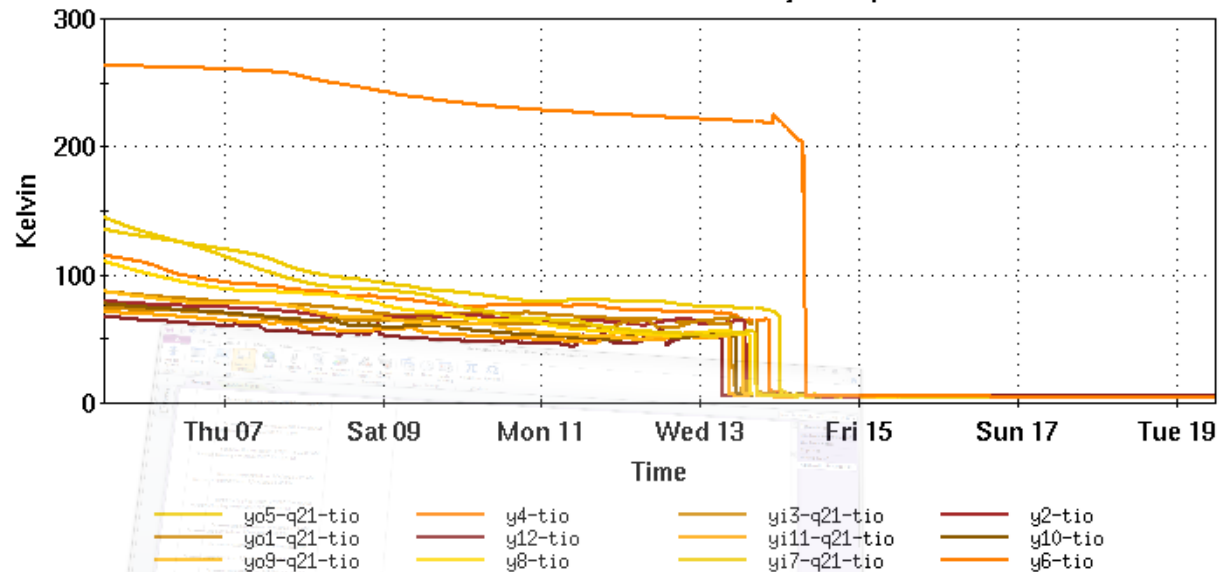


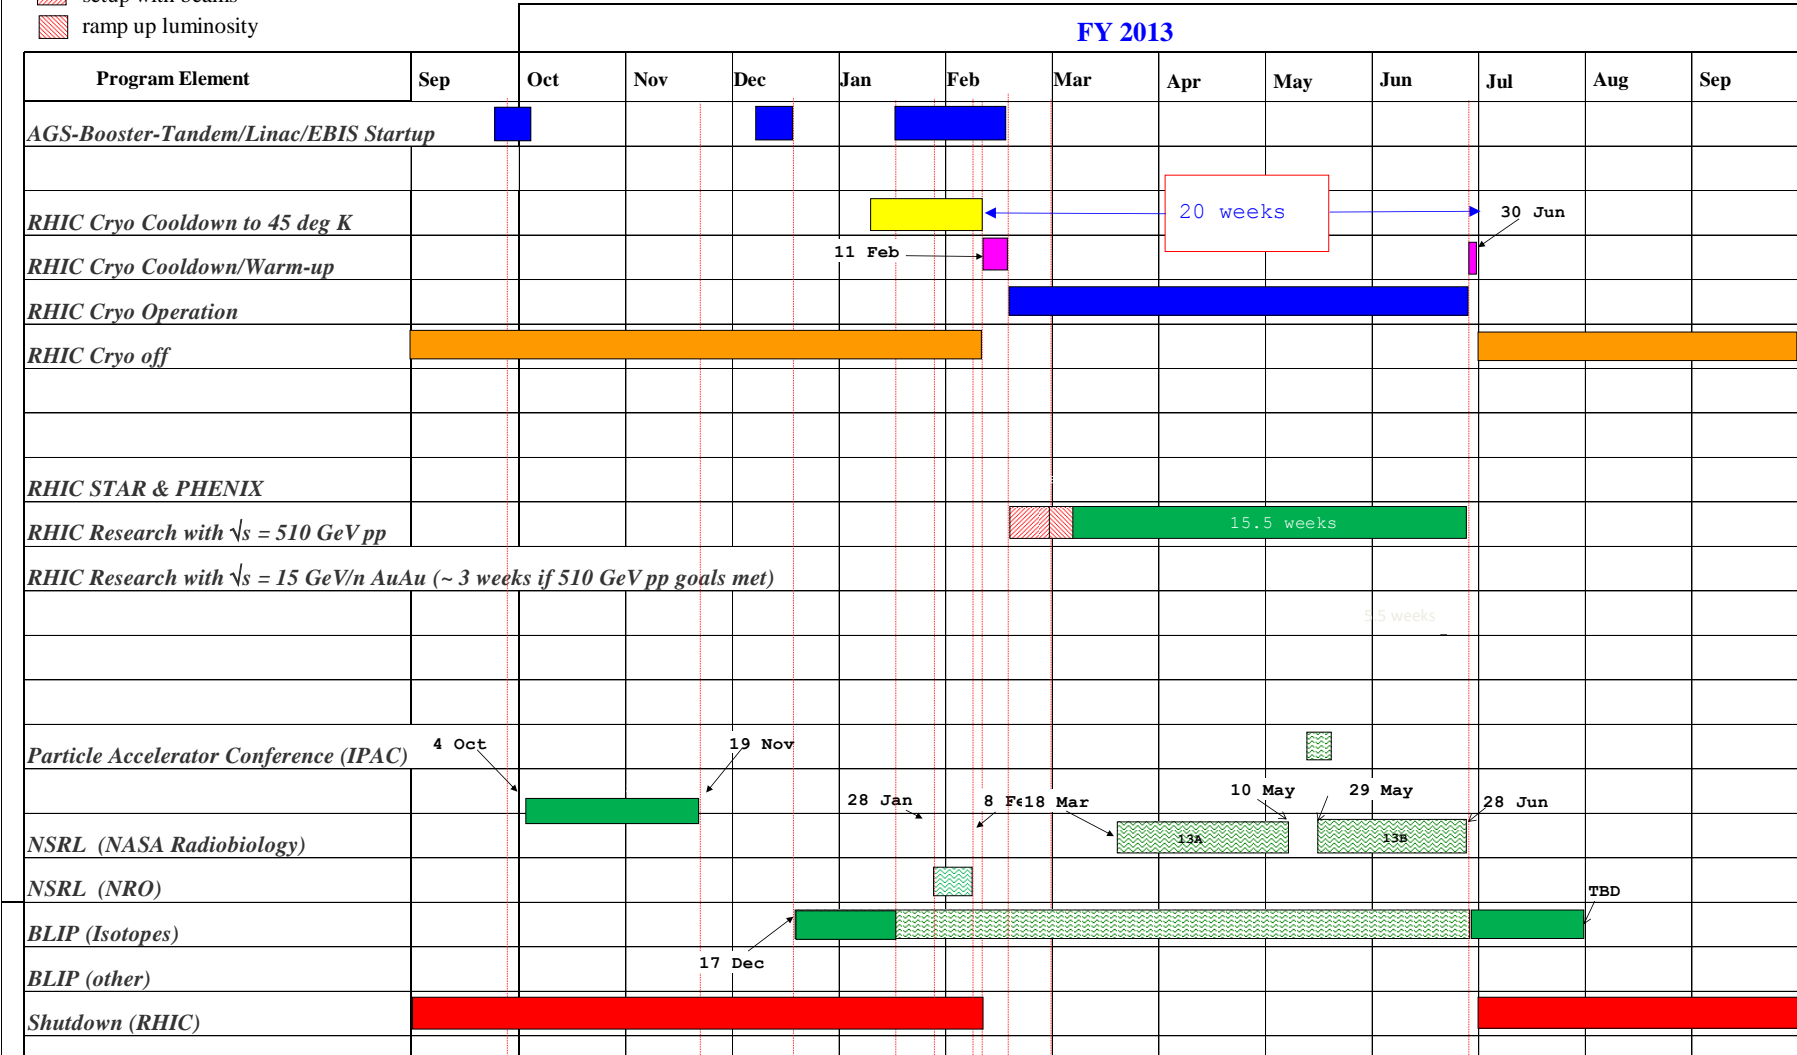
Yellow Cryo Temperatures



C-A Operations-FY13

planned, budget permitting, Preliminary

-  concurrent with RHIC
-  setup with beams
-  ramp up luminosity



For Run 13 the PAC recommends the following (*in order of priority*):

1. Running with polarized proton collisions at 500 GeV to provide an integrated luminosity of 750 pb^{-1} at an average polarization of 55%.
2. Depending on the amount of running time remaining after priority #1
 - a. If less than 3 weeks remain, a week of 200 GeV Au+Au collisions.
 - b. If at least 3 weeks of running time remain, 3 weeks of 15 GeV Au+Au collisions.
3. 8 days of 62 GeV p+p collisions.
4. At the discretion of the ALD, 4 days of low-luminosity running to accomplish the pp2pp goals.
